



South East New Territories (SENT) Landfill Extension

Quarterly Environmental Monitoring & Audit Report No.9

May 2021

ERM

2507, 25/F One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong T: 2271 3000 F: 2723 5660 www.erm.com





South East New Territories (SENT) Landfill Extension

Environmental Certification Sheet EP-308/2008/B and FEP-01/308/2008/B

Reference Document/Plan

Quarterly Environmental Monitoring & Audit Report No.9 Document/Plan to be Certified/Verified: for South East New Territories (SENT) Landfill Extension

Date of Report: 5 May 2021

Reference EM&A Manual Requirement

EM&A Manual: Section 11.4

The quarterly EM&A summary report shall be prepared by the ET, certified by the ET Leader and verified by the IEC. The quarterly EM&A summary report should contain all information listed under Section 11.4 of the approved EM&A Manual.

ET Certification

I hereby certify that the above referenced document/plan complies with the above referenced EM&A Manual requirement.

Warchitt.

Frank Wan,

Environmental Team Leader:

(ERM Hong-Kong, Limited)

5 May 2021 Date:

IEC Verification

I hereby verify that the above referenced document/plan complies with the above referenced EM&A Manual requirement.

W.K. Chiu,

Independent Environmental Checker:

(Meinhardt Infrastructure and

Environment Limited)

Date: 7 May 22

South East New Territories (SENT) Landfill Extension

Quarterly Environmental Monitoring & Audit Report No.9

Environmental Resources Management

2507, 25/F, One Harbourfront 18 Tak Fung Street Hunghom, Kowloon Hong Kong

Telephone: (852) 2271 3000 Facsimile: (852) 2723 5660 E-mail: post.hk@erm.com http://www.erm.com

Client:		Projec	t No:		
Green Valley Landfill Ltd.			0465169		
	ument presents the Quarterly EM&A Report No.9 for <i>South</i> v Territories (SENT) Landfill Extension	Appro	y 2021 ved by: MChill k Wan er	J.	
0	Quarterly EM&A Report No.9	AL	FW	FW	5 May 21
Revision	Description	Ву	Checked	Approved	Date
This report has been prepared by Environmental Resources Management the trading name of 'ERM Hong-Kong, Limited', with all reasonable skill, care and diligence within the terms of the Contract with the client, incorporating our General Terms and Conditions of Business and taking account of the resources devoted to it by agreement with the client. We disclaim any responsibility to the client and others in respect of any matters outside the		Distrib	oution Internal	Cer	OHSAS 18001:2007 tificate No. OHS 515956
scope of the above.		\boxtimes	Public		BSI
This report is confidential to the client and we accept no responsibility of whatsoever nature to third parties to whom this report, or any part thereof, is made known. Any such party relies on the report at their own risk.			Confide		ISO 9001 : 2008 rttificate No. FS 32515



CONTENTS

EXECU	TIVE SUMMARY	1
1	INTRODUCTION	1
1.1	BACKGROUND	1
1.2	PROJECT DESCRIPTION	1
1.3	SCOPE OF THE EM&A REPORT	2
1.4	PROJECT ORGANISATION	2 2 3
1.5	SUMMARY OF CONSTRUCTION WORKS	3
1.6	SUMMARY OF EM&A PROGRAMME REQUIREMENTS	5
1.7	STATUS OF STATUTORY ENVIRONMENTAL COMPLIANCE WITH THE	
	Environmental Permit	6
1.8	STATUS OF OTHER STATUTORY ENVIRONMENTAL REQUIREMENTS	7
2	EM&A RESULTS	8
2.1	AIR QUALITY MONITORING	8
2.2	Noise Monitoring	10
2.3	SURFACE WATER QUALITY MONITORING	11
2.4	LANDSCAPE AND VISUAL MONITORING	14
2.5	EM&A SITE INSPECTION	14
2.6	Waste Management Status	18
2.7	IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES	18
2.8	SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMAN	NCE
	LIMIT	18
2.9	SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS	19
3	CONCLUSION AND RECOMMENDATION	20

ANNEXES

- ANNEX A WORK PROGRAMME
- ANNEX B ENVIRONMENTAL MITIGATION IMPLEMENTATION SCHEDULE
- ANNEX C MONITORING SCHEDULE FOR THIS REPORTING PERIOD
- ANNEX D AIR QUALITY
- ANNEX D1 24-HOUR TSP MONITORING RESULTS
- ANNEX D2 EVENT AND ACTION PLAN FOR DUST MONITORING
- ANNEX D3 METEOROLOGICAL DATA
- ANNEX E NOISE
- ANNEX E1 NOISE MONITORING RESULTS
- ANNEX E2 EVENT AND ACTION PLAN FOR NOISE MONITORING
- ANNEX F SURFACE WATER QUALITY
- ANNEX F1 SURFACE WATER QUALITY MONITORING RESULTS
- ANNEX F2 EVENT AND ACTION PLAN FOR SURFACE WATER QUALITY MONITORING
- ANNEX F3 INVESTIGATION REPORTS OF ENVIRONMENTAL QUALITY LIMIT EXCEEDANCE
- ANNEX G CUMULATIVE STATISTICS ON EXCEEDANCES, ENVIRONMENTAL COMPLAINTS, NOTIFICATION OF SUMMONS AND STATUS OF PROSECUTIONS

EXECUTIVE SUMMARY

The SENT Landfill Extension (SENTX) forms an integral part in the Strategic Plan in maintaining the continuity of landfill capacity in the Hong Kong for the cost-effective and environmentally satisfactory disposal of waste. ERM-Hong Kong, Limited (ERM) is commissioned to undertake the role of Environmental Team (ET) for the construction, operation/restoration and aftercare of SENTX Project ("the Project") in accordance with the requirements specified in the Environmental Permit (EP), updated Environmental Monitoring and Audit (EM&A) Manual, the approved Environmental Impact Assessment (EIA) Report of the Project taking account of the latest design and other relevant statutory requirements. The construction (not including works related to site clearance and preparation) of the Project commenced on 2 January 2019.

This Quarterly EM&A report presents the EM&A works carried out during the period from 1 January to 31 March 2021 for the Project in accordance with the updated EM&A Manual.

Exceedance of Action and Limit Levels for Air Quality

No exceedance of Action and Limit Levels for construction air quality monitoring was recorded in the reporting period.

Exceedance of Action and Limit Levels for Noise

No exceedance of Action and Limit Levels for construction noise monitoring was recorded in the reporting period.

Exceedance of Action and Limit Levels for Surface Water Quality

One exceedance of the Limit Level for suspended solids (SS) was recorded for surface water quality impact monitoring in the reporting period. The SS exceedance at DP4 (Future, temporary) on 25 February 2021 was found deemed to Project-related activities.

Environmental Complaints, Summons and Prosecutions

There were no complaints, notification of summons or prosecution recorded in the reporting period.

Reporting Change

There was no reporting change in the reporting period.

1 INTRODUCTION

1.1 BACKGROUND

The SENT Landfill Extension (SENTX) forms an integral part in the Strategic Plan in maintaining the continuity of landfill capacity in the Hong Kong for the cost-effective and environmentally satisfactory disposal of waste. The *Environmental Impact Assessment (EIA) Report* and the associated *Environmental Monitoring and Audit (EM&A) Manual* for the construction, operation, restoration and aftercare of the SENTX (hereafter referred to as "the Project") have been approved under the *Environmental Impact Assessment Ordinance (EIAO)* in May 2008 (Register No.: AEIAR-117/2008) (hereafter referred to as the approved EIA Report) and an Environmental Permit (EP-308/2008) (EP) was granted by the Director of Environmental Protection (DEP) on 5 August 2008.

Since then, applications for Variation of an Environmental Permit (No. VEP-531/2017) were submitted to EPD and the Variation of Environmental Permits (EP-308/2008/A and EP-308/2008/B) were granted on 6 January 2012 and 20 January 2017, respectively, as the Hong Kong SAR Government has decided to reduce the scale of the design scheme of SENTX assessed in the approved EIA Report and SENTX will only receive construction waste. In May 2018, a Further Environmental Permit (FEP) (FEP-01/308/2008/B) was granted to the SENTX's contractor, Green Valley Landfill, Limited (GVL).


ERM-Hong Kong, Limited (ERM) and Meinhardt Infrastructure and Environment Limited (Meinhardt) are commissioned to undertake the roles of Environmental Team (ET) and the Independent Environmental Checker (IEC), respectively, to undertake the EM&A activities for the Project in accordance with the requirements specified in the EP, updated EM&A Manual (1), approved EIA Report (2) taking account of the latest design and other relevant statutory requirements.

1.2 PROJECT DESCRIPTION

The SENTX is a piggyback landfill, occupying the southern part of the existing SENT Landfill (including its infrastructure area) and 13 ha of Tseung Kwan O (TKO) Area 137. A layout plan of the SENTX is shown in *Figure 1.1*. Under the latest design, the SENTX has a net void capacity of about 6.5 Mm³ and provides an additional lifespan of about 6 years, commencing operation upon exhaustion of the SENT Landfill. The SENTX will receive construction waste only.

⁽¹⁾ ERM (2018). South East New Territories (SENT) Landfill Extension: Environmental Monitoring & Audit Manual

⁽²⁾ ERM (2007). South East New Territories (SENT) Landfill Extension – Feasibility Study: Environmental Impact Assessment Report

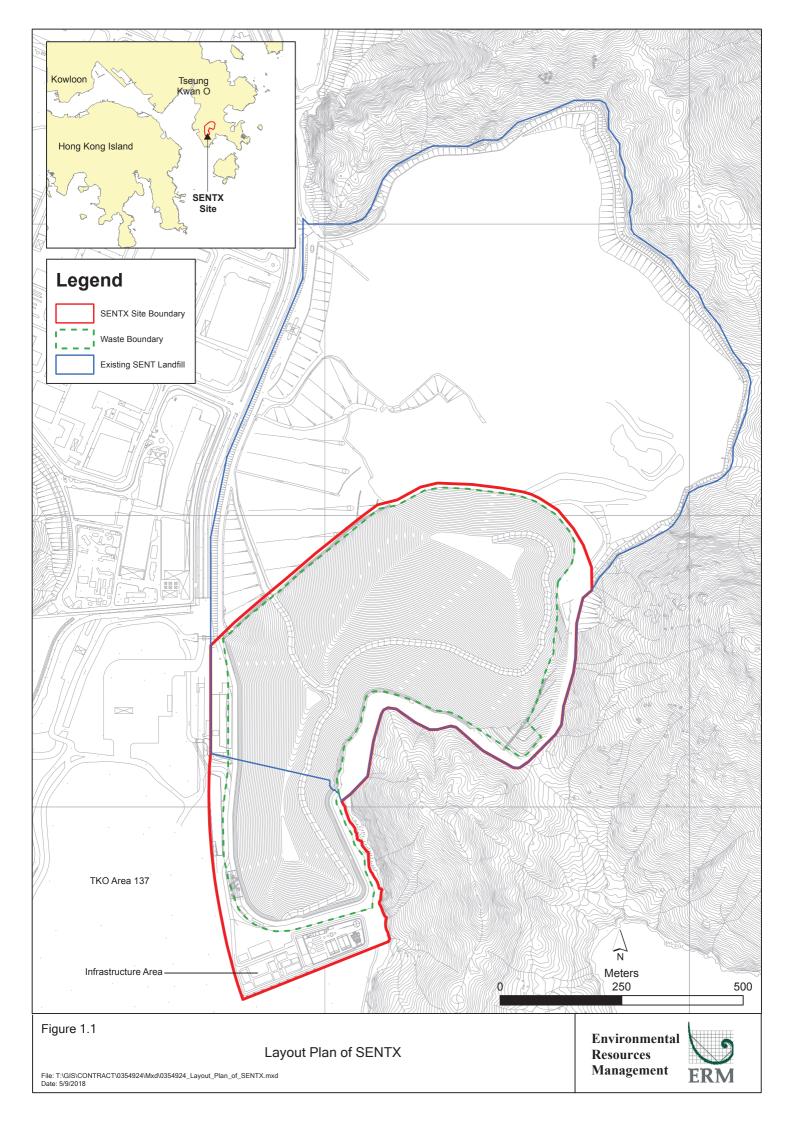

The key implementation milestones of the Project are indicatively summarised in *Table 1.1*. The construction works of the Project commenced on 2 January 2019.

 Table 1.1
 Estimated Key Dates of Implementation Programme

Key Stage of the Project	Indicative Date
Start construction	2 January 2019
Commissioning of new infrastructure facilities	2020
Demolition of existing infrastructure facilities	2021
Start waste intake at SENTX	2021 or upon exhaustion of SENT Landfill
Estimated exhaustion date of SENTX	2027
End of aftercare for SENTX	2057

The major construction works of the SENTX includes:

- Site formation at the TKO Area 137 and the existing infrastructure area at SENT Landfill;
- Construction of surface and groundwater drainage systems;
- Construction of the leachate containment and collection systems;
- Construction of new leachate and landfill gas treatment facilities, site offices, maintenance yards at the new infrastructure area;
- Construction of new pipelines to transfer the leachate and landfill gas
 collected from the existing SENT Landfill to the treatment facilities at
 the new infrastructure area;
- Construction of the site access and new waste reception facilities; and
- Demolition of the facilities at the existing SENT Landfill infrastructure area.


1.3 Scope of the EM&A Report

This is the Quarterly EM&A Report for the Project which summarises the key findings of the EM&A programme during the reporting period from 1 January to 31 March 2021 for the construction works.

1.4 PROJECT ORGANISATION

The organisation structure of the Project is presented in *Figure 1.2*.

Figure 1.2 Organisation Chart

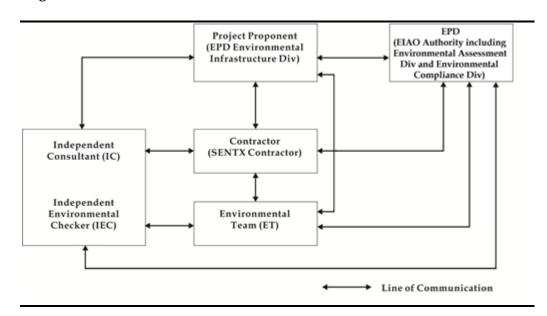

Contact details of the key personnel are summarized in *Table 1.2* below.

Table 1.2 Contact Information of Key Personnel

Party	Position	Name	Telephone
Contractor (Green Valley Landfill	Project Manager Complaint Hotline	Gary Barnicott	2706 8827
Limited)	1		
Environmental Team (ET) (ERM-Hong Kong, Limited)	ET Leader	Frank Wan	2271 3152
Independent Environmental Checker (IEC) (Meinhardt Infrastructure and Environment Limited)	IEC	W.K. Chiu	2858 0738

1.5 SUMMARY OF CONSTRUCTION WORKS

The programme of the construction is shown in *Annex A*. As informed by the Contractor, the major works carried out in this reporting period include:

January 2021

- Installation of cables and cable containment at Leachate Treatment Plant (LTP) area;
- Electro-mechanical installation (including pipe) at LTP area;
- Testing and commissioning at LTP;
- Building services works and fitting-out works for infrastructure buildings (EPD building, GVL building and laboratory building);

- Steel members and cladding installation for superstructure of maintenance building;
- Equipment installation for fire services tank room;
- Water main pipe installation for infrastructure buildings;
- Road pavement for the emergency vehicular access (EVA);
- Filling works at the West of Cell 3X;
- Maintenance and improvement of temporary surface water drainage;
- Construction of Cell 3X formation;
- Liner installation at Cell 3X;
- Road pavement for EVA along Western Bund from main entrance;
- Installation of steel members for vehicle washing facilities;
- Underground utilities and pipes installation at waste reception area; and
- Sewerage system works at waste reception area.

February 2021

- Testing and commissioning at LTP;
- Building services works and fitting-out works for infrastructure buildings (EPD building, GVL building and laboratory building);
- Cladding installation for maintenance building;
- Equipment installation for fire services tank room;
- Road pavement for carpark and EVA;
- Maintenance and improvement of temporary surface water drainage;
- Liner installation at Cell 3X;
- Installation of steel members for vehicle washing facilities;
- Underground utilities and pipes installation at waste reception area; and
- Sewerage system works at waste reception area.

<u>March 2021</u>

Functional testing at LTP;

- Building services works and fitting-out works for infrastructure buildings (EPD building, GVL building and laboratory building);
- Cladding installation for superstructure of maintenance building;
- Road pavement for EVA;
- Permanent equipment installation for sump houses 1, 2 and 3;
- Maintenance and improvement of temporary surface water drainage;
- Underground utilities and pipes installation at waste reception area; and
- Sewerage system works at waste reception area.

The implementation schedule of the mitigation measures recommended in the Updated EM&A Manual is presented in *Annex B*.

1.6 SUMMARY OF EM&A PROGRAMME REQUIREMENTS

The status for all environmental aspects are presented in *Table 1.3*. The EM&A requirements remained unchanged during the reporting period.

Table 1.3 Summary of Status for the Environmental Aspects under the Updated EM&A Manual

Parameters	Status
Air Quality	
Baseline Monitoring	The results of baseline air quality monitoring were reported in <i>Baseline Monitoring Report</i> and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going
Noise	
Baseline Monitoring	The results of baseline noise monitoring were reported in <i>Baseline Monitoring Report</i> and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going
Surface Water Quality	
Baseline Monitoring	The results of baseline surface water quality monitoring were reported in <i>Baseline Monitoring Report</i> and submitted to EPD under EP Condition 3.3
Impact Monitoring	On-going
Waste Management	
Waste Monitoring	On-going
Landscape and Visual	
Baseline Monitoring	The results of baseline landscape and visual monitoring were reported in <i>Baseline Monitoring Report</i> and submitted to EPD under EP Condition 3.3
Construction Phase Audit	On-going
Site Environmental Audit	
Regular Site Inspection	On-going
Complaint Hotline and Email Channel	On-going
Environmental Log Book	On-going
Groundwater Quality	
Pre-operation Baseline Monitoring	Commenced on 24 March 2020 and completed on 9 March 2021

Parameters	Status		
Landfill Gas			
Pre-operation Baseline	Commenced on 24 March 2020 and completed on 26 March		
Monitoring	2021		
Ambient VOCs, ammonia and	H_2S		
Pre-operation Baseline	Commenced on 27 May 2020 and completed on 17 February		
Monitoring	2021		

Taking into account the construction works, impact monitoring of air quality, noise, surface water quality and waste management were carried out in the reporting period. The impact monitoring schedule of air quality, noise and surface water quality monitoring are provided in *Annex C*. Groundwater and landfill gas pre-operation baseline monitoring and ambient VOCs, ammonia and H₂S pre-operation baseline monitoring were commenced on 24 March 2020 and 27 May 2020 respectively.

The EM&A programme also involved environmental site inspections and related auditing conducted by the ET for checking the implementation of the required environmental mitigation measures recommended in the approved EIA Report and relevant EP submissions. To promote the environmental awareness and enhance the environmental performance of the contractors, environmental trainings and regular environmental management meetings were conducted during the reporting period, which are summarised as below:

- Three environmental management meetings were held with the Contractor, ER, ET, IEC and EPD on 21 January, 18 February and 18 March 2021; and
- Environmental toolbox trainings on the following topics were provided by the Contractor to the workers:
 - Illegal Dumping on 11 January 2021;
 - Trip Ticket System on 22 January 2021;
 - Cut Down Construction Dust on 8 February 2021;
 - Wastewater Management on 22 February 2021;
 - Clean Recycling on 12 March 2021; and
 - Mosquito Nuisance on 16 March 2021.

1.7 STATUS OF STATUTORY ENVIRONMENTAL COMPLIANCE WITH THE ENVIRONMENTAL PERMIT

The status of statutory environmental compliance with the EP conditions under the EIAO, submission status under the EP and implementation status of the recommended mitigation measures are presented in *Table 1.4*.

Table 1.4 Status of Submissions required under the EP and Implementation Status of the recommended Mitigation Measures

EP Condition	Submission / Implementation Status	Status
2.3	Management Organisation of Main Construction Companies	Submitted and accepted by EPD.
2.4	Setting up of Community Liaison Group	Community Liaison Group was set up.
2.5	Submission of Detailed Landfill Gas Hazard Assessment Report	Submitted, and accepted by EPD on 10 January 2019.
2.6	Submission of Restoration and Ecological Enhancement Plan	Submitted to EPD on 28 June 2019.
2.7	Setting up of Trial Nursery	Trial Nursery works was commenced on 28 August 2019.
2.8	Advance Screen Planting	Advance Screen Planting works were completed on 28 June 2019.
2.9	Provision of Multi-layer Composite Liner System	Under implementation.

1.8 STATUS OF OTHER STATUTORY ENVIRONMENTAL REQUIREMENTS

The environmental licenses and permits (including EP, *Water Pollution Control Ordinance* (WPCO) discharge license, registration as a chemical waste producer, and construction noise permit) that are valid in the reporting period are presented in *Table 1.5*. No non-compliance with environmental statutory requirements was identified.

Table 1.5 Status of Statutory Environmental Requirements

Description	Ref No.	Status
Environmental Permit	EP-308/2008	Granted on 5 August 2008
Variation of Environmental Permit	EP-308/2008/A	Granted on 6 January 2012
	EP-308/2008/B	Granted on 20 January 2017
Further Environmental Permit	FEP-01/308/2008/B	Granted on 16 May 2018
Water Discharge License under WPCO (Permit Holder: Chun Wo)	Licence No.: WT00033525- 2019	Validity from 27 March 2019 to 31 March 2024
Billing Account for Disposal of Construction Waste	Chit Account Number: 5001692	Approved on 28 December 2005
Registration as a Chemical Waste Producer (Permit Holder: Chun Wo)	5213-839-C3507-10	Issued on 23 August 2018
Registration as a Chemical Waste Producer (Permit Holder: REC)	5518-839-R2289-06	Issued on 24 October 2019
Construction Noise Permit (Permit Holder: GVL)	GW-RE0542-20	Validity from 1 September 2020 to 28 February 2021
	GW-RE0154-21	Validity from 1 March 2021 to 30 September 2021
Construction Noise Permit (Permit Holder: Chun Wo)	GW-RE1047-20	Validity from 9 December 2020 to 7 June 2021
Construction Noise Permit (Permit Holder: REC)	GW-RE0889-20	Validity from 1 November 2020 to 31 March 2021

2 EM&A RESULTS

The EM&A programme for the Project required environmental monitoring for air quality, noise and surface water quality as well as environmental site inspections for air quality, noise, surface water quality, waste management, and landscape and visual impacts. The EM&A requirements and related findings for each component are summarised in the following sections.

2.1 AIR QUALITY MONITORING

2.1.1 Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact air quality monitoring (dust, in term of Total Suspended Particulates (TSP)) was carried out at the two designated monitoring locations (i.e. DM1 and DM2) at a 6-day interval. It is proposed and agreed by IEC and EPD that the two existing TSP monitoring stations (i.e. TKO-A1 and TKO-A2a) currently operating by the Civil Engineering and Development Department (CEDD) can be used to monitor the 24-hour TSP impact associated with the SENTX construction. The dust monitoring results were obtained from CEDD on regular basis.


The Action and Limit Levels of the air quality monitoring is provided in *Table* 2.1 below.

Table 2.1 Action and Limit Levels for 24-hour TSP

Monitoring Station	Action Level	Limit Level
DM-1 - Site Egress of TKO Area 137 Fill Bank	204 μg m- ³	260 μg m- ³
DM-2A -Combined Reception and Exit Office (CREO) of TKO Area 137 Fill Bank	193 μg m- ³	260 μg m- ³

High volume air samplers (HVSs) in compliance with the specifications listed under Section 3.2.2 of the updated EM&A Manual were used to measure 24-hour TSP levels at the CEDD dust monitoring stations. The HVSs were calibrated upon installation and thereafter at bi-monthly intervals to check the validity and accuracy of the results.

The equipment used in the impact air quality monitoring programme and monitoring locations are summarised in *Table 2.2* and illustrated in *Figure 2.1* respectively.

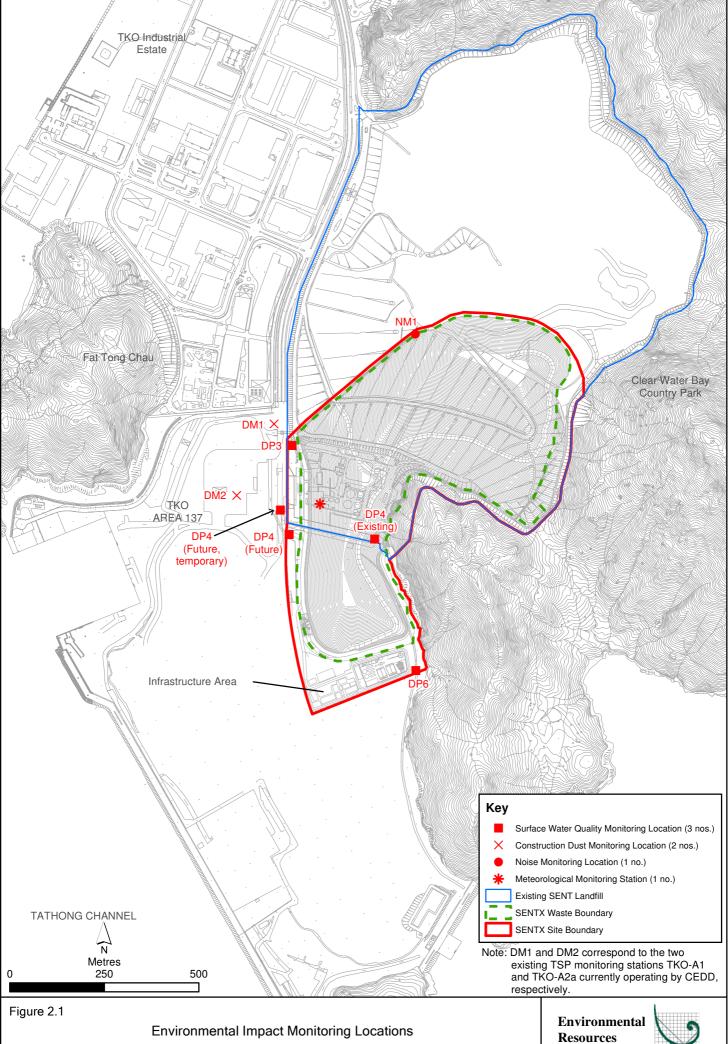

 $File: T. \\ IGIS/CONTRACT/0465169 \\ Imxd/0465169 \\ Environmental_Impact_Monitoring_Locations. \\ mxd/Date: 28/5/2019$

Management



Table 2.2 Dust Monitoring Details

Monitoring Station	Location	Parameter	Frequency and Duration	Monitoring Dates	Equipment
DM1	Site Egress of TKO Area 137 Fill Bank	24-hour TSP	Once every 6 days during the	5, 11, 17, 23, 29 January 2021	HVS Greasby 105 (S/N: 9795 (ET/EA/003/18))
DM2	Combined Reception and Exit Office		construction phase of the Project	4, 10, 16, 22, 28 February 2021	HVS Andersen G1051 (S/N: 1176 (ET/EA/003/05))
	(CREO) of TKO Area 137 Fill Bank			6, 12, 18, 24, 30 March 2021	

2.1.2 Monitoring Schedule for the Reporting Period

The schedule for air quality monitoring during the reporting period is provided in *Annex C*.

2.1.3 Results and Observations

The 24-hour TSP monitoring results are summarised in *Table 2.3*. The detailed monitoring results and the graphical presentation of the 24-hour TSP monitoring results at each monitoring location are provided in *Annex D1*.

Table 2.3 Summary of 24-hour TSP Monitoring Results in the Reporting Period

Month	Monitoring	24-hr TSP Concentration (μg m ⁻³)		Action Level	Limit Level (μg/m³)
Station		Average	Range	(μg/m³)	
January 2021	DM-1	111	105 - 117	204	260
	DM-2	104	95 - 115	193	260
February 2021	DM-1	104	92 - 113	204	260
	DM-2	98	89 - 103	193	260
March 2021	DM-1	104	90 - 115	204	260
	DM-2	100	93 - 109	193	260

The major dust sources in the reporting period included fugitive dust emission from exposed area in SENTX, as well as nearby operations of the existing SENT landfill and the TKO Area 137 Fill Bank.

All the 24-hour TSP results measured at the two monitoring stations were below the Action and Limit Levels in the reporting period. No additional measure is thus required in accordance with the Event and Action Plan presented in *Annex D2*.

2.1.4 Meteorological Data

Meteorological data obtained from the on-site meteorological monitoring station at the existing SENT landfill (see *Figure 2.1*) were used for the dust monitoring and are shown in *Annex D3*. The meteorological station will be moved to a new location at SENTX infrastructure area as per the updated EM&A Manual after the construction of the new infrastructure area is

completed. For the purpose of this EM&A programme, it is considered that meteorological data obtained at the existing SENT landfill meteorological monitoring station are representative of the Project area and could be used for the interpretation of the construction phase dust monitoring results.

2.2 Noise Monitoring

2.2.1 Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact noise monitoring was conducted weekly at the monitoring location (i.e. NM1) to obtain one set of 30 minutes measurement between 07:00 and 19:00 hours on normal weekdays.

The Action and Limit Levels for construction noise of the Project are provided in *Table 2.4* below.

Table 2.4 Action and Limit Levels for Construction Noise

Time Period	Action Level (a)	Limit Level (b)
07:00 – 19:00 hrs on normal weekdays	When one documented complaint is received from any one of the noise sensitive receivers (NSRs)	75 dB(A) at NSRs
	or	
	75 dB(A) recorded at the monitoring station	

Notes:

- (a) 75dB(A) along and at about 100m from the SENTX site boundary was set as the Action Level.
- (b) Limits specified in the GW-TM and IND-TM for construction and operational noise, respectively.

Noise monitoring was performed by ALS Technichem (HK) Pty Ltd (HOKLAS Registration No. 066) using a sound level meter placed at the designated monitoring station NM1 (see *Figure 2.1*) in accordance with the requirements stipulated in the updated EM&A Manual. Acoustic calibrator was deployed to check the sound level meter at a known sound pressure level. Details of the deployed equipment are provided in *Table 2.5*.

Table 2.5 Noise Monitoring Details

Monitoring Station (1)	Location	Parameter	Frequency and Duration	Monitoring Dates	Equipment
NM1	SENTX Site Boundary (North)	L _{eq (30 min)} measurement between 07:00	Once per week for 30 mins during the	7, 14, 20, 28 January 2021	Sound Level Meter: B&K 2238 (S/N:
		and 19:00 hours on normal	construction period of the Project	4, 9, 17, 25 February 2021	2285722) (S/N: 2285762)
		weekdays (Monday to Saturday)		4, 11, 18, 25 March 2021	Acoustic Calibrator: Rion NC-74 (S/N: 34657230) (S/N: 34657231)

2.2.2 Monitoring Schedule for the Reporting Period

The schedule for noise monitoring during the reporting period is provided in *Annex C*.

2.2.3 Results and Observations

A total of 12 impact noise monitoring events were scheduled during the reporting period. However, noise monitoring on 4 March 2021 was cancelled due to adverse weather. The noise monitoring results are summarised in *Table 2.6* and graphically presented in *Annex E1*.

Table 2.6 Summary of Construction Noise Monitoring Results in the Reporting Period

Month	Monitoring	Measured Noise Level Leq (30 min), dB(A)				
	Station	Average	Range	Action and Limit Level		
January 2021	NM1	51.1	49.8 - 52.6	75		
February 2021	NM1	51.0	49.8 - 54.1	75		
March 2021	NM1	51.0	49.3 – 52.2	75		

Major noise sources identified during the noise monitoring included noise from operations of the existing SENT landfill and the TKO Area 137 Fill Bank, aircrafts and insects.

No exceedance of the Action and Limit Levels for construction noise monitoring was recorded in the reporting period. No further mitigation measure was required in accordance with the Event and Action Plan presented in *Annex E2*.

2.3 SURFACE WATER QUALITY MONITORING

2.3.1 Monitoring Requirements and Equipment

According to the updated EM&A Manual of the Project, impact surface water quality monitoring were carried out at the three designated surface water discharge points (i.e. DP3, DP4 and DP6) weekly to ensure that the SENTX

will not cause adverse water quality impact. Temporary relocation of surface water discharge point DP4 to DP4 (Future, temporary) as an interim arrangement due to site constraints and construction sequence was approved by EPD on 14 May 2019. Impact surface water quality monitoring was carried out at DP4 (Future, temporary) (i.e. DP4T) from the monitoring event on 16 May 2019. In addition, suspension of impact surface water quality monitoring at DP3 was approved under the Baseline Monitoring Report by EPD on 24 July 2019 until the actual commencement of construction works affecting DP3 in 2021.

Dissolved Oxygen (DO) and pH value were measured *in situ* whereas the level of suspended solids (SS) were determined by ALS Technichem (HK) Pty Ltd (HOKLAS Registration No. 066).

The Action and Limit Levels of the surface water quality impact monitoring are provided in *Table 2.7*.

Table 2.7 Action and Limit Levels for Surface Water Quality

Parameters	Action Level	Limit Level	
	DP4 & DP6		
DO	< 5.80 mg/L	< 5.42 mg/L	
SS	> 11.7 mg/L	> 12.7 mg/L	
pН	> 8.39	> 8.40	

The locations of the monitoring stations for the Project are shown in *Figure 2.1*. All *in situ* monitoring instruments were checked, calibrated and certified by a laboratory accredited under HOKLAS or other international accreditation scheme before use, and subsequently re-calibrated at 3 monthly intervals throughout all stages of the surface water quality monitoring programme. Calibration for a DO meter was carried out before measurement according to the instruction manual of the equipment model. Details of the equipment used in the impact surface water quality monitoring works are provided in *Table 2.8*.

Table 2.8 Impact Surface Water Quality Monitoring Details

Monitoring Station	Location	Frequency	Monitoring Dates	Parameter	Equipment
DP4 (Future, temporary)	Surface water discharge point DP4	Weekly	7, 14, 20, 28 January 2021 4, 9, 17, 25 February 2021	•pH •DO •SS	YSI Professional DSS (S/N: 17B102764)
DP6	Surface water discharge point DP6	-	4, 11, 18, 25 March 2021		YSI Professional DSS (S/N: 15H103928)
					pH Meter AZ8685 (S/N:1259868)

Notes:

- (a) DP4 was temporary relocated to DP4 (Future, temporary) (i.e. DP4T) as an interim discharge point from the monitoring event on 16 May 2019.
- (b) Impact surface water quality monitoring at DP3 was suspended from the monitoring event on 25 July 2019 until the actual commencement of construction works affecting DP3 in 2021.

2.3.2 Monitoring Schedule for the Reporting Period

The schedule for surface water quality monitoring during the reporting period is provided in *Annex C*.

2.3.3 Results and Observations

A total of 12 monitoring events for impact surface water quality monitoring were scheduled at all designated monitoring stations during the reporting period. However, sampling could not be carried out at the monitoring events below due to insufficient flow:

- January 2021 at all monitoring locations;
- 4 February 2021 at all monitoring locations;
- 9 February 2021 at all monitoring locations;
- 17 February 2021 at all monitoring locations;
- 25 February 2021 at DP6; and
- March 2021 at all monitoring locations;

Impact water quality monitoring results and graphical presentations are provided in *Annex F1*.

Action and Limit Level exceedance was recorded for surface water quality impact monitoring in the reporting period and actions in accordance with the Event and Action Plan presented in *Annex F2* were undertaken.

Investigation on the Action and Limit Levels exceedance was conducted and summarised in *Table 2.9* below. Investigation report of the exceedance is presented in *Annex F3*.

Table 2.9 Details of Exceedances Recorded for Surface Water Quality Monitoring

Date	Monitoring Location	Parameter	Type of Exceedance	Remarks
25 February 2021	DP4T	SS	Limit Level	Project-related

Based on the investigation conducted for the monitoring event with potential Action and Limit Levels exceedance with the Contractor, and the IEC, the SS exceedance at DP4 (Future, temporary) on 25 February 2021 was found deemed to Project-related activities.

The Contractor was reminded to implement all relevant mitigation measures for the construction works and maintain good site practice. The ET will keep track on the monitoring data and ensure Contractor's compliance of the environmental requirements.

2.4 LANDSCAPE AND VISUAL MONITORING

2.4.1 Monitoring Requirements

According to the updated EM&A Manual of the Project, the monthly landscape and visual audit was conducted on 19 January, 24 February and 26 March 2021 to monitor the implementation of the landscape and visual mitigation measures during construction phase.

All relevant environmental mitigation measures listed in the approved EIA Report and the updated EM&A Manual and their implementation status are summarised in *Annex B*.

2.4.2 Results and Observations

The Contractor has implemented environmental mitigation measures as stated in the approved EIA Report and the EM&A Manual.

Regarding the landscape and visual audit, the Contractor was reminded to maintain the advance screen planting works as soon as possible to ensure effective screening of views of project works from the High Junk Peak Trail. The Contractor has considered the mitigation measures during the design phase, including the preparation of the Construction Drawings and Detailed Landscape Design Drawings.

2.5 EM&A SITE INSPECTION

Site inspections were carried out on a weekly basis with the Contractor, IEC and ER to monitor the implementation of proper environmental pollution control and mitigation measures for air quality, noise, surface water quality

and waste management under the Project. In the reporting period, 11 site inspections were carried out on 7, 14, 21 and 28 January , 9, 18 and 25 February, 4, 11, 18 and 25 March 2021. Site inspection on 4 February 2021 was cancelled due to the coronavirus outbreak.

Key observations during the site inspections are summarized in *Table 2.10*.

Table 2.10 Key Observations Identified during the Site Inspections in this Reporting Period

Inspection Date	Environmental Observations and Recommendations
7 January 2021	The Contractor shall remove the general refuse and construction
	waste near future EPD building, at future GVL building and around
	future bioplant building and dispose of the waste accumulated at
	the refuse skips near DP4T and DP6 regularly.
	The Contractor shall provide drip trays for the chemicals stored at
	future GVL building and near Cell 2X.
	 The Contractor shall enhance watering around the site, especially
	near Cell 3X and provide the water truck routing plan for review.
14 January 2021	The Contractor shall display NRMM label on the cherry picker near
	future maintenance building.
	The Contractor shall remove the general refuse accumulated along
	the EVA and dispose of the waste regularly.
	 The Contractor shall provide drip trays for the chemicals stored
	near EVA.
	 The Contractor shall clean up the oil spillage at the cherry picker
	near future EPD building, the generator near DP6 and the excavator
	near Cell 2X and treat the clean-up materials as chemical waste.
21 January 2021	 The Contractor shall enhance watering along the Western site
	boundary to minimise dust impacts.
	The Contractor shall remove the construction materials/ waste
	accumulated at LTP drain and near DP6 and dispose of the waste
	regularly.
28 January 2021	The Contractor shall clean up the oil spillage at the drip tray near
	DP6 and treat the clean-up materials as chemical waste.
	The Contractor shall designate an area for concrete truck washing
	and avoid discharge of wash-water into surrounding water body.
	The Contractor shall remove the general refuse accumulated near future FC tools future assessed area future registered as a building.
	future FS tank, future carpark area, future maintenance building
	and along EVA and dispose of the waste regularly.
	 The Contractor shall repair/ replace the refuse skip near DP6 to ensure proper waste storage.
	 The Contractor shall spray water when conducting dusty operation
	near Southern site boundary to ensure the entire surface is wet.
	The Contractor shall cover the dusty materials accumulated at
	future bioplant building to minimise dust impacts.
9 February 2021	The Contractor shall remove the general refuse accumulated near
of cordary 2021	future bioplant building and construction waste along the Southern
	site boundary and dispose of the waste regularly.
	The Contractor shall clean up the oil spillage around the drip tray
	near site entrance and treat the clean-up materials as chemical
	waste.
	The Contractor shall maintain the concrete truck washing area near
	DP4T to avoid overflow of wash-water into surrounding water
	body.

Inspection Date	Environmental Observations and Recommendations
18 February 2021	The Contractor shall remove the oil contained in the drip tray near
	DP6 and treat the clean-up materials as chemical waste.
	The Contractor shall maintain the concrete truck washing area near
	DP4T to avoid overflow of wash-water into surrounding water
	body.
	 The Contractor shall remove the deposited silt and grit at the
	sediment trap regularly to ensure it is functioning properly at all
	times.
	The Contractor shall maintain the temporary drain along Southern
	site boundary and fully adopt the approved temporary drainage
	plan.
25 February 2021	The Contractor shall maintain the temporary drain along Southern
•	site boundary, provide drainage pump along the drain and fully
	adopt the approved temporary drainage plan.
	The Contractor shall remove the stockpile near sediment trap to
	minimise the generation of high SS runoff.
	The Contractor shall clean up the oil spillage at the drip tray and
	generator near future bioplant and handle the clean-up materials as
	chemical waste.
	The Contractor shall remove the general refuse accumulated near
	future GVL building and dispose of the regularly.
4 March 2021	The Contractor shall maintain and properly form the temporary
1 1/10/21 2021	drain along Southern site boundary and fully adopt the approved
	temporary drainage plan.
	The Contractor shall remove the stockpile and unused pipes near
	DP6 to minimise the generation of high SS runoff.
	The Contractor shall remove the construction waste/ material
	accumulated at the drain at future bioplant and RC15 to ensure it is
	functioning properly at all times.
	The Contractor shall maintain the chemical storage cabinets at
	future LFG plant to allow adequate ventilation and proper
	containment of potential leakage in accordance with the COP.
	The Contractor shall review the capacity of the concrete truck
	washing area and ensure all wash-water are properly contained and
11.14 1 2001	treated before discharge.
11 March 2021	The Contractor shall close the opening at DP6 to minimise SS runoff
	to the channel and ensure all surface water is treated by the Wetsep
	before discharge.
	The Contractor shall remove the stagnant water/ chemical and
	construction materials accumulated in the drip trays near site
	entrance and future LTP and treat the clean-up materials as
	chemical waste.
	The Contractor shall remove the general refuse accumulated near
	future EPD building and GVL building and dispose of the waste
	regularly.
	The Contractor shall provide drip tray for the chemical stored at
	future GVL building.
	The Contractor shall designate an area for concrete truck washing to
	ensure all wash-water is properly contained and treated before
	discharge.
	The Contractor shall remove and dispose of the chemical container
	near sediment trap as chemical waste.

Inspection Date	Environmental Observations and Recommendations
18 March 2021	The Contractor shall replace the faded NRMM labels displayed on
	the excavator near existing LFG plant and generator near Cell 2X
	and display NRMM label on the water pump near Cell 2X, if
	necessary.
	The Contractor shall continue the maintenance work and placement
	of liner at the temporary drain along Southern site boundary to
	fulfil the approved temporary drainage plan.
	The Contractor shall remove the general refuse accumulated near
	future GVL building and at the drain around future LTP and
	dispose of the waste regularly.

The Contractor has rectified all of the observations identified during environmental site inspections in the reporting period. Key environmental deficiencies identified and the corresponding rectification actions are presented in *Table 2.11*.

Table 2.11 Summary of Environmental Deficiencies Identified and Corresponding Additional Control Measures

Deficiencies	Rectifications Implemented	Proposed Additional Control Measures
Surface Water		
Intercepting channels & drainage system	Reviewed drainage plan.	 Provision of additional drainage channels. Expedite the construction of permanent sediment trap and discharge culverts.
DP channels (design & regular silt removal)	 Carried out regular maintenance and cleaning of channels. DP4 channel: Area near the channel was paved with concrete and a bund was built. DP6 channel: Gravel piles on the channel were covered with concrete which serve as blocks for running water and to divide the channel into several sections. A pump was placed in the water zone in the upstream section to pump water to the Wetsep for treatment prior to the discharge to the last section before the weir plate. DP6: Pipes through the gravel piles between different channel sections were covered with geotextiles to block debris and silt. 	N.A.
Stockpiles & exposed soil	• Installed silt fencing near surface water channel along DP6 channel.	Improve soil covering.Compaction and cover for stockpiles and soil slopes.
Wetsep (treatment capacity & number)	 Reviewed Wetsep capacity. Chemicals dosage of the Wetsep was increased to enhance the efficiency. 	Install additional Wetsep.

Deficiencies	Rectifications Implemented	Proposed Additional Control Measures
Backflow / ponding	 Raised with EPD (LDG) and CEDD. 	N.A.
during heavy rainfall		

2.6 WASTE MANAGEMENT STATUS

The Contractor has registered as a chemical waste producer under the Contract. Sufficient numbers of receptacles were available for general refuse collection and sorting.

As informed by the Contractor, waste generated during this reporting period include mainly inert C&D materials. Reference has been made to the waste flow table prepared by the Contractor. The quantities of different types of wastes and imported fill materials are summarised in *Table 2.12*.

Table 2.12 Quantities of Different Waste Disposed and Imported Fill Materials

Month/ Year	Inert C&D Materials ^(a) (in '000m ³)		rted Fill 10kg) ^(b)	Inert Construction Waste Re- used	Non-inert Construction Waste (c) (in '000m³)	Recyclable Materials (d) (in '000kg)	Chemical Wastes (in '000kg)
		Rock	Soil	(in '000m ³)			
January 2021	0.297	0	0	0	0.090	0.090	0
February 2021	1.584	0	0	0	0.061	0	0.086
March 2021	0.875	0	0	0	0.100	0	0

Notes:

- (a) Inert construction wastes include hard rock and large broken concrete, and materials disposed as public fill. Density assumption: $1.6 \text{ (t/m}^3)$ for public fill.
- (b) Imported fill refers to materials generated from other project for on-site resue.
- (c) Non-inert construction wastes include general refuse disposed at landfill. Density assumption: $0.9 \text{ (t/m}^3)$ for general refuse.
- (d) Recyclable materials include metals, paper, cardboard, plastics and others.

2.7 IMPLEMENTATION STATUS OF ENVIRONMENTAL MITIGATION MEASURES

A summary of the Environmental Mitigation Implementation Schedule is presented in *Annex B*. The necessary mitigation measures were implemented properly for the Project.

2.8 SUMMARY OF EXCEEDANCES OF THE ENVIRONMENTAL QUALITY PERFORMANCE LIMIT

The 24-hour TSP monitoring results and construction noise monitoring results complied with the Action and Limit Levels in the reporting period. One exceedance of the Limit Level for SS was recorded for surface water quality impact monitoring in the reporting period. The SS exceedance at DP4 (Future, temporary) on 25 February 2021 was found deemed to Project-related activities.

Cumulative statistics on exceedances is provided in *Annex G*.

2.9 SUMMARY OF COMPLAINTS, NOTIFICATION OF SUMMONS AND SUCCESSFUL PROSECUTIONS

There were no complaints, notification of summons or prosecution recorded in the reporting period.

Statistics on complaints, notifications of summons and successful prosecutions are summarised in *Annex G*.

3 CONCLUSION AND RECOMMENDATION

This Quarterly EM&A Report presents the findings of the EM&A activities undertaken during the period from 1 January to 31 March 2021 in accordance with the updated EM&A Manual and the requirements of the Environmental Permit (*EP-308/2008/B*).

Air quality (24-hour TSP), noise and water quality (DO, pH and SS) monitoring were carried out in the reporting period. Results for air quality monitoring (24-hour TSP) complied with the Action and Limit Levels in the reporting period. No Action and Limit Levels exceedances were recorded for construction noise monitoring. One exceedance of the Limit Level for SS was recorded for surface water quality impact monitoring in the reporting period. The SS exceedance at DP4 (Future, temporary) on 25 February 2021 was found deemed to Project-related activities.

Eleven environmental site inspections were carried out during the reporting period. Environmental deficiencies were identified during the site inspection and the Contractor has proposed additional control measures to rectify the deficiencies.

There were no complaints, notification of summons or prosecution recorded in the reporting period.

It is noted that most environmental pollution control and mitigation measures were properly implemented and the construction activities of the Project did not introduce any adverse impact to the sensitive receivers in the reporting period. Yet, some environmental deficiencies were identified during the reporting period and additional control measures have been proposed by the Contractor to rectify the corresponding deficiencies. The monitoring programme has been reviewed and was considered as adequate to cater for the nature of works in progress. Change to the monitoring programme was thus not recommended at this stage. The monitoring programme will be evaluated as appropriate in the next reporting period. The ET will keep track on the construction works to confirm compliance of environmental requirements and the proper implementation of all necessary mitigation measures.

Annex A

Work Programme

A2.5 Construction (Initial Works) 6A2.5.02 Advance Works & Site Establishment SA2.5.02.01 Site Establishment & Mobilization 5.00.04	1153 12-Apr-18 07-Jun-21 705 1148 12-Apr-18 02-Jun-21 35 333 12-Apr-18 10-Mar-19 820		
02.01 52-1000 Site Mobilization for Parts X1 & X2 02.01 52-1100 Site Mobilization for Parts X3, X4 & X5 02.01 52-1200 Temporary Office for Employer / ER / IC	30 31-Dec-18 29-Jan-19 820 11-1100: FS, 11-1200: FS 30 12-Apr-18 11-May-18 1083 11-1300: FS, 11-1400: FS, 11-1500: FS 60 10-Oct-18 08-Dec-18 0 23-1300: FS	52-1300: FS, M 3. 1: FS, M 3. 2: FS 52-1300: FS, M 3. 1: FF 11-1700: SS, M 3. 1: FS	
A2.5.02.02 Site Survey & Investigation Works for Parts X1 & X2 5.02.02 52-1400 Condition Survey	40 30-Jan-19 10-Mar-19 820 52-1000: FS, 52-1100: FS 50 31-Dec-18 18-Feb-19 840 25 31-Dec-18 24-Jan-19 840 11-1100: FS, 11-1200: FS	32-1500: FS, M10. 1: FS -26, M10. 2: FS -13, M10. 3: FS 52-1600: FS	
5.02.02 52-1500 Topographic Survey 5.02.02 52-1600 Site inspection, Review of Condition Survey Report SA2.5.02.03 Site Survey & Investigation Works for Parts X3, X4 & X5	20 31-Dec-18 19-Jan-19 845 11-1100: FS, 11-1200: FS 25 25-Jan-19 18-Feb-19 840 52-1500: FS, 52-1400: FS 50 12-Apr-18 31-May-18 1103	52-1600: FS 32-1500: FS	
5.02.03 52-1700 Condition Survey 5.02.03 52-1800 Topographic Survey 5.02.03 52-1900 Site inspection, Review of Condition Survey Report	25 12-Apr-18 06-May-18 1103 11-1300: FS, 11-1400: FS, 11-1500: FS 20 12-Apr-18 01-May-18 1108 11-1300: FS, 11-1400: FS, 11-1500: FS 25 07-May-18 31-May-18 1103 52-1700: FS, 52-1800: FS	52-1900: FS 52-1900: FS 32-1500: FS	
SA2.5.02.04 Environmental Monitoring 5.02.04 52-2000 Installation of Monitoring Stations & Wells (GP & GW) 5.02.04 52-2100 Installation of Monitoring Stations & Wells (GP & GW) on Buttress Wall	975 02-Oct-18 02-Jun-21 35 120 02-Oct-18 29-Jan-19 0 23-1600: FS 120 02-Oct-18 29-Jan-19 0 23-1600: FS	52-2200: SS 60 52-2200: SS 60	
5.02.04 52-2200 Conduct Baseline Monitoring for Construction (one month) 5.02.04 52-2300 Conduct Baseline Monitoring for Operation (one year)	30 01-Dec-18 30-Dec-18 0 52-2000: SS 60, 52-2100: SS 60 365 03-Jun-20 02-Jun-21 35 32-1500: FS -400, 53-4500: FS	11-1100: FS 12-1400: FS	
SA2.5.03 Civil Engineering Works SA2.5.03.0 Buttress Wall 5.03.0 Section adj. SENT	748 13-Jan-19 29-Jan-21 834 475 02-Mar-19 18-Jun-20 83 300 13-Apr-19 06-Feb-20 96 11-1300: FS, 23-2500: FS, 53-3000: FS, 31-1200: F 11-1400: FS	S, 53-1100: FS, 53-1300: FS, 53-3100: FS, M 3. 5: FS -150, M 3. 7: FS	
5.03.0 53-1100 Diversion of SENT Landfill Gas Pipe 5.03.0 53-1200 Section at Cell 4	45 07-Feb-20 22-Mar-20 96 23-2500: FS, 53-1000: FS 400 02-Mar-19 04-Apr-20 83 11-1300: FS, 23-2500: FS, 53-3000: FS, 11-1400: F		
5.03.0 53-1300 Install Landfill Gas Pipe on Buttress Wall SA2.5.03.1 Landfill Cell 1 5.03.1 53-1400 Earth bund (Eastern)	75 05-Apr-20 18-Jun-20 83 41-1500: FS, 53-1100: FS, 53-1200: FS, 53-1000: F 503 13-Jan-19 29-May-20 214 90 04-Aug-19 01-Nov-19 9 11-1100: FS, 23-2500: FS, 53-4200: FS, 53-2800: F	5 53-2000: FS, 53-2300: FS, 53-3400: FS, 63-1000: FS,	
5.03.1 53-1500 Earth bund (Southern)	90 26-Apr-19 24-Jul-19 314 11-1100: FS, 23-2500: FS, 53-2800: FS	63-1100: FS, 63-1200: FS, 63-1300: FS, M 4. 2: FS 53-2000: FS, 53-2200: FS, 53-2300: FS, 53-3400: FS, 53-3700: FS, 53-3800: FS	
5.03.1 53-1600 Earth bund (Western) 5.03.1 53-1700 Intercell bund (Cell 1/2)	90 13-Jan-19 12-Apr-19 417 11-1100: FS, 23-2500: FS 75 13-Jan-19 28-Mar-19 432 11-1100: FS, 23-2500: FS	53-1900: FS, 53-2000: FS, 53-2200: FS, 53-3800: FS 53-2000: FS	
5.03.1 53-1800 Site Formation 5.03.1 53-1900 Pump Station (PS#1X) 5.03.1 53-2000 Lining Works	90 13-Jan-19 12-Apr-19 217 11-1100: FS, 23-2500: FS, 31-1300: FS 45 13-Apr-19 27-May-19 507 53-1800: FS, 53-1600: FS 135 02-Nov-19* 15-Mar-20 214 41-1500: FS, 53-1400: FS, 53-1500: FS, 53-1600: FS	53-1900: FS, 63-1100: FS, 63-1200: FS, 63-1300: FS, M 4. 1: FS -45 53-2100: FS, 53-2200: FS	
5.03.1 53-2000 Lining Works 5.03.1 53-2100 Protective Stone Laying & Leachate Collection Pipe 5.03.1 53-2200 Install Leachate Force Main	135 02-Nov-19* 15-Mar-20 214 41-1500: FS, 53-1400: FS, 53-1500: FS, 53-1600: F 75 16-Mar-20 29-May-20 214 53-2000: FS, 41-1500: FS, 53-1900: FS 75 25-Jul-19 07-Oct-19 449 53-1500: FS, 53-1600: FS, 41-1500: FS, 53-1900: F	32-1500: FS, 54-2800: FS, M 4. 3: FS	
5.03.1 53-2300 Install Landfill Gas Pipe on earth bund 5.03.1 53-2400 Leachate Pipe Connection (Cell 1 to LTP)	55 02-Nov-19 26-Dec-19 258 41-1500: FS, 53-1400: FS, 53-1500: FS 30 09-Mar-20 07-Apr-20 266 23-2500: FS, 54-1000: SS	54-4000: FS 54-2800: FS	
SA2.5.03.4 Landfill Cell 4 5.03.4 53-2500 Provide Temporary Leachate Pipe on Cell 4 Area SA2.5.03.5 Drainage - Surface Run-Off 5.03.5 53-2600 Construct Cut-Off Channel 12A	30 09-Jul-20 07-Aug-20 144 30 09-Jul-20 07-Aug-20 144 23-2500: FS, 63-2600: SS -90 740 16-Jan-19 24-Jan-21 839 60 16-Jan-19 16-Mar-19 9 11-1100: FS 23-2800: FS	54-2800: FS, M 3. 3: FS	
5.03.5 53-2600 Construct Cut-Off Channel 12A 5.03.5 53-2700 Connect Cut-Off Channel 12A to DP6 5.03.5 53-2800 Diversion from Existing Trapezoidal Channel into Channel 12A	60 16-Jan-19 16-Mar-19 9 11-1100: FS, 23-2800: FS 20 17-Mar-19 05-Apr-19 9 53-2600: FS, 31-1400: FS, 23-1900: FS 20 06-Apr-19 25-Apr-19 9 53-2700: FS	53-2700: FS 53-2800: FS 53-1400: FS, 53-1500: FS, 53-2900: FS, 63-1000: FS, 63-1900: FS, M 3. 3: FS	
5.03.5 53-2900 Removal of Existing Trapezoidal Channel along Eastern Bund 5.03.5 53-3000 Cut-Off Channel C4 Diversion to Cut-Off Channel 17-2 5.03.5 53-3100 Cut-Off Channel X5 on Buttress Wall, Cell 4, Cell 3	30 26-Apr-19 25-May-19 9 53-2800: FS 45 16-Jan-19 01-Mar-19 83 11-1300: FS, 23-2800: FS 90 05-Apr-20 03-Jul-20 289 53-1000: FS, 53-1200: FS	63-1900: FS, M 3. 3: FS 53-4200: FS 53-1000: FS, 53-1200: FS	
5.03.5 53-3200 Temporary Diversion Cut-Off Channel X5 to 12A 5.03.5 53-3300 Culvert X5 (5m long) & Perm Connection of Cut-Off Channel X5	20 04-Jul-20 23-Jul-20 289 53-3100: FS, 23-1900: FS 30 26-Dec-20 24-Jan-21 134 53-4100: FF, 63-1900: FS, 53-3200: FS	53-3300: FS, M 3. 4: FS 32-1500: FS	
 5.03.5	50 02-Nov-19 21-Dec-19 249 53-1400: FS, 53-1500: FS 50 20-Feb-20 09-Apr-20 189 63-1000: FS, 53-3400: FS 50 09-Jun-20 28-Jul-20 129 63-1900: FS, 53-3500: FS	53-3500: FS 53-3600: FS 53-3900: FS	
5.03.5 53-3700 Culvert X6 (25m long) at Cell 1 Southern Bund 5.03.5 53-3800 Perimeter Channel (X9B) at Cell 1 Southern & Western Bund 5.03.5 53-3900 Drop Inlet & Culvert (X9) - 21m long	75 25-Jul-19 07-Oct-19 1314 53-1500: FS 45 25-Jul-19 07-Sep-19 1344 53-1500: FS, 53-1600: FS 180 29-Jul-20 24-Jan-21 129 11-1100: FS, 23-1900: FS, 53-3600: FS	53-4000: FF, 53-4100: FF, 53-6000: FS, M 9. 1: FS -90, M 9.	
5.03.5 53-4000 Sediment Trap (ST) 5.03.5 53-4100 Dual Culvert 74m long (connect to DP4)	180 29-Jul-20 24-Jan-21 129 11-1100: FS, 23-1900: FS, 11-1200: FS, 53-3900: F	2: FS 53-6000: FS, M 9. 3: FS -90, M 9. 4: FS	
5.03.5 53-4100 Dual Culvert 74m long (connect to DP4) SA2.5.03.6 Drainage - Ground Water 5.03.6 53-4200 Construct Groundwater Collection Pipe along Cells X1 & X2 Eastern Bund	180 29-Jul-20 24-Jan-21 129 11-1100: FS, 11-1200: FS, 23-1900: FS, 53-3900: F 200 26-May-19 11-Dec-19 209 70 26-May-19 03-Aug-19 9 11-1100: FS, 23-1600: FS, 53-2900: FS	53-3300: FF, 53-6000: FS, M 9. 1: FS -90, M 9. 2: FS 53-1400: FS, 53-4300: FS, 63-1000: FS, 63-1900: FS	
5.03.6 53-4300 Construct Groundwater Collection Pipe along Cell X3 Eastern Bund 5.03.6 53-4400 Construct Groundwater Collection Pipe along Intercell Bund X2/X3 5.03.6 53-4500 Construct Manhole MH-X1	50 04-Aug-19 22-Sep-19 159 53-4200: FS 50 23-Sep-19 11-Nov-19 209 53-4300: FS 30 12-Nov-19 11-Dec-19 209 53-4400: FS	53-4400: FS, 63-1900: FS 53-4500: FS, 63-1200: FS 52-2300: FS M 9, 5: FS	
5.03.6 53-4500 Construct Manhole MH-X1 SA2.5.03.7 Utilities - Distribution within New Infrastructure Area 5.03.7 53-4600 Power Supply HV Works (Transformer & HV switchgear)	30 12-Nov-19 11-Dec-19 209 53-4400: FS 391 11-Aug-19 04-Sep-20 276 5 30-Jun-20 04-Jul-20 0 54-3000: FS	52-2300: FS, M 9. 5: FS 12-1200: FS	
 5.03.7	2 05-Jul-20 06-Jul-20 0 54-3100: FS, 12-1200: FS 60 07-Jul-20 04-Sep-20 271 54-1000: FS, 54-3100: FS, 54-3300: FS, 54-4100: F 60 07-Jul-20 04-Sep-20 271 54-1000: FS, 54-4100: FS, 54-4600: FS	12-1000: FS 3 12-1100: FS, 53-6100: FS 12-1100: FS, 53-6100: FS	
5.03.7 53-5000 Lighting Provision 5.03.7 53-5100 Fire Services	30 07-Jul-20 05-Aug-20 6 54-1000: FS, 54-4100: FS, 54-4600: FS 115 12-Mar-20 04-Jul-20 2 53-6800: FS	12-1100: FS, 32-2100: FS 12-1000: FS	
5.03.7 53-5200 Water Supply (Fresh & Salt) 5.03.7 53-5300 Telecom & Network 5.03.7 53-5400 Gas Network (LFG to LTP)	115 12-Mar-20 04-Jul-20 338 53-6600: FS, 53-6700: FS 45 11-Aug-19 24-Sep-19 622 53-6400: FS 15 22-Jun-20 06-Jul-20 176 54-1000: FF	12-1100: FS 12-1100: FS 54-2800: FS	
SA2.5.03.8 Utilities - Works Associated with Utilities Undertakers SA2.5.03.8.U1 CLP 5.03.8.U1 53-5500 Excavate Trench for CLP Cable	703 27-Feb-19 29-Jan-21 129 459 27-Feb-19 30-May-20 43 100 13-May-19 20-Aug-19 194 23-2900: FS	53-5800: FS, 54-1000: SS, 54-4100: SS, 54-4600: SS, M10. 1: FS -60, M10. 2: FS -30, M10. 3: FS	
5.03.8.U1 53-5600 Backfill Trench after CLP Cable Laying 5.03.8.U1 53-5700 CLP Cable Laying (from CLP Substation to Site Boundary)	30 01-May-20 30-May-20 43 53-5800: FS 200 27-Feb-19 14-Sep-19 229 32-2400: FS	54-1000: FF, 54-4100: FF, 54-4600: FF 54-3000: FS	
5.03.8.U1 53-5800 CLP Cable Laying (from Site Boundary to HV Switchroom) 5.03.8.U1 53-5900 CLP HV associated equipment installation	60 02-Mar-20 30-Apr-20 0 53-5500: FS, 54-2900: FS, 32-2400: FS, 53-5900: FI 120 18-Dec-19 15-Apr-20 0 54-2900: FS, 32-2400: FS 147 05-Sep-20 29-Jap-21 129	53-5600: FS, 54-3000: FS 53-5800: FF 15	
SA2.5.03.8.U2 DSD 5.03.8.U2 53-6000 Connection to Storm Drain System 5.03.8.U2 53-6100 Connection to Foul Drain System	147 05-Sep-20 29-Jan-21 129 5 25-Jan-21 29-Jan-21 129 53-4100: FS, 53-4000: FS, 53-3900: FS 5 05-Sep-20 09-Sep-20 271 53-4800: FS, 53-4900: FS 100 13 May 19 20 Aug 19 327	32-1500: FS 32-1500: FS	
SA2.5.03.8.U3 Telecom 5.03.8.U3 53-6200 Excavate Trench for PCCW	100 13-May-19 20-Aug-19 327 60 13-May-19 11-Jul-19 307 23-2900: FS	53-6400: FS, 54-1000: SS, 54-4100: SS, 54-4600: SS, M10. 1: FS -40, M10. 2: FS -20, M10. 3: FS	
5.03.8.U3 53-6300 Backfill Trench after PCCW Cable Laying 5.03.8.U3 53-6400 Laying Cables & Connection SA2.5.03.8.U4 WSD	10 11-Aug-19 20-Aug-19 327 53-6400: FS 30 12-Jul-19 10-Aug-19 327 53-6200: FS 304 13-May-19 11-Mar-20 338	54-1000: FF, 54-4100: FF, 54-4600: FF 53-5300: FS, 53-6300: FS	
 5.03.8.U4 53-6500 Install Watermain & Piping for Water Supplies 5.03.8.U4 53-6600 Connection for Fresh Water & Meter Installation 	60 13-May-19 11-Jul-19 216 23-2900: FS 30 11-Feb-20 11-Mar-20 338 53-6500: FS, 32-2300: FS	53-6600: FS, 53-6700: FS, 53-6800: FS, 53-6900: FS 53-5200: FS 53-5200: FS	
5.03.8.U4 53-6700 Connection for Salt Water 5.03.8.U4 53-6800 Connection for Fire Services 5.03.8.U4 53-6900 Connection for Cooling Tower & Meter Installation	30 11-Feb-20 11-Mar-20 338 53-6500: FS, 32-2300: FS 30 11-Feb-20 11-Mar-20 2 53-6500: FS, 32-2300: FS 30 11-Feb-20 11-Mar-20 117 53-6500: FS, 32-2300: FS	53-5200: FS 53-5100: FS 54-2700: FS, 54-3900: FS	
SA2.5.03.8.U5 HyD Lighting 5.03.8.U5 53-7000 Installation of Public Street Lighting / Handover SA2.5.04 Building Construction, incl. E&M and System Installation, and T&C SA2.5.04 Part X1 Area A	120 07-Jul-20 03-Nov-20 216 120 07-Jul-20 03-Nov-20 216 54-4100: FS, 54-4600: FS, 54-1000: FS 890 31-Dec-18 07-Jun-21 0	32-1500: FS	
SA2.5.04.A Part X1 Area A 5.04.A 54-1000 General Area & Access Road	554 31-Dec-18 06-Jul-20 36 120 09-Mar-20 06-Jul-20 6 23-1300: FS, 53-5500: SS, 53-5600: FF, 53-6200: S 53-6300: FF, 12-1000: FF, 11-1100: FS, 54-1100: FI 54-1800: FF	, 53-5000: FS, 53-5400: FF, 53-7000: FS, 68-1700: FS	
5.04.A 54-1100 Carpark & Supporting Area 5.04.A 54-1200 Diesel Fuel Tanks	60 31-Dec-18 28-Feb-19 64 23-1300: FS, 11-1100: FS 60 08-May-20 06-Jul-20 36 23-1300: FS, 23-5200: FS, 12-1000: FF, 11-1100: FS		
5.04.A 54-1300 EPD Building 5.04.A 54-1400 Fire Service Tank	270 30-Apr-19 24-Jan-20 44 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1700: Si 270 29-Jun-19 24-Mar-20 44 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1300: Si	54-1400: SS 60	
5.04.A 54-1500 GVL Building 5.04.A 54-1600 Laboratory Building	300 31-Dec-18 26-Oct-19 44 23-1300: FS, 23-5200: FS, 11-1100: FS 270 28-Aug-19 23-May-20 44 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1400: S	32-2100: FS, M 5. 1: SF 30, M 5. 2: SF 150, M 5. 3: FS, 54-1700: SS 60 32-2100: FS, M 5. 6: FS -135, M 5. 7: FS, 12-1000: FS,	
5.04.A 54-1700 Maintenance Building & Area 5.04.A 54-1800 Storage Facility & Area	270 01-Mar-19 25-Nov-19 44 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1500: S 60 01-Mar-19 29-Apr-19 64 23-1300: FS, 11-1100: FS, 54-1100: FS	54-1300: SS 60 32-1500: FS, M 5.11: FS -30, M 5.12: FS, 54-1000: FF,	
5.04.A 54-2000 Waste Oil Tanks 5.04.A 54-2000 Water Service House	90 08-Apr-20 06-Jul-20 36 23-1300: FS, 23-5200: FS, 12-1000: FF, 11-1100: FS 60 30-Apr-19 28-Jun-19 64 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1800: F	54-2000: FS 32-2200: FS	
SA2.5.04.B Part X1 Area B SA2.5.04.B.1 BioPlant Building	890 31-Dec-18 07-Jun-21 0 330 17-Jan-19 12-Dec-19 243		
5.04.B.1 54-2100 LTP BioPlant Building SA2.5.04.B.2 Leachate Treatment Plant 5.04.B.2 54-2200 Main Plant Area included Civil works	330 17-Jan-19 12-Dec-19 243 23-1300: FS, 23-5200: FS, 23-3200: FS, 11-1100: FS 31-1000: FS 31-Dec-18 10-Aug-20 21 274 31-Dec-18 30-Sep-19 0 23-1300: FS, 23-3200: FS, 11-1100: FS	54-2300: FS, 54-2400: FS, 54-2500: FS, 64-1100: FS, M 6. 1:	
5.04.B.2 54-2300 MEP Installation	220 01-Oct-19 07-May-20 0 41-2100: FS, 41-1800: FS, 22-2100: FS, 54-2200: FS	SF 30, M 6. 4: FS -137, M 6. 5: FS	
5.04.B.2 54-2400 SBR Tanks 5.04.B.2 54-2500 Ammonia Stripper SA2.5.04.B.3 LTP - Test & Commission	100 01-Oct-19 08-Jan-20 236 41-2400: FS, 54-2200: FS 315 01-Oct-19 10-Aug-20 21 41-3000: FS, 54-2200: FS 301 11-Aug-20 07-Jun-21 0	54-2600: FS, M 6. 6: FS 54-2600: FS, M 6. 8: FS -150, M 6. 9: FS	
5.04.B.3 54-2700 Wet testing 5.04.B.3 54-2700 Wet testing	45 11-Aug-20 24-Sep-20 21 54-2300: FS, 54-2400: FS, 54-2500: FS 75 25-Sep-20 08-Dec-20 21 54-2600: FS, 12-1200: FS, 53-6900: FS, 31-2200: FS 23-6800: FS	23-6600: FS -150, 23-6900: SS, 54-2700: FS, M11. 1: FS 5, 54-2800: FS, M11. 2: FS	
5.04.B.3 54-2800 Operational testing SA2 5.04.C. Part X1 Area C.	160 30-Dec-20 07-Jun-21 0 54-2700: FS, 53-2400: FS, 53-2500: FS, 53-2100: FS 53-2200: FS, 63-1700: FS, 63-2600: FS, 53-5400: FS 54-4000: FS		
SA2.5.04.C.1 LFG - Power Supply Building 5.04.C.1 54-2900 LFG Building (with Transformer Room)	730 31-Dec-18 29-Dec-20 0 530 17-Jan-19 29-Jun-20 5 335 17-Jan-19 17-Dec-19 0 23-1300: FS, 23-3500: FS, 11-1100: FS, 31-1000: FS	FS S	
5.04.C.1 54-3000 Transformer & HV Swtichgear Installation 5.04.C.1 54-3100 MEP Installation, with T&C	60 01-May-20 29-Jun-20 0 54-2900: FS, 41-1200: FS, 53-5800: FS, 53-5700: FS 75 18-Dec-19 01-Mar-20 125 54-2900: FS	5 53-4600: FS, M 7. 4: FS -30, M 7. 5: FS, M 7. 5: FF 32-1400: FS, 32-2100: FS, 53-4700: FS, 53-4800: FS, M 7. 4: FS -30, M 7. 5: FS	
SA2.5.04.C.2 LFG Treatment Plant 5.04.C.2 54-3200 Main Plant Area included Civil Works	554 31-Dec-18 06-Jul-20 0 384 31-Dec-18 18-Jan-20 0 23-3500: FS, 11-1100: FS	54-3300: FS, 54-3400: FS, 54-3500: FS, 54-3600: FS, 54-3700: FS, 54-3800: FS, M 7. 1: SF 30, M 7. 2: FS -200, M 7. 3: FS	
5.04.C.2 54-3300 MEP Installation 5.04.C.2 54-3400 GHS600 Blower 601 A&B Relocation	170 19-Jan-20 06-Jul-20 0 54-3200: FS, 12-1000: FF 15 19-Jan-20 02-Feb-20 155 23-5800: FS, 54-3200: FS	32-2000: FS, 53-4800: FS, 54-3900: FS, M 7. 4: FS -80, M 7. 5: FS 54-3900: FS, M 7. 4: FS -8, M 7. 5: FS	
5.04.C.2 54-3500 Pre-treatment 5.04.C.2 54-3600 Flares (incl. PLC control, interlink to Towngas PF & LTP) 5.04.C.2 54-3700 LFG Engine (incl. on-grid protection, PLC control, turning)	60 19-Jan-20 18-Mar-20 110 41-3900: FS, 54-3200: FS 125 19-Jan-20 22-May-20 45 41-3300: FS, 54-3200: FS 110 21-Feb-20 09-Jun-20 27 41-3600: FS, 54-3200: FS	54-3900: FS, M 7. 4: FS -30, M 7. 5: FS 54-3900: FS, M 7. 4: FS -60, M 7. 5: FS 54-3900: FS, M 7. 4: FS -60	
5.04.C.2 54-3800 Cooling System SA2.5.04.C.3 LFG - Test & Commission 5.04.C.3 54-3900 MEP Testing	45 19-Jan-20 03-Mar-20 125 22-1500: FS, 54-3200: FS 176 07-Jul-20 29-Dec-20 0 65 07-Jul-20 09-Sep-20 0 54-3400: FS, 54-3500: FS, 54-3600: FS, 54-3700: FS 54-3800: FS, 54-3600: FS, 54-3700: FS, 54-3800: FS, 54-3800: FS, 54-3700: FS, 54-3800: FS,	54-3900: FS, M 7. 4: FS -25, M 7. 5: FS 6, 23-7000: SS -150, 23-7300: SS, 54-4000: FS, M11. 1: FS -30,	
5.04.C.3 54-4000 Operational Testing	54-3800: FS, 12-1200: FS, 53-6900: FS, 31-2200: FS 54-3300: FS 111	S, M11. 2: FS	
SA2.5.04.D Part X1 Area D 5.04.D 54-4100 General Area & Access Road	374 29-Jun-19 06-Jul-20 6 120 09-Mar-20 06-Jul-20 6 23-1300: FS, 53-5500: SS, 53-5600: FF, 53-6200: SS	3, 32-2100: FS, 53-4800: FS, 53-4900: FS, 53-5000: FS, 53-7000: FS, M 8. 5: FS	
5.04.D 54-4200 VWF Building 5.04.D 54-4300 Weighbridge	120 28-Oct-19 24-Feb-20 63 23-1300: FS, 23-5200: FS, 41-4500: FS, 11-1100: FS 54-4300: SS 60 75 29-Aug-19 11-Nov-19 63 41-4200: FS, 23-1300: FS, 23-5200: FS, 11-1100: FS	S, 32-2100: FS, M 8. 4: FS, M 8. 6: FS -60, M 8. 7: FS, 12-1000: FS, 54-4500: SS 60	
5.04.D 54-4300 Weighbridge 5.04.D 54-4400 Weighmaster House	54-4400: SS 60 120 29-Jun-19 26-Oct-19 64 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-2000: FS	32-2100: FS, M 8. 1: FS, 12-1000: FS, 54-4300: SS 60	
5.04.D 54-4500 Wheel Wash Bath SA2.5.04.E Part X1 Area E & Part X2 5.04.E 54-4600 General Area & Access Road	75 27-Dec-19 10-Mar-20 63 23-1300: FS, 23-5200: FS, 41-4500: FS, 11-1100: FS 54-4200: SS 60 163 26-Jan-20 06-Jul-20 6 53-5500: SS, 53-5600: FF, 53-6200: SS, 53-6300: FI		
5.04.E 54-4600 General Area & Access Road 5.04.E 54-4700 Guard House & Entrance Gate	120 09-Mar-20 06-Jul-20 6 53-5500: SS, 53-5600: FF, 53-6200: SS, 53-6300: FF 12-1000: FF, 11-1100: FS, 11-1200: FS 100 26-Jan-20 04-May-20 63 23-1300: FS, 23-5200: FS, 11-1100: FS, 11-1200: FS 54-4500: SS 30		
SA2.5.08 Landscape Works - Advance Screen Planting in CWB Country Park SA2.5.08.N Area N 5.08.N 58-1000 Advance Screen Planting	54-4500: SS 30 270	14-1800: SS -60, 58-1100: SS, 68-1600: SS 30, M 3. 2: FS	
5.08.N 58-1100 Establishment of Screen Planting SA2.5.08.S Area S	270 01-Apr-19* 26-Dec-19 529 58-1000: SS, 14-1800: FS 270 01-Apr-19 26-Dec-19 529	32-1500: FS	
5.08.S 58-1200 Advance Screen Planting 5.08.S 58-1300 Establishment of Screen Planting 6A2.6 Construction (Remaining Works)	90 01-Apr-19* 29-Jun-19 529 23-7900: FS, 31-1100: FS, 11-1500: FS 270 01-Apr-19* 26-Dec-19 529 58-1200: SS 1474 01-Apr-19 13-Apr-23 30	58-1300: SS, M 3. 2: FS 32-1500: FS	
SA2.6.02 Advance Works SA2.6.02.9 Demolition of SENT Infrastructure Area 6.02.9 62-1000 Existing SENT General Infrastructure Facility & Building	80 09-Jul-21 26-Sep-21 339 80 09-Jul-21 26-Sep-21 339 60 09-Jul-21 06-Sep-21 239 32-2100: FS, 12-1300: FS	23-2000: SS -90, 63-2800: FS, 63-2900: FS, 63-3000: FS, 63-4300: FS, M12. 4: FS -30, M12. 5: FS	
6.02.9 62-1100 Existing SENT LTP	60 29-Jul-21 26-Sep-21 339 32-1500: FS, 12-1300: FS, 23-2200: FS 60 29-Jul-21 26-Sep-21 339 32-1500: FS, 12-1300: FS, 23-2200: FS	63-3000: FS, 63-4500: FS, M12. 4: FS -30, M12. 5: FS	
6.02.9 62-1200 Existing SENT LFG	60 29-Jul-21 26-Sep-21 339 32-1500: FS, 12-1300: FS, 23-2200: FS	63-3000: FS, 63-4500: FS, M12. 4: FS -30, M12. 5: FS	

#	WBS Path		ctivity O	Activity Name	Dur	Sta	t Finish	Total Predecessor Details Float	Successor Details
509		. <mark>6.03 Civ</mark> .6.03.2 La		eering Works			9 13-Apr-23 9 23-Jan-21		
511				Earth bund (Eastern)				9 11-1100: FS, 23-2500: FS, 53-4200: FS, 53-1400: F	
	ı							53-2800: FS	63-2000: FS, 63-2100: FS, 63-2200: FS, M12. 1: FS -50, M12. 2: FS, 63-1100: FS
512	6.03	3.2	3-1100	Earth bund (Western)	110	20-Feb-	0 08-Jun-20	84 11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: F	S, 63-1400: FS, 63-1500: FS, 63-1700: FS, 63-3500: FS,
012								63-1000: FS	63-3600: FS, 63-1200: FS
513	6.03	,.2 f	3-1200	Intercell bund (Cell 2/3)	90	09-Jun-	0 06-Sep-20	734 11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: F 53-4400: FS, 63-1100: FS	S, 63-1500: FS
514	6.03	3.2	3-1300	Site Formation	75	02-Nov-	9 15-Jan-20	14 11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: F	S 63-1400: FS, 63-4200: FS
515	6.03	3.2	3-1400	Pump Station (PS#2X)	45	09-Jun-	0 23-Jul-20	84 63-1300: FS, 63-1100: FS	63-1600: FS, 63-1700: FS
516				Lining Works				710 41-1500: FS, 63-1000: FS, 63-1100: FS, 63-1200: F	·
517	6.03	2 2	2 1600	Protective Stone Laying & Leachate Collection Pipe	25	30 Doo	0 22 Ion 21	810 63-1500: FS, 41-1500: FS, 63-1400: FS	32-1600: FS, M12. 3: FS
518				Install Leachate Force Main				84 63-1100: FS, 41-1500: FS, 63-1400: FS	54-2800: FS, M12. 3: FS
519				Install Landfill Gas Pipe on earth bund				168 41-1500: FS, 63-1000: FS	54-4000: FS, M12. 3: FS
520		2.6.03.3 La		<u>'</u>	714	20-Feb-	0 02-Feb-22	435	·
521	6.03).3 ر	3-1900	Earth bund (Eastern)	110	20-Feb-	0 08-Jun-20	9 11-1100: FS, 53-4200: FS, 63-1000: FS, 53-4300: F 53-2800: FS, 63-4200: FS	S, 53-3300: FS, 53-3600: FS, 63-2400: FS, 63-2700: FS, M12. 1: FS -50, M12. 2: FS, 63-2000: FS -45, 63-2200: FS
								35-2000.1 3, 05-4200.1 3	1 3 -30, W112. 2.1 3, 03-2000. 1 3 -43, 03-2200. 1 3
522	6.03	5.3	3-2000	Earth bund (Western)	110	25-Apr-	0 12-Aug-20	19 11-1100: FS, 63-1000: FS, 63-1900: FS -45	63-2300: FS, 63-2400: FS, 63-2600: FS, 63-3700: FS, 63-2100: FS -45
523	6.03	3.3	3-2100	Intercell bund (Cell 3/4)	105	29-Jun-	0 11-Oct-20	789 11-1100: FS, 63-1000: FS, 63-4200: FS, 63-2000: F	
524				Site Formation				9 11-1100: FS, 63-1000: FS, 63-1900: FS	63-2300: FS
525				Pump Station (PS#3X) Lining Works				9 63-2200: FS, 63-2000: FS 435 41-1500: FS, 63-1900: FS, 63-2000: FS, 63-2100: F	63-2500: FS, 63-2600: FS S, 63-2500: FS, M12. 3: FS
320	0.03	.5	3-2400	Lilling Works	100	01-Oct-2	00-5 an-22	435 41-1300: F3, 03-1300: F3, 03-2100: F3	3, 03-2300. F3, W12. 3. F3
527				Protective Stone Laying & Leachate Collection Pipe	25	09-Jan-	2 02-Feb-22	435 63-2400: FS, 41-1500: FS, 63-2300: FS	32-1700: FS, M12. 3: FS
528				Install Leachate Force Main				9 63-2000: FS, 41-1500: FS, 63-2300: FS	53-2500: SS -90, 54-2800: FS, M12. 3: FS
529				Install Landfill Gas Pipe on earth bund				58 41-1500: FS, 63-1900: FS	54-4000: FS, M12. 3: FS
530		2. 6.03.4 L a 3.4 6		Remaining Portion of Buttress Wall			1 13-Apr-23 1 04-Jan-22	30 494 62-1000: FS	
532				Earth bund (Western) incl. MSE Wall				239 62-1000: FS	63-3000: FS, 63-3100: FS, 63-3200: FS, 63-3400: FS,
									63-3800: FS, 63-3900: FS, 63-4100: SS -90, M 9. 6: FS -60, M 9. 7: FS -30, M 9. 8: FS
									·
533	6.03	.4 f	3-3000	Site Formation	120	05-Jan-	2 04-May-22	239 62-1000: FS, 62-1100: FS, 62-1200: FS, 63-2900: F 63-4100: FS	S, 63-3100: FS
534	6.03	3.4	3-3100	Pump Station (PS#4X)	45	05-May-	2 18-Jun-22	239 63-3000: FS, 63-2900: FS	63-3300: FS, 63-3400: FS
535	6.03	3.4	3-3200	Lining Works	135	01-Oct-2	12-Feb-23	0 41-1500: FS, 63-2900: FS	63-3300: FS, M12. 6: FS
536	6.03	3.4	3-3300	Protective Stone Laying & Leachate Collection Pipe	60	13-Feb-	3 13-Apr-23	0 41-1500: FS, 63-3200: FS, 63-3100: FS	12-1900: FS, 32-1800: FS, M12. 6: FS
537	6.03	3.4	3-3400	Install Leachate Force Main & Remove Temporary Leachate Pipe	30	19-Jun-	2 18-Jul-22	269 41-1500: FS, 63-2900: FS, 63-3100: FS	12-1900: FS, 32-1800: FS, M12. 6: FS
538				Surface Run-Off			0 03-Feb-22		10.1000 =0
539				Perimeter Channel (X9A) at Cell 2 Western Bund Perimeter Channel (X10A) at Cell 2 Western Bund				1054 63-1100: FS 1029 63-1100: FS	12-1900: FS 63-4000: FS
540				Perimeter Channel (X10A) at Cell 2 Western Bund Perimeter Channel (X10A) at Cell 3 Western Bund				964 63-2000: FS	63-4000: FS
542				Perimeter Channel (X10A) at Cell 3 Western Bund				464 63-2900: FS	63-4000: FS
543				Perimeter Channel (X10C) at Cell 4 Western Bund				469 63-2900: FS	63-4000: FS
544				Connection to Existing DP3				464 63-3900: FS, 63-3600: FS, 63-3700: FS, 63-3800: F	
545				Remove Cut-Off Channel C-7 at bottom of Buttress Wall				419 63-2900: SS -90	63-3000: FS
546				Temporary Channel (X7T) at SENT Infrastructure Area				14 63-1300: FS	63-1900: FS, 63-2100: FS
548				Ground Water Construct Temporary Channel (TC-1), from MH-1 to Existing UC-825			1 30-Nov-21 1 26-Oct-21	529 23-1900: FS, 11-1300: FS, 62-1000: FS	63-4400: FS
549				Divert GW at MH-1 to TC-1	5	27-Oct-	1 31-Oct-21	529 63-4300: FS	63-4500: FS, M 9. 9: FS
550	6.03	3.6	3-4500	Reconnection of GWCP across Cell 4	30	01-Nov-	1 30-Nov-21	529 62-1100: FS, 62-1200: FS, 63-4400: FS	12-1900: FS
551				Vorks Associated with Utilities Undertakers			0 27-Jul-21		
552 553		2.6.03.8.U 03.8.U1 6		LFG Generator On-grid Testing			0 27-Jul-21 0 27-Jun-21	655 32-2500: FS, 12-1200: FS, 54-4000: FS	63-4700: FS
554				LFG Generator On-grid Inspection & Verify				655 63.4600: FS	12-1900: FS
555	SA2	2.6.03.8.U	6 Town	<u>Gas</u>	55	15-Nov-	0 08-Jan-21	855	
556	6.03	03.8.U6 6	3-4800	Laying Gas Mains (from LFG to Town Gas PF)	45	15-Nov-	0 29-Dec-20	855 54-4000: FF	63-4900: FS
557				Gas Meter Relocation & Connection at LFG				855 63-4800: FS, 54-4000: FS	12-1900: FS
558 559		<mark>.6.04 Bui</mark> .6.04.C P	_	E&M Works ea C			9 22-Jul-21 9 22-Jul-21		
560				ea C reatment Plant			9 22-Jul-21 9 22-Jul-21		
561	6.04	04.C.02	4-1000	GHS600 Blower 601 C Relocation	15	08-Jul-	1 22-Jul-21	660 32-1500: FS	12-1900: FS
562	6.04	14 0 00	4-1100	Absorption Chiller (Optional)				1231 54-2200: FS	12-1900: FS
563							9 03-Dec-20 9 26-Nov-19		
EC4		. <mark>6.08 Lar</mark>	<mark>dscape</mark>	- Iron Mamovel & Ironomianting	240			1264 1264 14-1300: FS	68-1100: FS, 68-1200: FS, 68-1400: FS
564 565	SA2.0	<mark>.6.08 Lar</mark> .6.08.1 SI	<mark>dscape</mark> NT Area	- Tree Removal & Transplanting Access trees condition and select for transplanting		U1-Apr-1	30-ADI-19		
564 565 566	SA2. 0	.6.08 Lar .6.08.1 St	dscape NT Area 8-1000	Access trees condition and select for transplanting Prepare new site to receive trees	30			1264 68-1000: FS	68-1200: SS
564 565 566 567	SA2.0 6.08 6.08	.6.08 Lar 2.6.08.1 SE 8.1 6	dscape NT Area 8-1000 8-1100	Access trees condition and select for transplanting	30 90	01-May-	9 29-Jul-19		68-1200: SS 68-1300: FS
564 565 566 567 568	6.08 6.08 6.08	.6.08 Lar 2.6.08.1 SE 8.1 6 8.1 6	dscape NT Area 8-1000 8-1100 8-1200	Access trees condition and select for transplanting Prepare new site to receive trees	30 90 120	01-May- 01-May-	9 29-Jul-19 9 28-Aug-19	1264 68-1000: FS	
564 565 566 567 568 569	\$A2.0 6.08 6.08 6.08 6.08	8.1 68.1 68.1 68.1 68.1 68.1 68.1 68.1 6	dscape 8-1000 8-1100 8-1200 8-1300 8-1400	Access trees condition and select for transplanting Prepare new site to receive trees Transplant selected trees Prune trees prior to removal from Cell 4 Tree Felling - Part X3	30 90 120 90 90	01-May- 01-May- 29-Aug- 01-May-	9 29-Jul-19 9 28-Aug-19 9 26-Nov-19 9 29-Jul-19	1264 68-1000: FS 1264 68-1000: FS, 68-1100: SS 1264 68-1200: FS 1384 23-8200: FS, 31-1600: FS, 68-1000: FS	68-1300: FS
564 565 566 567 568 569 570	\$A2.0 6.08 6.08 6.08 6.08 \$A2.0	.6.08 Lar .6.08.1 Si 8.1 6 8.1 6 8.1 6 8.1 6	ciscape ENT Area 8-1000 8-1100 8-1200 8-1300 8-1400 ENTX Area	Access trees condition and select for transplanting Prepare new site to receive trees Transplant selected trees Prune trees prior to removal from Cell 4 Tree Felling - Part X3 sa - Trial Nursery & Tree Planting	30 90 120 90 90 583	01-May- 01-May- 29-Aug- 01-May-	9 29-Jul-19 9 28-Aug-19 9 26-Nov-19 9 29-Jul-19 9 03-Dec-20	1264 68-1000: FS 1264 68-1000: FS, 68-1100: SS 1264 68-1200: FS 1384 23-8200: FS, 31-1600: FS, 68-1000: FS	68-1300: FS 12-1900: FS 12-1900: FS
564 565 566 567 568 569 570 571	\$A2.0 6.08 6.08 6.08 6.08 \$A2.0		ciscape ent Area 8-1000 8-1100 8-1200 8-1300 8-1400 ent Area 8-1600	Access trees condition and select for transplanting Prepare new site to receive trees Transplant selected trees Prune trees prior to removal from Cell 4 Tree Felling - Part X3	30 90 120 90 90 90 583 300	01-May- 01-May- 29-Aug- 01-May- 01-May- 01-May-	9 29-Jul-19 9 28-Aug-19 9 26-Nov-19 9 29-Jul-19 9 03-Dec-20 9 24-Feb-20	1264 68-1000: FS 1264 68-1000: FS, 68-1100: SS 1264 68-1200: FS 1384 23-8200: FS, 31-1600: FS, 68-1000: FS	68-1300: FS 12-1900: FS

Annex B

Environmental Mitigation Implementation Schedule

Annex B Environmental Mitigation Implementation Schedule

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the m	to impleeasure?	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
Air Quali	ty - Cons	truction Phase							
4.8.1	AQ1	Blasting	To minimise potential	Blasting area	SENTX	,	/	Air Pollution Control	Not applicable.
		• The area within 30m of the blasting area will be wetted prior to blasting.		and 30m of blasting area	Contractor			(Construction Dust) Regulations	Blasting is not required in the latest landfill design
		 Blasting will not be carried out when the strong wind signal or tropical cyclone warning signal No. 3 or higher is hoisted, unless this is with the express prior permission of the Commissioner of Mines. 							
		 loose material and stones in the Site will be removed prior to the blast operation 							
		 During blasting, blast nets, screens and other protective covers will be used to prevent the projection of flying fragments and material resulting from blasting 							
4.8.1	AQ2	Rock Drilling	To minimise potential	Ŭ	_	Air Pollution Control	Not applicable. Rock		
		 Watering will be carried out at the rock drilling activities to avoid fugitive dust emissions. 	dust nuisance	area				(Construction Dust) Regulations	drilling is not required in the latest landfill design
(1) D=Desig	gn; C=Const	ruction; O/R=Operation/Restoration; A=Aftercare							

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	•		When to implement the measure? (1)			What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R A	measure to achieve?	
4.8.1	AQ3	Site Access Road	To minimise potential		SENTX		✓		Air Pollution Control	Deficiency of
		The main haul road will be kept clear of dusty materials or sprayed with	dust nuisance	road	Contractor				(Construction Dust) Regulations	mitigation measures but rectified by the Contractor
		water.The main haul road will be paved							HKAQO and EIAO- TM Annex 4	
		with aggregate or gravel.							TWITTING T	
		• Vehicle speed will be limited to 10kph.								
4.8.1	AQ4	Stockpiling of Dusty Materials		All construction works area	SENTX Contractor		✓		Air Pollution Control	Deficiency of
		Any stockpile of dusty materials will be covered entirely by impervious							(Construction Dust) Regulations	mitigation measures but rectified by the Contractor
		sheeting or placed in an area sheltered on the top and three sides or sprayed with water so as to ensure that the entire surface is wet.							HKAQO and EIAO- TM Annex 4	
4.8.1	AQ5	Loading, unloading or transfer of dusty materials	To minimise potential dust nuisance	All construction works area	SENTX Contractor		✓		Air Pollution Control (Construction Dust)	Implemented
		All dusty materials will be sprayed							Regulations	
		with water immediately prior to any loading, unloading or transfer operation so as to maintain the dusty material wet.							HKAQO and EIAO- TM Annex 4	
4.8.1	AQ6	Site Boundary and Entrance	To minimise potential dust nuisance	-	SENTX		✓		Air Pollution Control	Not applicable
		 Where a site boundary adjoins a road, street, service lane or other area accessible to the public, hoarding of height not less than 2.4m from 		and entrance	Contractor				(Construction Dust) Regulations	
									HKAQO and EIAO-	

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main	Location of the Measures	Who to implement the measure?		implem sure? ⁽¹⁾ O/R	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		ground level will be provided along the entire length of that portion of the site boundary except for the site entrance or exit.	Concerns to address					TM Annex 4	
4.8.1	AQ7	 Excavation Works Working area of any excavation or earth moving operation will be sprayed with water immediately before, during and immediately after the operation so as to ensure that the entire surface is wet. 	To minimise potential dust nuisance	All construction works area	SENTX Contractor	√		Air Pollution Control (Construction Dust) Regulations HKAQO and EIAO- TM Annex 4	Deficiency of mitigation measures but rectified by the Contractor
4.8.1	AQ8	 Building Demolition The area where the demolition works are planned to take place will be sprayed with water immediately prior to, during and immediately after the demolition activities. Any dusty materials remaining after a stockpile is removed will be wetted 	To minimise potential dust nuisance	All construction works area	SENTX Contractor	✓		Air Pollution Control (Construction Dust) Regulations HKAQO and EIAO- TM Annex 4	Not applicable
4.8.1	AQ9	 a stockpile is removed will be wetted with water and cleared from the surface of roads or street. Construction of the Superstructure of Building Effective dust screens, sheeting or netting will be provided to enclose the scaffolding from the ground level up to the highest level of the scaffolding. 	To minimise potential dust nuisance	All construction works area	SENTX Contractor	✓		Air Pollution Control (Construction Dust) Regulations HKAQO and EIAO- TM Annex 4	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement	the	meas	implei ure? ⁽¹⁾		What requirements or standards for the	the Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R	A	measure to achieve?	
4.8.1	AQ10	Should a stone crushing plant be needed on site, the control measures recommended in the Best Practicable Means Requirement for Mineral Works (Stone Crushing Plants) BPM 11/1 should be implemented.	To minimise potential dust nuisance	Stone crushing plant/ construction phase	SENTX Contractor		✓			Best Practicable Means Requirement for Mineral Works (Stone Crushing Plants) BPM 11/1	Not applicable. Stone crushing plant is not required in the latest landfill design
4.8.1	AQ11	Good site practices such as regular maintenance and checking of the diesel powered mechanical equipment will be adopted to avoid any black smoke emissions and to minimize gaseous emissions.	To minimise potential dust nuisance	All construction works area	SENTX Contractor		✓			HKAQO and EIAO- TM Annex 4	Implemented
4.10.1	AQ12	Dust monitoring once every 6 days	Ensure the dust generated from the project meets the air quality requirement	At monitoring locations shown in <i>Figure 3.2a</i>	SENTX Contractor		✓			HKAQO and EIAO- TM Annex 4	Implemented
4.10.2	AQ41	Monitoring of ambient TSP once every 6 days	Ensure the dust emission from the project meets the dust requirement	At monitoring locations shown in Figure 11.3a	SENTX Contractor		✓	✓		HKAQO and EIAO- TM Annex 4	Implemented
4.10.2	AQ46	Monitoring of meteorological station, continuously	Collect site specific meteorological data	At meteorologica l station shown in Figure 11.3a	SENTX Contractor		✓	✓	✓	-	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	the		impler sure? ⁽¹⁾ O/R	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
5.7.1	N1	Adopt good site practice listed below: Only well-maintained plant will be operated on-site and plant should be serviced regularly during the construction program;	To minimise potential construction noise nuisance.	All construction works area	SENTX Contractor		✓		Noise Control Ordinance (NCO) and EIAO-TM Annex 5	Implemented
		• Silencers or mufflers on construction equipment should be utilized and will be properly maintained during the construction program;								
		• Mobile plant, if any, will be sited as far from NSRs as possible;								
		Machines and plant (such as trucks) that may be in intermittent use will be shut down between work periods or should be throttled down to a minimum;								
		Plant known to emit noise strongly in one direction will, wherever possible, be orientated so that the noise is directed away from the nearby NSRs; and								
		 Material stockpiles and other structures will be effectively utilised, wherever practicable, in screening noise from on-site construction activities. 								

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement			implement	What requirements or standards for the	Implementation Status and Remarks
	Kei	witigation weasures	Measure & Main Concerns to address	the weasures	the measure?	D	С	O/R A	measure to achieve?	Status and Remarks
5.8	N2	Weekly noise monitoring	Ensure noise generated from the project meets the criteria	At monitoring locations shown in Figure 6.4a	SENTX Contractor		✓		Noise Control Ordinance (NCO) and EIAO-TM Annex 5	Implemented
Water Qu	ality - Co	onstruction Phase								
6.8.1	WQ1	Construction Runoff								
		• Exposed soil areas will be minimised	To minimise potential		SENTX		✓		ProPECC PN 1/94	Implemented
		to reduce the contamination of runoff and erosion.	water quality impacts arising from the construction works	construction works area	Contractor				EIAO-TM Annex 6	
6.8.1	WQ2	Perimeter channels will be	To minimise potential		SENTX	✓	✓		ProPECC PN 1/94	Deficiency of
		constructed in advance of site formation works and earthworks and intercepting channels will be provided	water quality impacts arising from the construction works	construction works area	Contractor				Water Pollution Control Ordinance (WPCO)	mitigation measures but rectified by the Contractor
		for example along the edge of excavation.							EIAO-TM Annex 6	
6.8.1	WQ3	Silt removal facilities, channels and	To minimise potential	All	SENTX		✓		ProPECC PN 1/94	Deficiency of
		manholes will be maintained and the deposited silt and grit should be	water quality impacts arising from the	construction works area	Contractor				WPCO	mitigation measures but rectified by the
		removed regularly to ensure they are functioning properly at all times.	construction works	WOIKS area					EIAO-TM Annex 6	Contractor
6.8.1	WQ4	Temporary covers such as tarpaulin	To minimise potential		SENTX		✓		ProPECC PN 1/94	Implemented
		will also be provided to minimise the generation of high SS runoff.	water quality impacts arising from the construction works	construction works area	Contractor				WPCO	
6.8.1	WQ5	The surface runoff contained any oil	To minimise potential	All	SENTX		✓		ProPECC PN 1/94	Not applicable

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement			impler ure? ⁽¹⁾	What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R	measure to achieve?	
		and grease will pass through the oil interceptors.	water quality impacts arising from the	construction works area	Contractor				WPCO	
		miercepiors.	construction works	works area					EIAO-TM Annex 6	
6.8.1	WQ6	• All sewer and drains will be sealed to	To minimise potential		SENTX		✓		ProPECC PN 1/94	Not applicable
		prevent building debris, soil etc from entering public sewers/drains before	water quality impacts arising from the	area at existing SENT	Contractor				WPCO	
		commencing any demolition works	demolition works	Landfill					EIAO-TM Annex 6	
6.8.1	WQ7	During the excavation works for the	To minimise potential	Tunnel boring			✓		ProPECC PN 1/94	Not applicable.
		twin drainage tunnels, the recycle water for cooling the cutter head of	water quality impacts arising from the	sites	Contractor				WPCO	Excavation of drainage tunnels is not required
		the TBM will be conveyed to the sedimentation tanks for treatment and most of the treated water will be reused, where applicable and as much as possible, in the boring operations.	tunnel works						EIAO-TM Annex 6	in the latest landfill design.
6.8.1	WQ8	• The fuel and waste lubricant oil from	To minimise potential	SENTX Site	SENTX		✓		ProPECC PN 1/94	Implemented
		the on-site maintenance of machinery and equipment will be collected by a	water quality impacts arising from improper		Contractor				WPCO	
		licensed chemical waste collector.	handling of fuel and oil						Waste Disposal Ordinance (WDO)	
6.8.1	WQ9	Implementation of excavation	To minimise	All	SENTX		✓		ProPECC PN 1/94	Implemented
		schedules, lining and covering of excavated stockpiles	contaminated stormwater run-off	construction works	Contractor				WPCO	
		excavated stockpiles	from the SENTX Site	WOIRS					EIAO-TM Annex 6	
6.13	WQ10	Monitoring of surface water quality	To minimise potential	SENTX Site	SENTX		✓		WPCO	Implemented
		will be conducted on a regular basis as stated in the EM&A Manual.	water quality impacts on surface water arising from the construction works		Contractor				Water-TM	

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main	Location of the Measures	Who to implement the measure?			implement ure? (1) O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
			Concerns to address							
6.8.2	WQ11	Sewage Effluents								
		• Sufficient chemical toilets will be provided for the construction workforce.	To minimise potential water quality impacts arising from the sewage effluents	SENTX Site	SENTX Contractor		✓		WPCO	Implemented
6.8.2	WQ12	• Untreated sewage will not be allowed	To minimise potential	SENTX Site	SENTX		✓		WPCO	Implemented
		to discharge into the surrounding water body.	water quality impacts arising from the sewage effluents		Contractor				WDO	
6.8.2	WQ13	A licensed waste collector will be	To minimise potential	SENTX Site	SENTX		✓		WPCO	Implemented
		employed to clean the chemical toilets on a regular basis.	water quality impacts arising from the sewage effluents		Contractor				WDO	
Waste Ma	nagement	t - Construction Phase								
7.6.1	WM1	All the necessary waste disposal permits are obtained prior to the commencement of construction work.	To ensure compliance with relevant statutory requirements	Before construction works commence	SENTX Contractor	✓	✓		WDO	Implemented
7.6.1	WM2	Management of Waste Disposal								
		The construction contractor will open a	To ensure that	SENTX Site	SENTX		✓		WDO	Implemented
		billing account with the EPD. Every construction waste or public fill load to be transferred to the Government waste disposal facilities such as public fill reception facilities, sorting facilities,	adverse environmental impacts are prevented		Contractor				Waste Disposal (Charges for Disposal of Construction Waste) Regulation;	
		landfills will required a valid "chit" which contains the information of the account holder to facilitate waste							Works Bureau Technical Circular No.31/2004; and	

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?	When to the mea D C	o implement sure? (1) O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		transaction recording and billing to the waste producer. A trip-ticket system will also be established to monitor the disposal of construction waste at the SENT Landfill and to control fly-tipping. The trip-ticket system will be included as one of the contractual requirements and implemented by the contractor.						Annex 5 and Annex 6 of Appendix G of ETWBTC No. 19/2005)	
		A recording system for the amount of waste generated, recycled and disposed of (including the disposal sites) will be established.							
7.6.1	WM3	Measures for the Reduction of Construction Waste Generation							
		Inert and non-inert construction waste will be segregated and stored in different containers or skips to facilitate reuse or recycling of the inert waste and proper disposal of the non-inert construction waste. Specific areas of the work site will be designated for such segregation and storage if immediate use is not practicable.	To reduce construction waste generation	SENTX Site	SENTX Contractor	√		WDO EIAO-TM Annex 7	Deficiency of mitigation measures but rectified by the Contractor
7.6.1	WM4	Chemical Waste The construction contractor will register as a chemical waste producer with the EPD. Chemical waste will be handled in accordance with the Code of Practice on the Packaging, Handling and Storage of	To ensure proper handling of chemical waste	SENTX Site	SENTX Contractor	✓		WDO Code of Practice on the Packaging, Handling and Storage of Chemical Wastes	Deficiency of mitigation measures but rectified by the Contractor

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main Concerns to address	Location of the Measures	Who to implement the measure?		implement ure? ⁽¹⁾ O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		Chemical Wastes.							
7.6.1	WM5	<u>Sewage</u>							
		An adequate number of portable toilets will be provided at the site to ensure that sewage from site staff is properly collected. The portable toilets will be desludged and maintained regularly by a specialist contractor.	To ensure proper handling of sewage	SENTX Site	SENTX Contractor	✓		WDO EIAO-TM Annex 7	Implemented
7.6.1 and	WM6	General Refuse							
SENTX latest design		General refuse will be stored in enclosed bins separately from construction and chemical wastes. The general refuse will be delivered to a transfer station or other landfill, separately from construction and chemical wastes, on a daily basis to reduce odour, pest and litter impacts.	To ensure proper handling of general refuse	SENTX Site	SENTX Contractor	√		WDO EIAO-TM Annex 7	Deficiency of mitigation measures but rectified by the Contractor
		Recycling bins will be provided at strategic locations to facilitate recovery of aluminium can and waste paper from the SENTX Site. Materials recovered will be sold for recycling.							
7.6.1	WM7	Staff Training							
		At the commencement of the construction works, training will be provided to workers on the concepts of site cleanliness and on appropriate waste management procedures, including	To ensure that adverse environmental impacts are prevented	SENTX Site	SENTX Contractor	✓			Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement			implement ure? ⁽¹⁾	What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R A	measure to achieve?	
		waste reduction, reuse and recycling.								
7.8	WM8	Environmental Monitoring & Audit Requirements	To ensure that	SENTX Site	SENTX		√		WDO	Implemented
		Weekly audits of the waste management practices will be carried out during the construction phase. The audits examine all aspects of waste management including waste generation, storage, recycling, transport and disposal.	adverse environmental impacts are prevented		Contractor					
Landfill G	Gas Hazar	ds - Design and Construction Phase								
8.6.2 and SENTX latest design	LFG1	Precautionary measures to be adopted by the contractors at the Project site and the adjacent development site within the landfill consultation zone are outlined in Paragraphs 8.3 to 8.49 of EPD's Landfill Gas Hazard Assessment Guidance Notes (the Guidance Note). Those precautionary measures applicable to the SENTX will be confirmed in the detailed Qualitative Landfill Gas Hazard Assessment to be	-	All construction works area	SENTX Contractor		√		Paragraphs 8.3 to 8.49 of EPD's Landfill Gas Hazards Assessment Guidance Note EIAO-TM Annex 7	Implemented
8.6.2	LFG2	submitted by the contractor. Monitoring will be undertaken when construction works are carried out in confined space within the consultation zone with reference to the monitoring requirements and procedures specified in Paragraphs 8.23 to 8.28 of EPD's <i>Guidance Note</i> will be followed.	To protect workers from landfill gas risk	Confined space within the construction works area	SENTX Contractor		✓			Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement			imple:		What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address	11204 04100	the measure?			O/R		measure to achieve?	0.11.1 0 1.11.1
		In the event of the trigger levels being exceeded, it is recommended that a person, such as the Safety Officer, is nominated, with deputies, to be responsible for dealing with any emergency which may occur due to landfill gas. In an emergency situation, the nominated person, or his deputies, shall have the necessary authority and shall ensure that the confined space is evacuated and the necessary works implemented for reducing the concentrations of gas. The appropriate organisations shall be contact.									
8.6.3	LFG4	Implementation of engineering measures according to Contract Specification requirements. These measures will include the placement of liner and installation of landfill gas management system to contain, manage and control landfill gas.	To protect workers from landfill gas risk	SENTX Site	SENTX Contractor	√	✓	√	√	EIAO-TM Annex 7	Implemented
8.6.3	LFG5	Engineering measures to significant engineering measures will be required in the design of the SENTX to protect the staff working in the infrastructure area. These measures include a combination of passive and active systems (examples are recommended in EPD's <i>Guidance Notes</i>). Landfill gas monitoring boreholes will be installed at the edge of the waste slope	· ·	Infrastructure Area	SENTX Contractor	✓	✓			EPD's Landfill Gas Hazards Assessment Guidance Note EIAO-TM Annex 7	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement	When the m		-	What requirements or standards for the	Implementation Status and Remarks
	Kei	witigation weasures	Measure & Main Concerns to address	the Weasures	the measure?			O/R A	measure to achieve?	Status and Remarks
		between the waste and the new infrastructure area to monitor the migration of landfill gas, if any.								
Ecology -	Construc	tion Phase								
9.10.2	EC1	Measures to control construction runoff:	To minimise potential		SENTX	,	/		EIAO-TM Annex 16	Implemented
		• Exposed soil areas will be	water quality impacts affecting ecological	construction works area	Contractor				ProPECC PN 1/94	
		minimised to reduce the contamination of runoff and erosion;	resources						Water Pollution Control Ordinance (WPCO)	
									EIAO-TM Annex 6	
		 To prevent stormwater runoff from washing across exposed soil surfaces, perimeter channels will be constructed in advance of site formation works and earthworks and intercepting channels will be provided for example along the edge of excavation; 							-	Deficiency of mitigation measures but rectified by the Contractor
		 Silt removal facilities, channels and manholes will be maintained and the deposited silt and grit will be removed regularly to ensure they are functioning properly at all times; 							-	Deficiency of mitigation measures but rectified by the Contractor
		 Temporary covers such as tarpaulin will also be provided to minimise the generation of high suspended solids runoff; 							-	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement		mplei ire? (1)		What requirements or standards for the	Implementation Status and Remarks
	KCI	Miligation Measures	Measure & Main Concerns to address	the weasures	the measure?		O/R		measure to achieve?	Status and Remarks
		 The surface runoff contained any oil and grease will pass through the oil interceptors; and, 							-	Not applicable
		 Control measures, including implementation of excavation schedules, lining and covering of excavated stockpiles will be implemented to minimise contaminated stormwater run-off from the SENTX site. 							-	Implemented
9.10.2 and	EC2	Good Construction Practice:								
SENTX latest design		 Fences along the boundary of the SENTX Site will be erected before the commencement of works to prevent vehicle movements, and encroachment of personnel, onto adjacent areas. 	To minimise potential ecological impacts arising from the Project	SENTX Site	SENTX Contractor	√			EIAO-TM Annex 16	Implemented
		 The work site boundaries will be regularly checked to ensure that they are not breached and that damage does not occur to surrounding areas. 								
9.12.1	EC9	Environmental Monitoring & Audit Requirements						,		
		The implementation of the ecological mitigation measures should be checked as part of the environmental monitoring and audit procedures during the	To ensure that adverse ecological impacts are prevented	SENTX	SENTX Contractor	√	√	√	EIAO-TM Annex 16	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended Measure & Main	Location of the Measures	Who to implement the measure?			implement sure? (1) O/R A	What requirements or standards for the measure to achieve?	Implementation Status and Remarks
		construction period.	Concerns to address							
Landscape	and Visu	al - Construction Phase								
10.6.5	LV1	CM1 - The construction area and area allowed for the contractor's office, leachate treatment plant and laboratory areas will be minimised to a practical minimum, to avoid impacts on adjacent landscape.	To minimise the landscape and visual impacts	SENTX Site	SENTX Contractor		✓		EIAO-TM Annex 18 and ETWBC 3/2006	Implemented
10.6.5	LV2	CM2 - Topsoil, where identified, will be stripped and stored for re-use in the construction of the soft landscape works, where practical. The Contract Specification will include storage and reuse of topsoil as appropriate.	To minimise the landscape and visual impacts	All construction works area	SENTX Contractor		✓		EIAO-TM Annex 18	Not applicable
10.6.5	LV3	CM3 - All existing trees at the edges of the landfill will be carefully protected during construction. Detailed Tree Protection Specification will be provided in the Contract Specification. Under this Specification, the Contractor will be required to submit, for approval, a detailed working method statement for the protection of trees prior to undertaking any works adjacent to all retained trees, including trees in Contractor's works areas.	To minimise the landscape and visual impacts	Potential impacted area	SENTX Contractor		✓		EIAO-TM Annex 18 and ETWBC 3/2006	Not applicable
10.6.5	LV4	CM4 - Trees unavoidably affected by the works will be transplanted, where necessary and practical. A detailed Tree	landscape and visual	Potential impacted area	SENTX Contractor	✓	✓		EIAO-TM Annex 18 and ETWBC 3/2006	Implemented

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement			implement sure? (1)	What requirements or standards for the	Implementation Status and Remarks
		o .	Measure & Main Concerns to address		the measure?	D	С	O/R A	measure to achieve?	
		Transplanting Specification will be provided in the Contract Specification, if applicable. Sufficient time for necessary tree root and crown preparation periods will be allowed in the project programme.								
10.6.5 and SENTX latest design	LV5	CM5 - Within 3 months of taking possession of the SENTX Site, the Contractor will plant advance screen planting of native species at Light Standard size at 1.5m centres along the High Junk Peak Trail so as to screen views of the Works from the trail. Tree planting locations will be agreed with AFCD. Works will be completed within 9 months of taking possession of the SENTX Site.	To minimise the landscape and visual impacts	At High Junk Peak Hiking Trail	SENTX Contractor		✓		EIAO-TM Annex 18	Implemented
10.6.5	LV6	CM6 - The Contractor's office, leachate treatment plant and laboratory will be given an aesthetic treatment in earth tones to reduce their visual impact and albedo and blend them into the surrounding landscape.	To minimise the landscape and visual impacts	Infrastructure area	SENTX Contractor	✓	✓		EIAO-TM Annex 18	Implemented
10.6.5	LV7	CM7 - The Contractor's office, leachate treatment plant and laboratory will be surrounded by a minimum of 5m wide and 0.75m high earth bund on the west and south sides planted with a dense screen of tree and shrub vegetation. Additional tree planting will be provided in unused spaces with thin infrastructure	To minimise the landscape and visual impacts	Infrastructure area	SENTX Contractor	✓	√		EIAO-TM Annex 18 and ETWBC 7/2002	Not applicable

EIA Ref.	EM&A Ref	Environmental Protection Measures/ Mitigation Measures	Objectives of the Recommended	Location of the Measures	Who to implement			implement ure? ⁽¹⁾	What requirements or standards for the	Implementation Status and Remarks
			Measure & Main Concerns to address		the measure?	D	С	O/R A	measure to achieve?	
		site, along access roads and in and around car parks. This will be supplemented with shrub planting, where appropriate.								
10.6.5	LV8	CM8 - Planting trials will be carried out in an on-site nursery prior to implementation of the first phase of restoration to establish the best planting matrix and management intensity of the recommended plant materials for the restoration.	To minimise the landscape and visual impacts	SENTX Site	SENTX Contractor		✓		EIAO-TM Annex 18	Implemented
11.4.1 and SENTX latest design	LV9	During the preparation of the detailed landscape design plan, the design submission will be audited against the recommendation proposed in the <i>ER Report</i> by the Registered Landscape Architect from the ET.	To ensure the implementation of mitigation measures proposed in this EIA Report	SENTX Site	SENTX Contractor/E T	✓	√		EIAO-TM Annex 18	Implemented

Annex C

Monitoring Schedule for This Reporting Period

South East New Territories (SENT) Landfill Extension EM&A Impact Monitoring Schedule during Construction Phase

January 2021

Sun	Mon	Tue	Wed	Thu	Fri	Sat
					1	2
3	4	5	6	7	8	9
		Dust Monitoring		Surface Water Monitoring (pm)	-	
				Noise Monitoring (pm)		
10	11	12	13	14	15	16
	Dust Monitoring			Surface Water Monitoring (pm)		
				Noise Monitoring (pm)		
17	18	19		21	22	23
Dust Monitoring			Surface Water Monitoring (pm)			Dust Monitoring
			Noise Monitoring (pm)			
24	25	26	27	28	29	30
				Surface Water Monitoring (pm)	Dust Monitoring	
				Noise Monitoring (pm)		
31						

Note

Impact dust monitoring will be conducted at two monitoring stations (DM1 and DM2) under the on-going EM&A programme TKO Area 137 Fill Bank and the results will be shared with SENTX.

South East New Territories (SENT) Landfill Extension EM&A Impact Monitoring Schedule during Construction Phase

February 2021

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3	4	5	6
				Surface Water Monitoring (pm)		
				Noise Monitoring (pm)		
				Dust Monitoring		
7	8	9	10	11	12	13
		Surface Water Monitoring (pm)	Dust Monitoring			
		Noise Monitoring (pm)				
14	15	16	17	18	19	20
		Dust Monitoring	Surface Water Monitoring (pm)			
			Noise Monitoring (pm)			
21	22	23	24	25	26	27
	Dust Monitoring			Surface Water Monitoring (pm)		
				Noise Monitoring (pm)		
28						
Dust Monitoring						

Note

Impact dust monitoring will be conducted at two monitoring stations (DM1 and DM2) under the on-going EM&A programme TKO Area 137 Fill Bank and the results will be shared with SENTX.

South East New Territories (SENT) Landfill Extension EM&A Impact Monitoring Schedule during Construction Phase

March 2021

Sun	Mon	Tue	Wed	Thu	Fri	Sat
	1	2	3	4	5	6
				Surface Water Monitoring (pm)		Dust Monitoring
				Noise Monitoring (pm)		
7	8	9	10	11	12	13
				Surface Water Monitoring (pm)	Dust Monitoring	
				Noise Monitoring (pm)		
14	15	16	17	18	19	20
				Surface Water Monitoring (pm)		
				Noise Monitoring (pm)		
				Dust Monitoring		
21	22	23	24	25	26	27
			Dust Monitoring	Surface Water Monitoring (pm)		
				Noise Monitoring (pm)		
28	29	30	31			
		Dust Monitoring				

Note

Impact dust monitoring will be conducted at two monitoring stations (DM1 and DM2) under the on-going EM&A programme TKO Area 137 Fill Bank and the results will be shared with SENTX.

Air Quality

24-hour TSP Monitoring Results

Table D1.1 24-hour TSP Monitoring Results at DM1

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (μg/m3)
5 Jan 21	8:00	6 Jan 21	8:00	Fine	107
11 Jan 21	11:36	12 Jan 21	11:36	Cloudy	114
17 Jan 21	12:00	18 Jan 21	12:00	Fine	110
23 Jan 21	8:00	24 Jan 21	8:00	Fine	117
29 Jan 21	14:05	30 Jan 21	14:05	Fine	105
4 Feb 21	8:00	5 Feb 21	8:00	Fine	92
10 Feb 21	9:40	11 Feb 21	9:40	Rainy	98
16 Feb 21	11:50	17 Feb 21	11:50	Fine	105
22 Feb 21	12:20	23 Feb 21	12:20	Fine	113
28 Feb 21	12:00	1 Mar 21	12:00	Fine	110
6 Mar 21	8:00	7 Mar 21	8:00	Rainy	100
12 Mar 21	9:55	13 Mar 21	9:55	Fine	111
18 Mar 21	8:00	19 Mar 21	8:00	Fine	90
24 Mar 21	9:04	25 Mar 21	9:04	Fine	104
30 Mar 21	8:30	31 Mar 21	8:30	Fine	115
				Average	106
				Min	90
				Max	117

Note:

DM1 corresponds to the existing TSP monitoring station TKO-A1 currently operating by CEDD.

Figure D1.1 Graphical Presentation for 24-hr TSP Monitoring at DM1

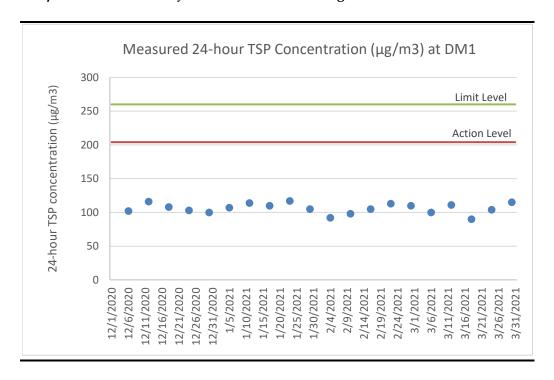



Table D1.2 24-hour TSP Monitoring Results at DM2

Start Date	Start Time	Finish Date	Finish Time	Weather	24-hour TSP (μg/m3)
5 Jan 21	8:00	6 Jan 21	8:00	Fine	95
11 Jan 21	11:30	12 Jan 21	11:30	Cloudy	101
17 Jan 21	12:00	18 Jan 21	12:00	Fine	98
23 Jan 21	8:00	24 Jan 21	8:00	Fine	109
29 Jan 21	14:15	30 Jan 21	14:15	Fine	115
4 Feb 21	8:00	5 Feb 21	8:00	Fine	103
10 Feb 21	9:45	11 Feb 21	9:45	Rainy	89
16 Feb 21	11:34	17 Feb 21	11:34	Fine	97
22 Feb 21	12:25	23 Feb 21	12:25	Fine	102
28 Feb 21	12:00	1 Mar 21	12:00	Fine	100
6 Mar 21	8:00	7 Mar 21	8:00	Rainy	93
12 Mar 21	9:58	13 Mar 21	9:58	Fine	103
18 Mar 21	8:00	19 Mar 21	8:00	Fine	99
24 Mar 21	9:15	25 Mar 21	9:15	Fine	97
30 Mar 21	8:30	31 Mar 21	8:30	Fine	109
				Average	101
				Min	89
				Max	115

Note:

 $\ensuremath{\mathsf{DM2}}$ corresponds to the existing TSP monitoring station TKO-A2a currently operating by CEDD.

Figure D1.2 Graphical Presentation for 24-hr TSP Monitoring at DM2

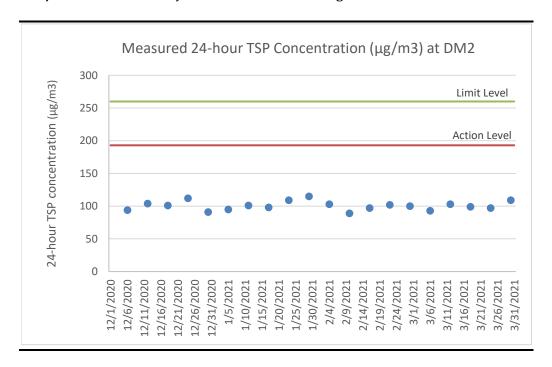

Event and Action Plan for Dust Monitoring

Annex D2 Event and Action Plan for Dust Monitoring During Construction Phase

Action							
Event	ET	IEC	Contractor				
Action Level							
Exceedance for one sample	 Identify the source(s) and investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project Repeat measurement to confirm finding if exceedance is due to the Project Increase monitoring frequency to daily if exceedance is due to the Project and continue until the monitoring results reduce to below action level 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods 	 Rectify any unacceptable practice Amend working methods if appropriate 				
Exceedance for two or more consecutive samples	 Identify the source(s) and investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented If exceedance continues, arrange meeting with Contractor & IEC Continue monitoring at daily intervals if exceedance is due to the Project If no exceedance for 3 consecutive days, cease additional monitoring 	 Check monitoring data submitted by ET 	 Submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate 				

		Action	
Event	ET	IEC	Contractor
Limit Level			
Exceedance for one sample	 Identify the source(s) and investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Repeat measurement to confirm finding if exceedance is due to the Project Increase monitoring frequency to daily if exceedance is due to the Project and continue until the monitoring results reduce to below limit level 	Check monitoring data submitted by ETCheck Contractor's working methods	 Take immediate action to avoid further exceedance Submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate
Exceedance for two or more consecutive samples	 Identify source(s) and investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD the causes & actions taken for the exceedances Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Continue monitoring at daily intervals if exceedance is due to the Project If no exceedance for 3 consecutive days, cease additional monitoring If exceedance due to the Project continues, consider what portion of the work is responsible and stop that portion of work until the exceedance is abated 		 Take immediate action to avoid further exceedance Submit proposals for remedial measures to IEC Implement the agreed proposals Resubmit proposals if problem still not under control


ENVIRONMENTAL RESOURCES MANAGEMENT


GREEN VALLEY LANDFILL LTD.


Meteorological Data


Annex D3 Meteorological Data


January 2021

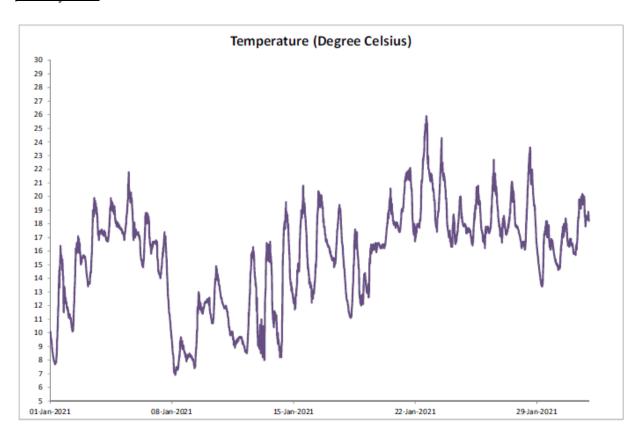


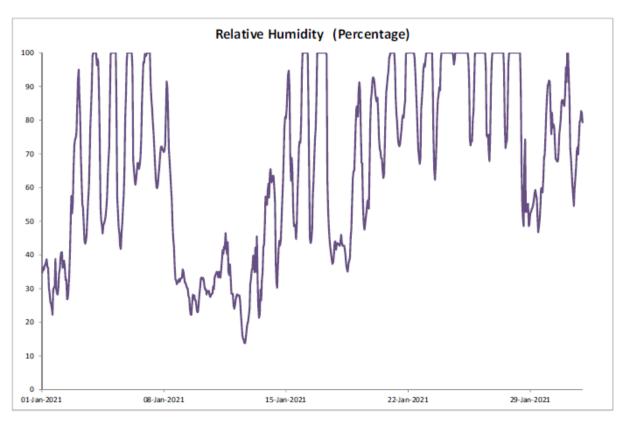


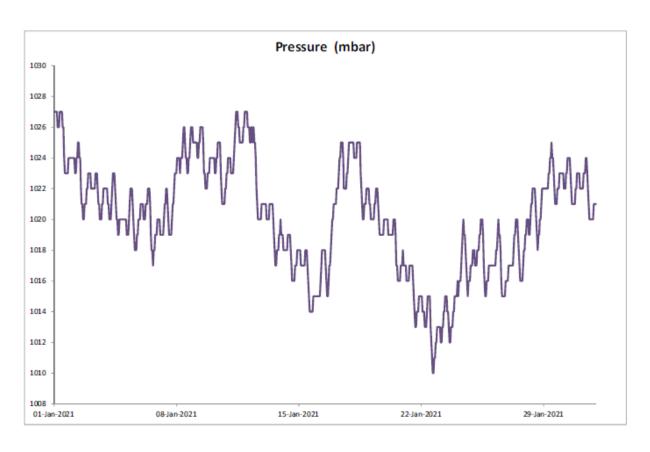

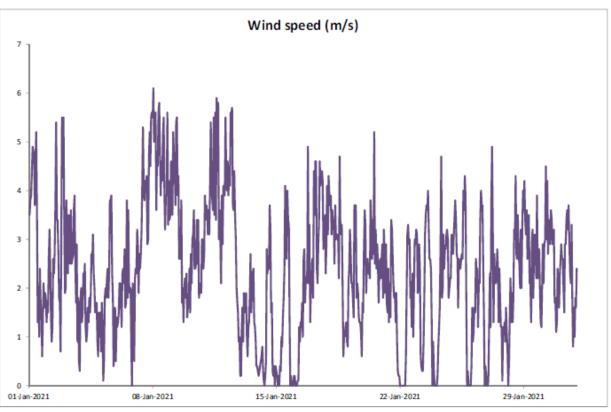


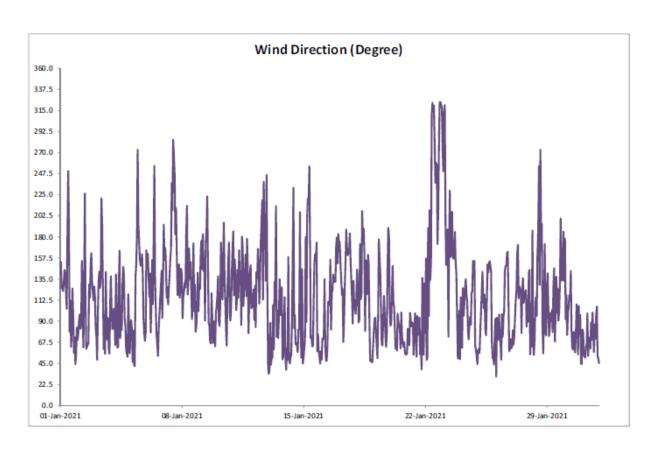


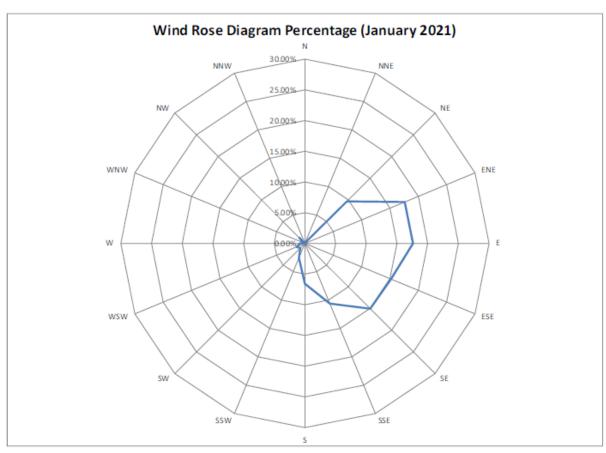


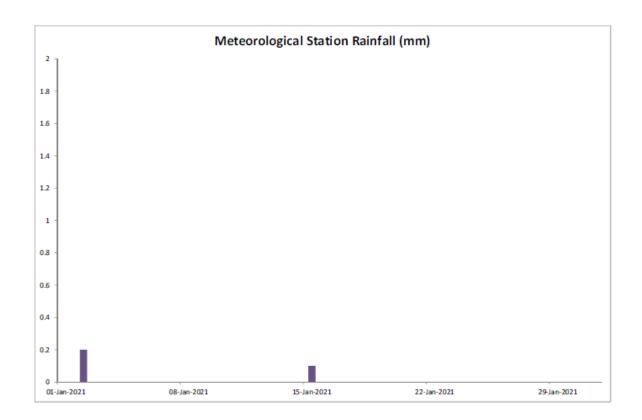



February 2021

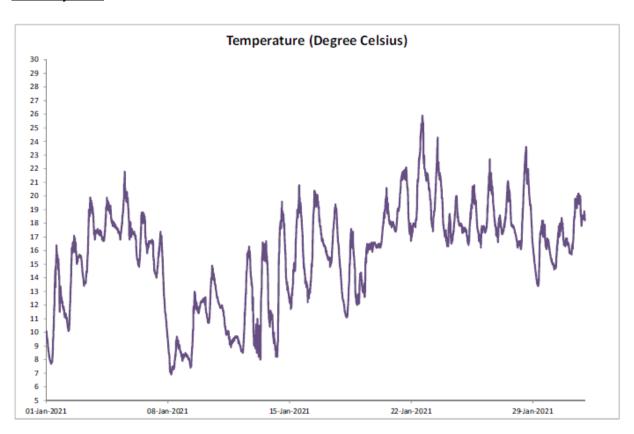


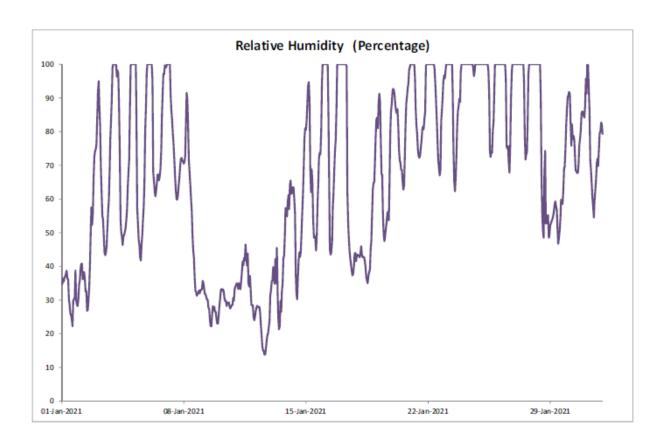


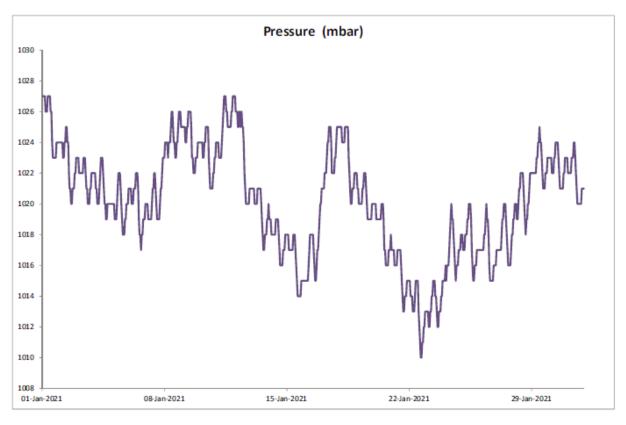


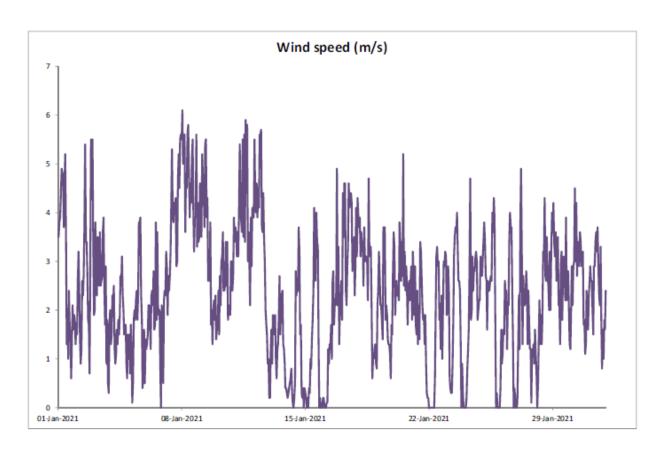


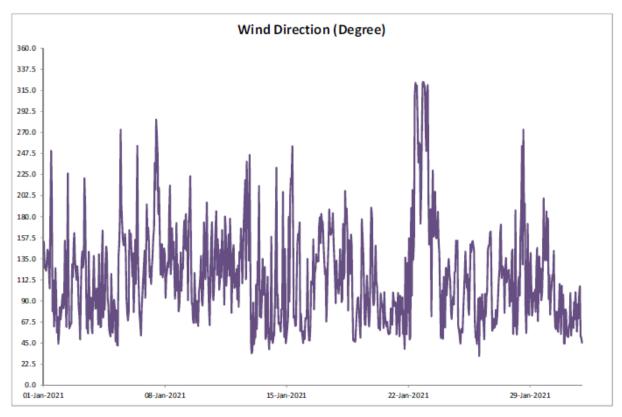


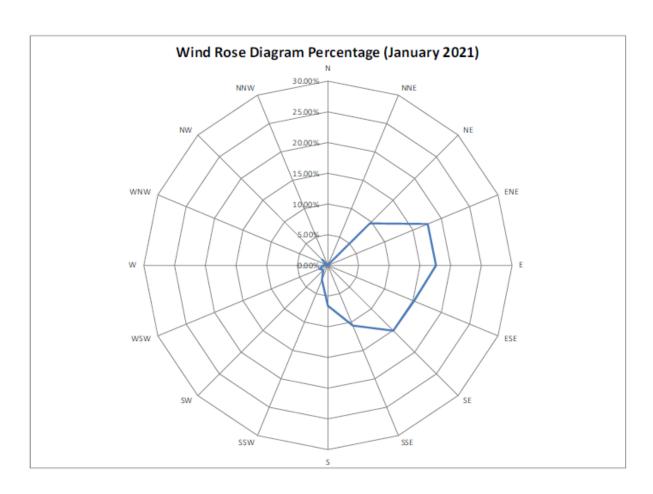


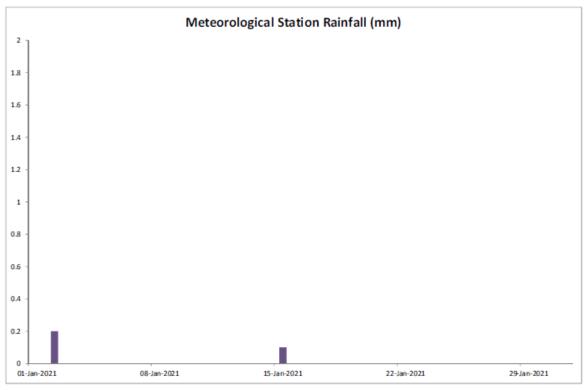


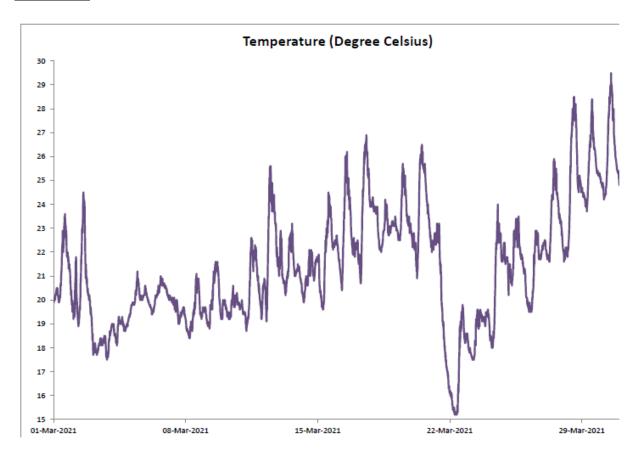


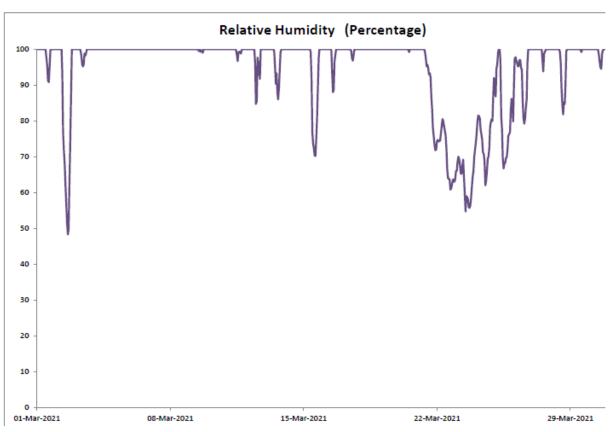


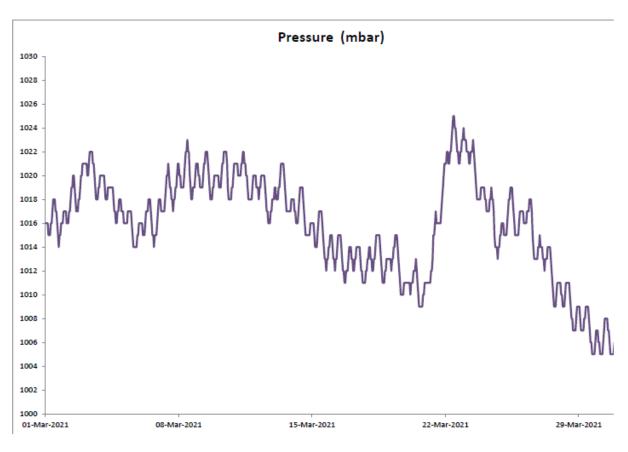

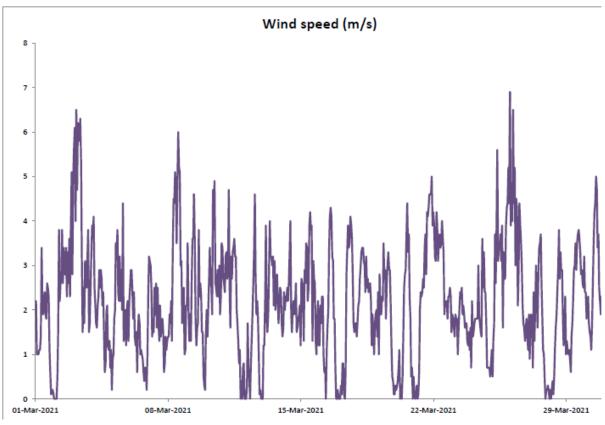

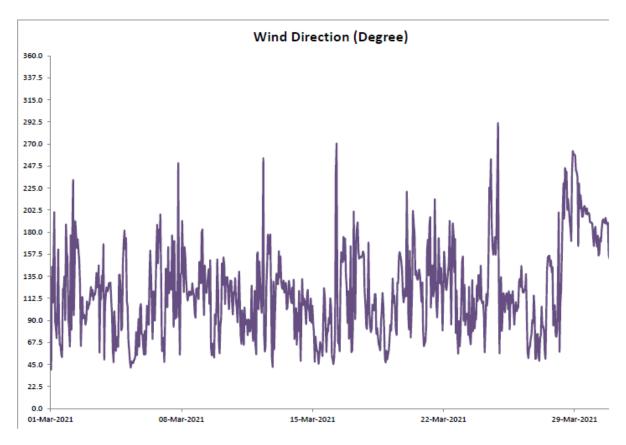

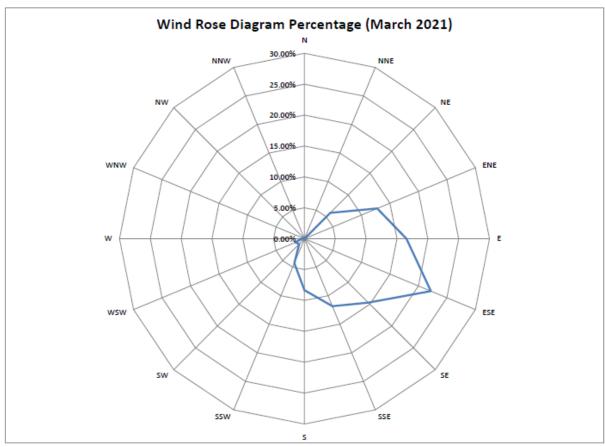

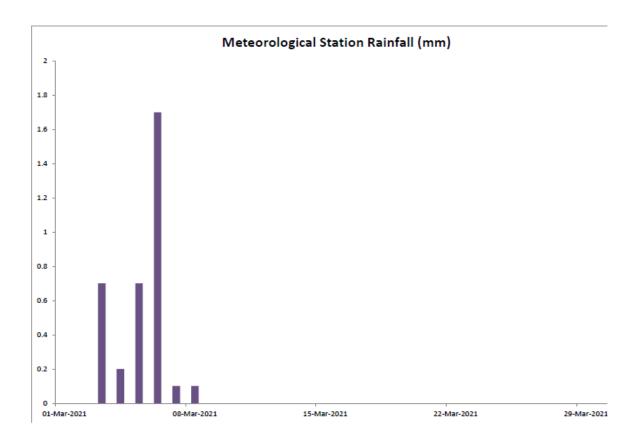

Annex E

Noise

Annex E1

Noise Monitoring Results


Table E1.1 Measured Noise Levels (dB(A)) at NM1 during Normal Working Hours (0700-1900 hours; Normal Weekdays)

Date	Start Time	Finish Time	Weather	L _{10 (30min)}	L _{90 (30min)}	Leq (30min)
7 Jan 21	14:52	15:22	Sunny	53.5	49.5	52.6
14 Jan 21	14:38	15:08	Sunny	52.5	46.5	50.7
20 Jan 21	14:49	15:19	Sunny	51.5	46.5	49.8
28 Jan 21	14:32	15:02	Sunny	52.5	49.0	51.3
4 Feb 21	14:32	15:02	Sunny	52.0	46.5	49.9
9 Feb 21	14:33	15:03	Cloudy	56.0	50.5	54.1
17 Feb 21	13:59	14:29	Sunny	52.0	45.0	49.8
25 Feb 21	15:13	15:43	Cloudy	51.5	48.5	50.2
4 Mar 21	NA	NA	Rainy	Monitori	ing was cance	lled due to
				a	dverse weath	ner.
11 Mar 21	14:30	15:00	Sunny	53.0	47.0	51.5
18 Mar 21	14:39	15:09	Sunny	51.0	46.0	49.3
25 Mar 21	14:37	15:07	Sunny	54.0	47.0	52.2
					Average	e 51.0
					Miı	n 49.3
					Ma	x 54.1

Note:

Correction of +3 dB(A) was made for free field measurements.

Figure E1.1 Graphical Presentation for Noise Monitoring at NM1

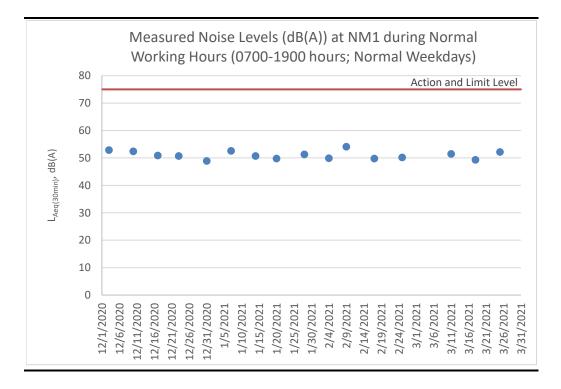

Annex E2

Event and Action Plan for Noise Monitoring

Annex E2 Event and Action Plan for Construction Noise

Event	Action							
	ET	IEC	Contractor					
Action Level	 Identify the source(s) and investigate the cause(s) of exceedance and complaint Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Have additional monitoring if exceedance is due to the Project. If exceedance stops, cease additional monitoring 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Submit proposals for remedial measures to IEC Implement the agreed proposals 					
Limit Level	 Identify the source(s) and investigate the cause(s) of exceedance and complaint Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD whether the cause of exceedance is due to the Project Analyse the operation of SENTX and investigate the causes of exceedance Provide interim report to Contractor, IEC, Project Proponent and EPD the causes of the exceedances Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Report the remedial measures implemented and the additional monitoring results to Contactor, IEC, Project Proponent and EPD Have additional monitoring if exceedance is due to the Project. If exceedance stops, cease additional monitoring 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Take immediate measures to avoid further exceedance Submit proposals for remedial measures to IEC within 3 working days of notification Implement the agreed proposals Resubmit proposals if problem still not under control Stop the relevant activity of works as determined by the Project Proponent until the exceedance is abated 					

Surface Water Quality

Surface Water Quality Monitoring Results

Table F1.1 Surface Water Quality Monitoring Results at DP4T

Date	Time	Weather	Water	Water	Water	Dissolved	pН	Suspended	Remarks
		Condition	Appearance	Condition	Temperature	Oxygen (DO)		Solids (SS)	
					(°C)	(mg/L)		(mg/L)	
7 Jan 21	14:32	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
14 Jan 21	14:30	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
20 Jan 21	14:28	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
28 Jan 21	14:20	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
4 Feb 21	14:19	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
9 Feb 21	14:23	Cloudy		Unable to	collect water samp	ole due to insuffici	ent flow		-
17 Feb 21	14:14	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
25 Feb 21	14:40	Cloudy	Light yellow	Semi clear	20.3	8.09	7.58	13.0	-
25 Feb 21	14:53	Cloudy	Light yellow	Semi clear	20.5	8.07	7.65	12.7	DP4 (Future, temporary) (Duplicate)
4 Mar 21	14:24	Rainy		Unable to	collect water samp	ole due to insuffici	ent flow		-
11 Mar 21	14:23	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
18 Mar 21	14:26	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
25 Mar 21	14:25	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
					Averag	ge 8.08	7.62	12.9	-
					Mi	n 8.07	7.58	12.7	-
					Ma	x 8.09	7.65	13.0	-

Notes: DP4 was temporary relocated to DP4 (Future, temporary) (i.e. DP4T) as an interim discharge point from the monitoring event on 16 May 2019.

Table F1.2 Surface Water Quality Monitoring Results at DP6

Date	Time	Weather	Water	Water	Water	Dissolved	pН	Suspended	Remarks
		Condition	Appearance	Condition	Temperature	Oxygen (DO)		Solids (SS)	
					(°C)	(mg/L)		(mg/L)	
7 Jan 21	14:19	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
14 Jan 21	14:16	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
20 Jan 21	14:13	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
28 Jan 21	14:07	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
4 Feb 21	14:09	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
9 Feb 21	14:10	Cloudy		Unable to	collect water samp	ole due to insuffici	ent flow		-
17 Feb 21	14:05	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
25 Feb 21	14:16	Cloudy		Unable to	collect water samp	ole due to insuffici	ent flow		-
4 Mar 21	14:08	Rainy		Unable to	collect water samp	ole due to insuffici	ent flow		-
11 Mar 21	14:07	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
18 Mar 21	14:09	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
25 Mar 21	14:06	Sunny		Unable to	collect water samp	ole due to insuffici	ent flow		-
					Averag	e -	-	-	-
					Mi	n -	-	-	-
					Ma	x -	-	-	-

Figure F1.1 Graphical Presentation for Surface Water Quality Monitoring (DO)

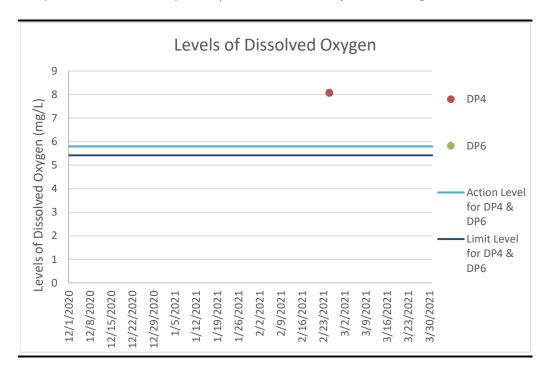


Figure F1.2 Graphical Presentation for Surface Water Quality Monitoring (pH)


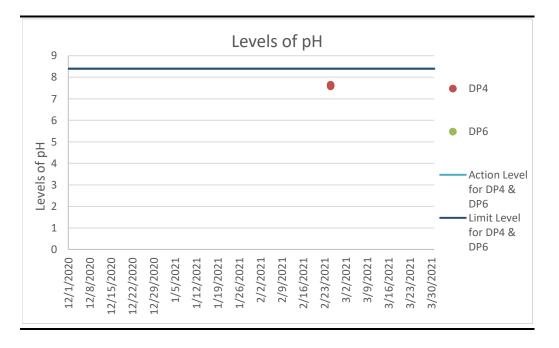


Figure F1.3 Graphical Presentation for Surface Water Quality Monitoring (SS)

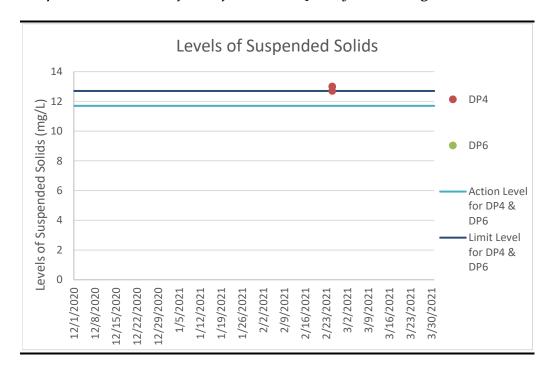

Event and Action Plan for Surface Water Quality Monitoring

Annex F2 Event and Action Plan for Surface Water Quality During Construction Phase

Event	Action						
	ET	IEC	Contractor				
Action Level being exceeded by one sampling day	 Repeat <i>in situ</i> measurement to confirm findings Identify the source(s) and investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project Repeat measurement on the next day of exceedance if exceedance is due to the Project 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods 	 Rectify any unacceptable practice Amend working methods if appropriate 				
Action Level being exceeded by two consecutive sampling days	 Repeat <i>in situ</i> measurement to confirm findings Identify the source(s) and investigate the cause(s) of exceedance Prepare Notification of Exceedance within 24 hours Inform Contractor, IEC and Project Proponent whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Increase the monitoring frequency to daily if exceedance is due to the Project and continue until no exceedance of Action Level 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods Discuss with ET Leader and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Submit proposals for remedial measures to IEC Implement the agreed proposals Amend proposal if appropriate 				

Event	Action						
	ET	IEC	Contractor				
Limit Level being exceeded by two consecutive sampling days	 Repeat <i>in situ</i> measurement to confirm findings Identify source(s) of impact and cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD whether the cause of exceedance is due to the Project Discuss with Contractor and IEC for remedial measures required Ensure remedial measures are properly implemented Increase the monitoring frequency to daily if exceedance is due to the Project until no exceedance of Limit Level 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Critically review the working methods Rectify unacceptable practice Check all plant and equipment Consider changes of working methods Discuss with the ET and IEC and propose mitigation measures to the IEC Implement the agreed mitigation measures 				
Limit Level being exceeded by more than two consecutive sampling days	 Repeat <i>in situ</i> measurement to confirm findings Identify source(s) of impact and cause(s) of exceedance Prepare the Notification of Exceedance within 24 hours Inform Contractor, IEC, Project Proponent and EPD whether the cause of exceedance is due to the Project Check monitoring data, all plant, equipment and Contractor's working methods Discuss with Contractor and IEC for remedial measures required Ensure mitigation measures are implemented Increase the monitoring frequency to daily if exceedance is due to the Project until no exceedance of Limit Level for two consecutive days 	 Verify the Notification of Exceedance Check monitoring data submitted by ET Check Contractor's working methods Discuss with ET and Contractor on proposed remedial measures Review proposals on remedial measures Audit the implementation of the remedial measures Audit the effectiveness of the implemented remedial measures 	 Critically review the working methods Rectify unacceptable practice Check all plant and equipment Consider changes of working methods Discuss with the ET and IEC and propose mitigation measures Implement the agreed mitigation measure As directed by the Project Proponent, slow down or stop all or part of the construction activities 				

ENVIRONMENTAL RESOURCES MANAGEMENT

GREEN VALLEY LANDFILL LTD.

Investigation Reports of Environmental Quality Limit Exceedance

Investigation Report of Environmental Quality Limit Exceedance

Project	South East New Territories (SENT) Landfill Extension
Date	25 February 2021
Time	14:40 and 14:53 (Duplicate)
Monitoring Location	DP4T
Parameter	Surface Water (Suspended Solids (SS))
Action / Limit Levels	Action level: >11.7 mg/L
	Limit level: >12.7 mg/L
Measured Level	DP4T: 13.0 mg/L
	DP4T (Duplicate): 12.7 mg/L
Possible reason	No works which may lead to potential SS increase (e.g. active stockpiling and excavation works) was conducted in the vicinity of surface water channel leading to DP4T on the sampling day based on on-site observations and construction activities described by the Contractor. Surface runoff collected at DP4T channel (solely from the vehicle washing facilities) was treated by the Wetsep prior to discharge. Wetsep near DP4T was functioning properly during the sampling event. Environmental deficiency in related to DP4T was not observed during the weekly site inspection in the morning. The Contractor has taken the necessary control /mitigation measures outlined in the updated EM&A Manual. During the sampling event, no raining was recorded and no other sources (e.g. Clearwater Bay Country Park, other project sites) was identified in the vicinity of surface water channel leading to DP4T which might cause the SS exceedance at DP4T. Contaminated wastewater from the vehicle washing facilities could be the potential source of SS contributing to the exceedance. The SS exceedance at DP4T was therefore deemed to Project-related activities. It should be noted that although the measured SS level exceeded the limit level of the EM&A programme, it is still well within the WPCO effluent discharge limit of SS for the Junk Bay Water Control Zone (30 mg/L). The discharge of surface water with this SS level from DP4T will not cause adverse water quality impact to the Junk Bay Water Control Zone.
Action Taken / Action to be Taken	Examination of environmental performance of the Project will be continued during the weekly inspections. The Contractor is reminded to implement relevant and appropriate mitigation measures according to the updated EM&A Manual to avoid any exceedance of the Action and Limit Level.
	In addition, the Contractor is reminded to check and monitor the Wetsep operation and maintain the system regularly to ensure it is

	functioning properly at all times.
Remarks	-

Prepared by: Abbey Lau

Environmental Team
5 May 2021 Designation:
Date:

Annex G

Cumulative Statistics on Exceedances, Environmental Complaints, Notification of Summons and Status of Prosecutions

 Table G1
 Cumulative Statistics on Exceedances

		Total No. recorded in this reporting period	Total No. recorded since project commencement
Air Quality (24-hr TSP)	Action	0	0
	Limit	0	0
Noise	Action	0	0
	Limit	0	0
Surface Water Quality	Action	0	0
	Limit	1	48

Table G2 Cumulative Statistics on Complaints, Notifications of Summons and Successful Prosecutions

Reporting Period	Cumulative Statistics					
	Complaints	Notifications of Summons	Prosecutions			
This Reporting Period (1 January – 31 March 2021)	0	0	0			
Total no. received since project commencement	1	0	0			
