


Annex C4

Catchment Area of DP3  
with Tentative Construction  
Programme

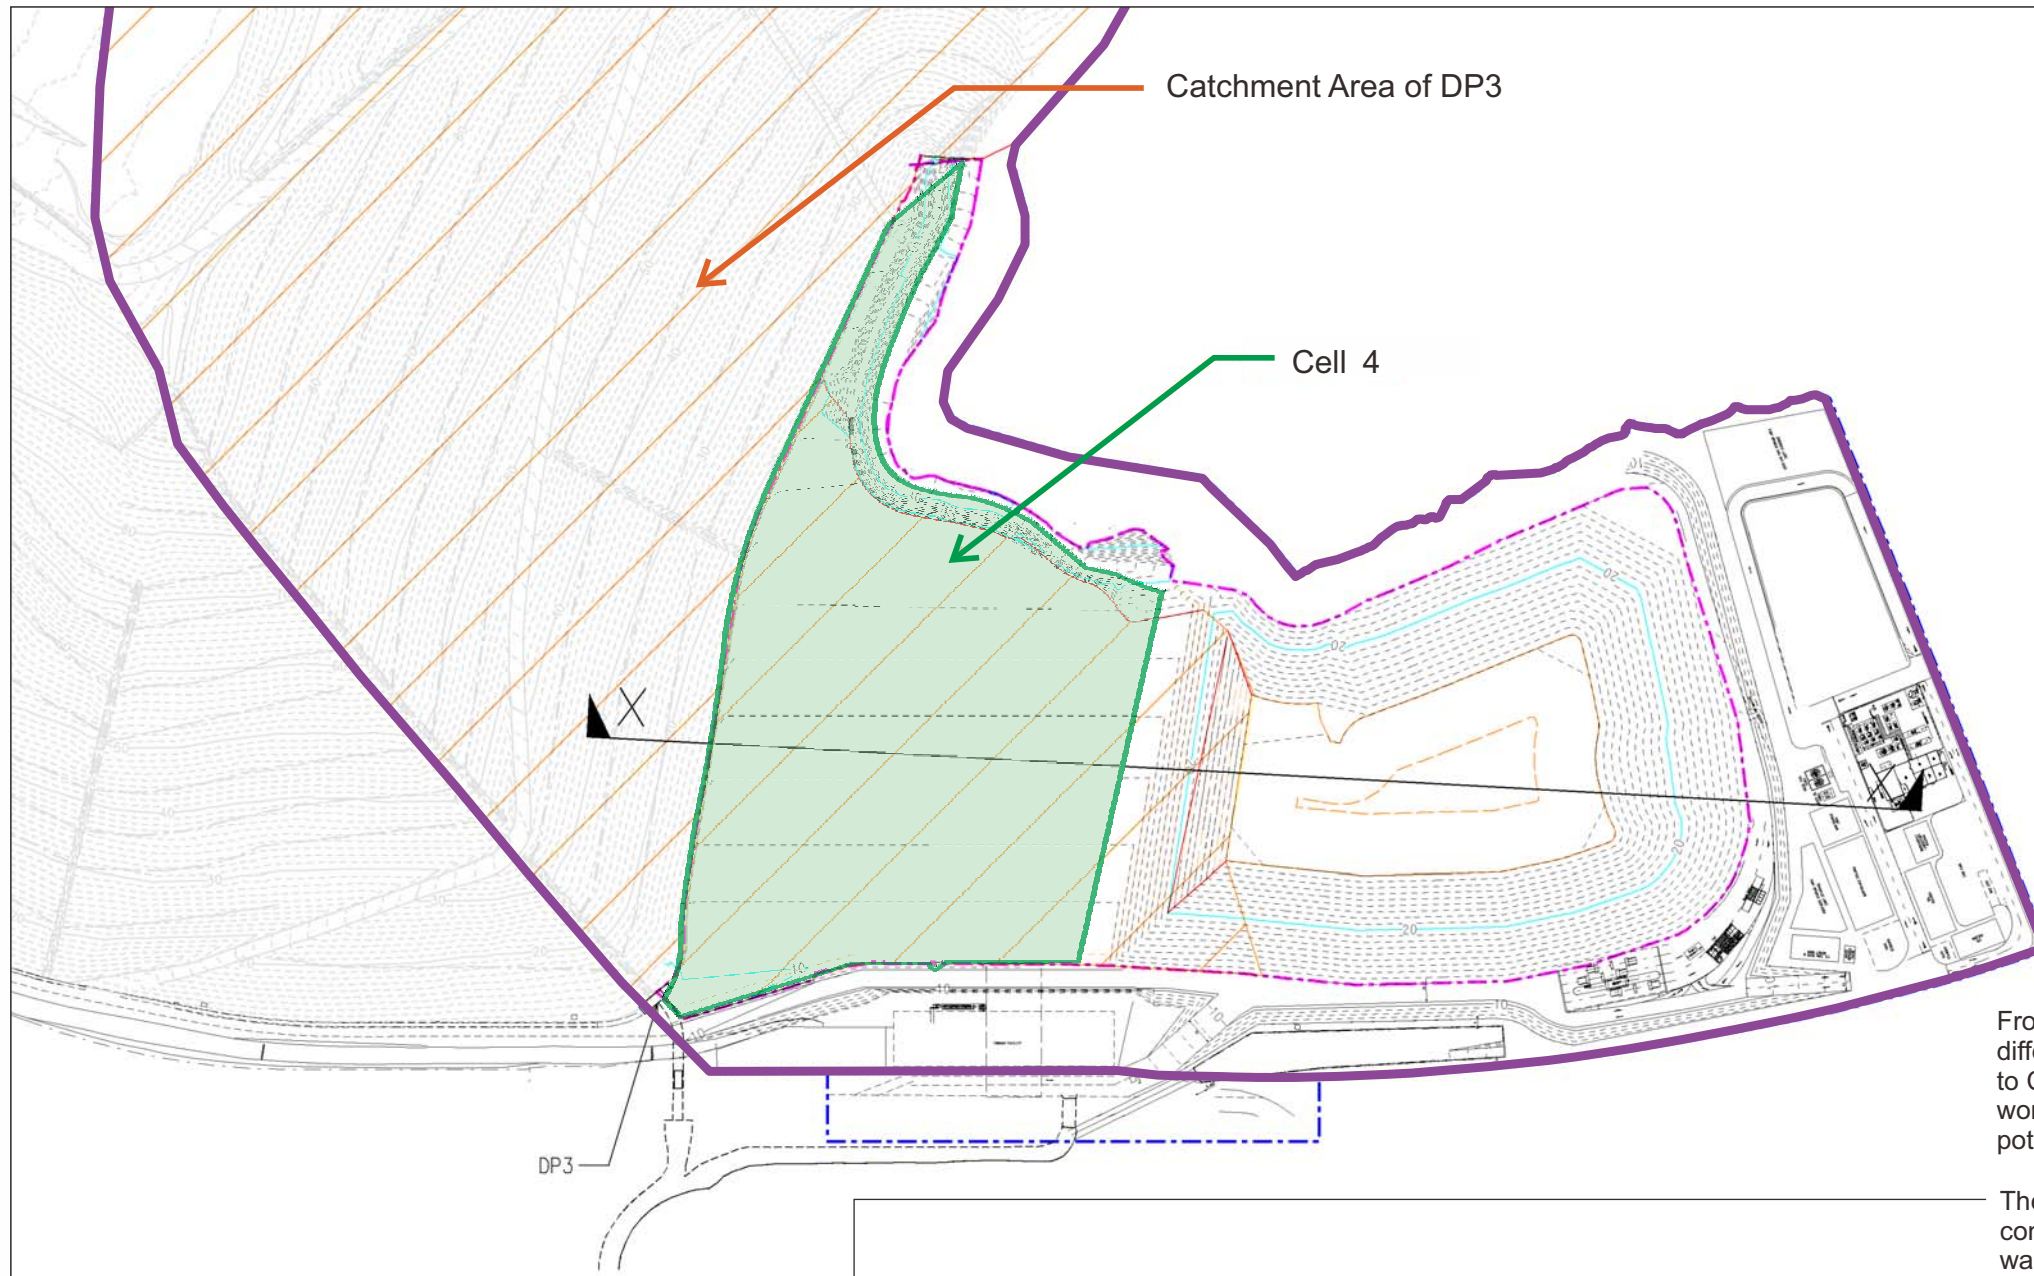

**Key**

The SENTX Site

Location	Tentative Works Programme
Landfill Cell 2	2/11/2019 – 23/1/2021
Landfill Cell 3	20/2/2020 – 2/2/2022
Landfill Cell 4	7/9/2021 – 13/4/2023

From the tentative construction programme above, the construction works at different areas will be conducted in phase, starting from Landfill Cell 2, Cell 3 to Cell 4. The start date of construction works at Cell 4 is 7/9/2021 where the works will be carried out below the level of the cutoff channel and have no potential impact to DP3.

The earliest date when DP3 will be influenced by the SENTX construction/operation is November 2022 when Phase 1A has been filled with waste at the level of the cutoff channel.

Before the filling of waste at the SENT Landfill restored area (i.e. piggyback area of the SENTX and the catchment of DP3 within the Project boundary), the construction works at the SENT Landfill restored area will be the works related to the tie in of the base liner between the existing SENT base liner and the extension part, which is anticipated to be carried out during the dry season 2021/22.

Hence, there will be no other SENTX construction activities affecting DP3 by 2021.

