Annex A

Work Programme

#	WBS Path	Activity	Activity Name	Dur	Start	Finish	Total Float	Predecessor Detail	Successor Detail
335									
336									
337									
338									
339									
340									
341									
342									
343									
344									
345									
346									
347									
348									
349									
350									
351									
352	SA2.5		Construction (Initial Works)	1153	12-Apr-18	01-Nov-21	705		
353	SA2.5.02		Advance Works & Site Establishment	1143	12-Apr-18	01-Nov-21	38		
354	SA2.5.02.01		Site Establishment & Mobilisation	830	12-Apr-18	02-Nov-20	830		
355	SJ02.21	SA4000	Site Mobilisation for Parts X1 & X2	39	31-Dec-18	25-Jan-20	830	1A-1100: FS, 1H-1000: FS	SA2300: FS, M 3, 1 FS, M 3, 2 FS
356	SJ02.21	SA4100	Site Mobilisation for Parts X3, X4 & X5	39	12-Apr-18	11-May-18	1083	1J-1000: FS, 1J-1400: FS, 1H-1000: FS	SA2300: FS, M 3, 1 FF
357	SJ02.21	SA4300	Temporary Office for Employer / EKPC	60	15-Oct-18	08-Jan-19	0	2A-1000: FS	1H-1000: SS, M 3, 1 FS
358	SJ02.21	SA4400	Hoarding and Fencing Works	43	30-Jul-18	10-Nov-18	830	2A-1000: FS, 2A-1100: FS	2A-1000: FS, MH2, 1 FS-20, MH2, 2 FS-10, MH6, 2 FS
359									
360	SA2.5.02.02		Site Survey & Investigation Works for Parts X1 & X2	13	31-Oct-18	15-Nov-18	840		
361	SJ02.22	SA4400	Condition Survey	25	31-Oct-18	30-Nov-18	840	1A-1100: FS, 1H-1000: FS	SA2300: FS
362	SJ02.22	SA4500	Topographic Survey	20	31-Oct-18	19-Nov-18	845	1A-1100: FS, 1H-1000: FS	SA2300: FS
363	SJ02.22	SA4600	Site Inspection, Review of Condition Survey Report	25	31-Oct-18	15-Nov-18	845	1A-1100: FS, SA4400: FS	SA2300: FS
364	SA2.5.02.03		Site Survey & Investigation Works for Parts X3, X4 & X5	13	12-Apr-18	27-May-18	1183		
365	SJ02.23	SA4700	Condition Survey	25	12-Apr-18	09-May-18	1183	1J-1000: FS, 1J-1400: FS, 1H-1000: FS	SA2300: FS
366	SJ02.23	SA4800	Topographic Survey	20	12-Apr-18	07-May-18	1188	1J-1000: FS, 1J-1400: FS, 1H-1000: FS	SA2300: FS
367	SJ02.23	SA4900	Site Inspection, Review of Condition Survey Report	25	12-Apr-18	31-May-18	1183	SA4700: FS, SA4800: FS	SA2300: FS
368	SA2.5.02.04		Environmental Monitoring	175	02-Jul-18	03-Nov-21	38		
369	SJ02.24	SA2000	Installation of Monitoring Stations & Wells (SP & GW)	120	02-Jul-18	25-Nov-18	0	2A-1000: FS	SA2300: SS 60
370	SJ02.24	SA2100	Installation of Monitoring Stations & Wells (SP & GW) on Bellows Well	120	02-Jul-18	25-Nov-18	0	2A-1000: FS	SA2300: SS 60
371	SJ02.24	SA2200	Contract Baseline Monitoring for Construction (one month)	30	01-Dec-18	30-Dec-18	0	1G-2000: SS 60, SA2100: SS 60	1K-1000: FS
372	SJ02.24	SA2300	Contract Baseline Monitoring for Operation (one year)	365	03-Nov-18	03-Nov-21	38	1G-2000: FS+60, SA2000: FS	1K-1000: FS
373	SA2.5.03		Civil Engineering Works	748	12-Apr-18	23-Nov-21	834		
374	SA2.5.03.0		Bulthouse Wall	475	12-Apr-18	15-Jul-20	84		
375	SJ03.2	SA4000	Section 4b, SENT	300	12-Apr-18	07-Feb-20	56	1J-1000: FS, 2A-2000: FS, 5A-2000: FS, 31-2000: FS, 1J-1400: FS	5A-1100: FS, 5A-1900: FS, 5A-2100: FS, M 3, 1: FS-150, M 3, 1: FS
376	SJ03.2	SA4100	Diversion of SENT Landfill Gas Pipe	45	07-Feb-20	27-Mar-20	56	2A-2000: FS, 5A-3000: FS	5A-3100: FS, 5A-4800: FS, M 3, 1: FS
377	SJ03.2	SA4200	Section 4d Cell 4	630	02-May-18	04-Nov-20	63	1J-1000: FS, 2A-2000: FS, 5A-2000: FS, 11-4600: FS	5A-3100: FS, 5A-3100: FS, M 3, 2: FS, M 3, 6: FS+200
378	SJ03.2	SA4300	Install Landfill Gas Pipe on Bulthouse Wall	75	05-Nov-20	19-Jan-20	63	4A-1000: FS, 5A-1100: FS, 5A-1000: FS, 5A-3000: FS	5A-4100: FS
379									
380	SA2.5.03.1		Landfill Cell 1	103	12-Apr-18	23-Aug-20	194		
381	SJ03.1	SA4400	Earth bund (Eastern)	50	04-May-20	31-Jul-20	9	1A-1100: FS, 2A-2000: FS, 5A-1000: FS, 5A-3000: FS	5A-2100: FS, 5A-2000: FS, 5A-3400: FS, 5A-1000: FS, 5A-1100: FS, 5A-1200: FS, 5A-1300: FS, M 4, 2: FS
382	SJ03.1	SA4500	Earth bund (Southern)	50	28-Apr-20	24-Jul-20	194	1A-1100: FS, 2A-2000: FS, 5A-2000: FS	5A-2100: FS, 5A-2000: FS, 5A-3000: FS, 5A-3400: FS, 5A-2100: FS, 5A-2000: FS
383	SJ03.1	SA4600	Earth bund (Western)	50	12-Apr-18	13-Aug-18	417	1A-1100: FS, 2A-2000: FS	5A-3100: FS, 5A-3000: FS, 5A-3000: FS, 5A-3000: FS
384	SJ03.1	SA4700	Bund (Cell 1C)	75	13-Jun-18	28-Nov-18	432	1A-1100: FS, 2A-2000: FS	5A-3100: FS
385	SJ03.1	SA4800	Site Formation	60	12-Apr-18	13-Aug-18	217	1A-1100: FS, 2A-2000: FS, 3A-1000: FS	5A-3100: FS, 5A-1100: FS, 5A-1000: FS, 5A-1000: FS, M 4, 1: FS+20
386									
387	SJ03.1	SA4900	Pump Station (PS#1X)	45	13-Apr-20	27-May-20	337	5A-1000: FS, 5A-3000: FS	5A-2100: FS, 5A-2000: FS
388	SJ03.1	SA5000	Lining Works	120	03-Nov-20	19-Mar-20	216	4A-1000: FS, 5A-1000: FS, 5A-3000: FS, 5A-1000: FS, 5A-1000: FS, 5A-1100: FS	5A-2100: FS
389									
390	SJ03.1	SA2100	Protective Stone Laying & Leachate Collection Pipe	75	14-Mar-20	29-May-20	216	5A-2000: FS, 4A-1100: FS, 5A-2000: FS	5A-2100: FS, 5A-2000: FS, M 4, 3: FS
391	SJ03.1	SA2200	Install Leachate Pipe Main	75	25-Jul-20	07-Nov-20	440	5A-2000: FS, 5A-3000: FS, 4A-5000: FS, 5A-1000: FS	5A-2100: FS
392									
393	SJ03.1	SA2300	Install Landfill Gas Pipe on earth bund	55	01-Nov-19	23-Dec-20	296	4A-5000: FS, 5A-1100: FS, 5A-2000: FS	5A-2100: FS
394	SJ03.1	SA2400	Leachate Pipe Connection (Cell 1 to LTP)	30	08-Nov-20	07-Dec-20	296	5A-2000: FS, 5A-3000: SS	5A-2100: FS
395	SA2.5.03.4		Landfill Cell 4	38	09-Jul-20	31-Aug-20	144		
396	SJ03.4	SA2500	Provide Temporary Leachate Pipe on Cell 4 Area	30	09-Jul-20	31-Aug-20	144	2A-2000: FS, 5A-2000: SS+90	5A-2100: FS, M 3, 3: FS
397	SA2.5.03.5		Drainage - Surface Water	700	12-Apr-18	23-Jul-21	838		
398	SJ03.5	SA2600	Construct Cut-Off Channel 10A	60	16-Apr-18	16-Jul-18	0	1A-1100: FS, 2A-2000: FS	5A-2100: FS
399	SJ03.5	SA2700	Connect CJ-Off Channel 10A to SPS	20	17-Apr-18	08-Apr-18	0	5A-2000: FS, 31-1400: FS, 2A-2000: FS	5A-2100: FS
400	SJ03.5	SA2800	Diversion from Existing Trapezoidal Channel into Channel 10A	20	09-Apr-18	28-Apr-18	0	5A-1100: FS	5A-1100: FS, 5A-1100: FS, 5A-2000: FS, 5A-3000: FS, 5A-1100: FS, M 3, 3: FS
401									
402	SJ03.5	SA2900	Removal of Existing Trapezoidal Channel along Eastern Bund	30	29-Apr-18	29-May-18	0	5A-2000: FS	5A-2100: FS
403	SJ03.5	SA3000	Cut-Off Channel 10 Diversion to Cut-Off Channel 11-2	45	16-Jun-18	29-Nov-18	83	1A-2000: FS, 5A-2000: FS	5A-1100: FS, 5A-1100: FS
404	SJ03.5	SA3100	Cut-Off Channel 11 on Bellows Well Cell 4, Cell 3	90	09-Apr-18	03-Jul-18	208	5A-2000: FS, 5A-3100: FS	5A-3100: FS
405	SJ03.5	SA3200	Temporary Diversion Cut-Off Channel 10 to 10A	20	04-Jul-18	23-Jul-18	208	5A-3100: FS, 2A-2100: FS	5A-3100: FS, M 3, 4: FS
406	SJ03.5	SA3300	Culvert 4A (km 1.4) & Farm Connection of Cut-Off Channel 4b	30	26-Nov-18	24-Jan-19	134	5A-1100: FF, 5A-1600: FS, 5A-3000: FS	5A-1300: FS
407	SJ03.5	SA3400	Construct Perimeter Channel 4b on Eastern Bund & Southern Bund of Cell 1	60	12-Nov-18	31-Jan-19	240	5A-4000: FS, 5A-1300: FS	5A-3100: FS
408	SJ03.5	SA3500	Construct Perimeter Channel 4b on Eastern Bund of Cell 2	50	28-Jul-18	05-Apr-18	168	5A-3000: FS, 5A-3400: FS	5A-3100: FS
409	SJ03.5	SA3600	Construct Perimeter Channel 4b Eastern Bund of Cell 3	50	09-Nov-18	28-Jan-19	120	5A-3100: FS, 5A-3400: FS	5A-3100: FS
410	SJ03.5	SA3700	Culvert 4A (km 1.8) of Cell 1 Southern Bund	15	28-Jul-18	07-Nov-18	1214	5A-3100: FS	
411	SJ03.5	SA3800	Perimeter Channel 4b of Cell 1 Southern & Western Bund	45	03-Jul-18	13-Nov-18	1344	5A-3100: FS, 5A-3100: FS	
412	SJ03.5	SA3900	Drop Inlet & Culvert (KB) +7 m long	100	29-Jul-18	31-Dec-18	120	1A-1100: FS, 2A-2000: FS, 5A-3000: FS	5A-3100: FF, 5A-4100: FF, 5A-3000: FS, M 3, 1: FS-40, MH5, 2: FS
413									
414	SJ03.5	SA4000	Sediment Trap (ST)	100	29-Jul-18	24-Nov-18	120	1A-1100: FS, 2A-2000: FS, 11-2300: FS, 5A-3000: FF	5A-3000: FS, M 3, 3: FS-20, M 3, 4: FS
415	SJ03.5	SA4100	Dual Culvert 7m long (connects DP4)	100	29-Jul-18	24-Nov-18	120	1A-1100: FS, 11-2300: FS, 2A-3000: FS, 5A-3000: FF	5A-3300: FF, 5A-4000: FS, M 3, 1: FS-40, M 3, 2: FS
416									
417	SA2.5.03.6		Drainage - Ground Water	330	04-May-18	14-Nov-18	378		
418	SJ03.6	SA4200	Construct Groundwater Collection Pipe along Cell X1 & X2 Eastern Bund	70	04-May-18	03-Aug-18	0	1A-1100: FS, 2A-2000: FS, 5A-3000: FS	5A-1100: FS, 5A-3000: FS, 5A-4000: FS, 5A-5000: FS
419									
420	SJ03.6	SA4300	Construct Groundwater Collection Pipe along Cell X3 Eastern Bund	50	04-Aug-18	22-Nov-18	158	5A-3000: FS	5A-4000: FS, 5A-3000: FS
421	SJ03.6	SA4400	Construct Groundwater Collection Pipe along Internal Bund (X3X4)	50	23-Aug-18	11-Nov-18	208	5A-3000: FS	5A-4000: FS, 5A-3000: FS
422	SJ03.6	SA4500	Construct Manhole (MH47)	30	12-Nov-18	14-Dec-18	203	5A-4000: FS	5A-3000: FS, M 3, 5: FS
423	SA2.5.03.7		Utilities - Distribution within New Infrastructure Area	201	14-Jun-18	04-Dec-18	215		
424	SJ03.7	SA4600	Power Supply PV Works (Transformer & HV switchgear)	5	30-Jun-18	06-Jul-18	0	5A-2000: FS	5A-3300: FS
425	SJ03.7	SA4700	Power Distribution, LV Power Supply Works	2	09-Jul-18	09-Jul-18	0	5A-3100: FS, 5A-2000: FS	1A-1900: FS
426	SJ03.7	SA4800	Sewerage (Sewerage Reticulation to LTP)	60	01-Jul-18	04-Jul-18	271	5A-3000: FS, 5A-2100: FS, 5A-2000: FS, 5A-1100: FS	5A-3100: FS, 5A-3100: FS
427									
428	SJ03.7	SA4900	Sewerage (Discharge to Site Boundary)	60	01-Jul-18	04-Jul-18	271	5A-3000: FS, 5A-1100: FS, 5A-4000: FS	1A-1100: FS, 5A-3100: FS
429	SJ03.7	SA5000	Lighting Provision	30	01-Jul-18	04-Aug-18	6	5A-2000: FS, 5A-1100: FS, 5A-4000: FS	1A-1100: FS, 5A-3100: FS
430	SJ03.7	SA5100	Fire Services	110	13-Mar-18	08-Jul-18	2	5A-3000: FS	1A-1900: FS
431	SJ03.7	SA5200	Water Supply (Fresh & Salt)	110	13-Mar-18	08-Jul-18	338	5A-3000: FS, 5A-1100: FS	1A-1100: FS
432	SJ03.7	SA5300	Telecom & Network	43	17-Apr-18	24-Jun-18	620	5A-3000: FS	1A-1100: FS
433	SJ03.7	SA5400	Gas Network (LPG to LTP)	15	28-Jun-18	09-Jul-18	178	5A-3000: FF	5A-3300: FS
434	SA2.5.03.8		Utilities - Works Associated with Utilities Undertakers	703	27-Jul-18	30-Jun-21	128		
435	SA2.5.03.8.1		CLP	508	27-Jul-18	30-Nov-21	43		
436	SJ03.8.1/P	SA5500	Excavate Trench for CLP Cable	100	13-May-19	30-Aug-19	104	2A-2000: FS	5A-5000: FS, 5A-1300: SS, 5A-1100: SS, 5A-4000: SS, MH3, 1: FS+40, MH3, 2: FS+40, MH3, 3: FS
437									
438	SJ03.8.1/P	SA5600	Backfill Trench after CLP Cable Laying	30	19-May-19	30-May-19	43	5A-5000: FS	5A-5000: FF, 5A-4100: FF, 5A-4000: FF
439	SJ03.8.1/P	SA5700	CLP Cable Laying (from CLP Substation to Site Boundary)	200	27-Jul-18	16-Jul-19	328	5A-2000: FS	5A-3000: FS
440	SJ03.8.1/P	SA5800	CLP Cable Laying (from Site Boundary to HV Switchroom)	60	03-Mar-20	28-Jul-20	0	5A-3000: FS, 5A-2000: FS, 5A-3000: FS, 5A-5000: FF 15	5A-3000: FS, 5A-3000: FS
441									
442	SJ03.8.1/P	SA5900	CLP HV associated equipment installation	120	19-Dec-19	13-Apr-20	0	5A-2000: FS, 5A-3000: FS	5A-3000: FF 15
443	SA2.5.03.8.2		DSD	187	30-Dec-20	30-Jun-21	128		
444	SJ03.8.2/P	SA6000	Connection to Storm Drain System	2	29-Jun-21	30-Jun-21	128	5A-3100: FS, 5A-2000: FS, 5A-2000: FS	5A-1900: FS
445	SJ03.8.2/P	SA6100	Connection to Foul Drain System	5	30-Dec-20	04-Jan-21	271	5A-3000: FS, 5A-2000: FS	5A-1900: FS
446	SA2.5.03.8.3		Telecom	100	13-May-19	30-Jun-19	327		
447	SJ03.8.3/P	SA6200	Excavate Trench for PCCW	60	13-May-19	11-Jul-19	307	2A-2000: FS	5A-5000: FS, 5A-1300: SS, 5A-4000: SS, 5A-5000: SS, MH3, 1: FS+40, MH3, 2: FS+20, M 3, 3: FS
448									
449	SJ03.8.3/P	SA6300	Backfill Trench after PCCW Cable Laying	10	12-Aug-19	30-Aug-19	327	5A-5000: FS	5A-3000: FF, 5A-4100: FF, 5A-4000: FF
450	SJ03.8.3/P	SA6400	Laying Cables & Connection	30	13-Jul-19	10-Aug-19	327	5A-3000: FS	5A-3300: FS, 5A-3300: FS
451	SA2.5.03.8.4		WSD	304	13-May-19	13-Dec-19	128		
452	SJ03.8.4/P	SA6500	Install Watermain & Piping for Water Supplies	60	13-May-19	11-Jul-19	216	2A-2000: FS	5A-5000: FS, 5A-4100: FS, 5A-5000: FS, 5A-5000: FS
453									
454	SJ03.8.4/P	SA6600	Connection for Fresh Water & Meter Installation	30	13-Jul-20	13-Aug-20	338	5A-3000: FS, 5A-2000: FS	5A-3200: FS
455	SJ03.8.4/P	SA6700	Connection for Salt Water	30	13-Jul-20	13-Aug-20	338	5A-3000: FS, 5A-2000: FS	5A-3200: FS
456	SJ03.8.4/P	SA6800	Connection for Fire Services	30	13-Jul-20	13-Aug-20	2	5A-3000: FS, 5A-2000: FS	5A-3100: FS
457	SJ03.8.4/P	SA6900	Connection for Cooling Tower & Meter Installation	30	13-Jul-20	13-Aug-20	117	5A-3000: FS, 5A-2000: FS	5A-3100: FS, 5A-3000: FS
458	SA2.5.03.8.5		HK Lighting	120	07-Jul-18	04-Nov-21	218		
459	SJ03.8.5/P	SA7000	Installation of Public Street Lighting / Handover	120	07-Jul-18	04-Nov-21	218	5A-4100: FS, 5A-4000: FS, 5A-5000: FS	5A-1900: FS
460									
461	SA2.5.04		Building Construction, incl. E&M and System Installation, and T&C	800	31-Oct-18	31-Jul-21	0		
462	SA2.5.04.A		Part X1 Area A	554	31-Oct-18	05-Jul-20	30		
463	SJ04.A	SA1000	General Area & Access Road	120	08-Mar-20	05-Jul-20	0	2A-3300: FS, 5A-5000: SS, 5A-5000: FF, 5A-3000: SS, 5A-5000: FF, 1A-1100: FS, 5A-4000: FF, 5A-5100: FS, 5A-5000: FF	2A-3100: FS, 2A-3100: SS, 2A-4000: FS, 5A-5000: FS, 5A-5000: FS, 5A-5100: FS, 5A-5100: FS
464									
465	SJ04.A	SA1100	Carpark & Supporting Area	60	31-Oct-18	28-Jan-19	84	2A-3300: FS, 1A-1100: FS	2A-3300: FS, M 3, 1: FS-30, M 3, 2: FS, 5A-4000: FF, 5A-1900: FS
466									
467	SJ04.A	SA1200	Diesel Fuel Tanks	60	08-May-20	05-Jul-20	30	2A-3300: FS, 2A-3000: FS, 12-4000: FF, 1A-1100: FS	5A-1900: FS
468									
469	SJ04.A	SA1300	EPD Building	270	30-Apr-19	30-Jan-20	46	2A-3300: FS, 2A-3000: FS, 1A-1100: FS, 5A-1700: SS 60	5A-1900: FS, M 3, 4: FS+135, M 3, 5: FS, 1A-4000: FS, 5A-1400: SS 60
470									
471	SJ04.A	SA1400	Fire Service Tank	270	29-Apr-19	24-Nov-19	44	2A-3300: FS, 2A-3000: FS, 1A-1100: FS, 5A-1400: SS 60	5A-1900: FS, M 3, 6: FS, 1A-4000: FS, 5A-1400: SS 60
472									
473	SJ04.A	SA1500	WA, Building	300	31-Oct-18	28-Oct-19	44	2A-3300: FS, 2A-3000: FS, 1A-1100: FS	5A-1900: FS, M 3, 1: SF 30, M 3, 2: SF 60, M 3, 3: FS, 5A-1400: SS 60
474									
475	SJ04.A	SA1600	Laboratory Building	270	29-Apr-19	23-May-19	44	2A-3300: FS, 2A-3000: FS, 1A-1100: FS, 5A-1400: SS 60	5A-1900: FS, M 3, 6: FS+135, M 3, 7: FS, 1A-4000: FS, 5A-1400: SS 60
476									
477	SJ04.A	SA1700	Maintenance Building & Area	270	09-Nov-19	05-Nov-19	44	2A-3300: FS, 2A-3000: FS, 1A-1100: FS, 5A-1500: SS 60	5A-1900: FS, M 3, 6: FS+135, M 3, 9: FS, 1A-4000: FS, 5A-1400: SS 60
478									
479	SJ04.A	SA1800	Storage Facility & Area	60	04-Mar-19	29-Apr-19	84	2A-3300: FS, 1A-1100: FS, 5A-1400: FS	5A-1900: FS, M 3, 10: FS+135, M 3, 12: FS, 5A-1900: FF, 5A-1900: FS
480									
481	SJ04.A	SA1900	Waste Oil Tanks	90	08-Mar-20	06-Jul-20	30	2A-3300: FS, 2A-3000: FS, 12-4000: FF, 1A-1100: FS	5A-1900: FS
482									
483	SJ04.A	SA2000	Water Service House	90	30-Apr-19	28-Jul-19	84	2A-3300: FS, 2A-3000: FS, 1A-1100: FS, 5A-1900: FS	5A-1100: FS, M 3, 13: FS, 1A-1000: FS, 5A-4400: FS
484									
485	SA2.5.04.B		Part X1 Area B	800	31-Oct-18	31-Jul-21	0		
486	SA2.5.04.B.1		Bus/Rest Building	310	31-Oct-18	12-Dec-19	243		
487	SJ04.B.1	SA2100	LTP Bus/Rest Building	300	31-Oct-18	12-Dec-19	243	2A-3300: FS, 2A-3000: FS, 2A-3000: FS, 1A-1100: FS, 3A-2000: FS	5A-2100: FS, 5A-2000: FS, M 4, 2: FS+20, M 4, 3: FS
488									
489	SA2.5.04.B.2		Leachate Treatment Plant	500	31-Oct-18	31-Jul-21	21		
490	SJ04.B.2	SA2200	Main Plant Area (excluded Civil works	274	31-Oct-18	30-Oct-19	0	2A-3300: FS, 2A-3000: FS, 1A-1100: FS	5A-2300: FS, 5A-2300: FS, 5A-2300: FS, 5A-4100: FS, M 5, 1: SF 30, M 5, 4: FS+131, M 5, 5: FS
491									
492	SJ04.B.2	SA2300	MEP Installation	226	01-Dec-19	03-May-20	0	4A-2100: FS, 4A-2000: FS, 2A-2100: FS, 5A-2000: FS, 1A-1100: FS	1A-1100: FS+90, 5A-1800: FS, 5A-3000: FS, M 5, 8: FS+193, M 5, 9: FS, 2A-2100: FS
493									
494	SJ04.B.2	SA2400	SBR Tanks	100	01-Dec-19	09-Mar-20	238	4A-2100: FS, 5A-2000: FS	5A-3000: FS, M 5, 6: FS
495	SJ04.B.2	SA2500	Ammonia Stripper	315	01-Dec-19	03-Aug-20	21	4A-2000: FS, 5A-2000: FS	5A-3000: FS, M 5, 8: FS+150, M 5, 9: FS
496	SA2.5.04.B.3		LTP - Test & Commission	301	17-Aug-20	31-Jul-21	0		
497	SJ04.B.3	SA2600	Dry testing	45	17-Aug-20	24-Oct-20	21	5A-2000: FS, 5A-2400: FS, 5A-2600: FS	2A-4000: FS+150, 2A-4000: SS, 5A-2700: FS, M 5, 1: FS
498									
499	SJ04.B.3	SA2700	Wet testing	75	30-Nov-20	09-Dec-20	21	5A-2000: FS, 12-2100: FS, 5A-2000: FS, 3A-2000: FS, 2A-4000: FS	5A-2000: FS, M 5, 2: FS
500									
501	SJ04.B.3	SA2800	Operational testing	169	30-Nov-20	01-Jul-21	0	5A-2700: FS, 5A-2400: FS, 5A-2500: FS, 5A-2100: FS, 5A-2000: FS, 5A-2700: FS, 5A-2600: FS, 5A-2600: FS, 5A-4000: FS, 5A-4000: FS	5A-3000: FS, M 5, 3: FS, M 5, 4: FS
502									
503	SA2.5.04.C		Part X1 Area C	730	31-Oct-18	29-Dec-20	0		
504	SA2.5.04.C.1		LPG - Power Supply Building	530	31-Oct-18	29-Dec-20	5		
505	SJ04.C.1	SA2900	LPG Building (with Transformer Room)	336	31-Oct-18	17-Dec-19	0	2A-3300: FS, 2A-3000: FS, 1A-1100: FS, 3A-1100: FS	5A-4000: FS, 5A-4000: FS, 5A-4000: FS, 5A-3100: FS, M 3, 8: FS
506									
507	SJ04.C.1	SA3000	Transformer & HV Switchgear Installation	60	01-Mar-20	29-Jun-20	0	5A-2000: FS, 4A-1100: FS, 5A-4000: FS, 5A-2100: FS	5A-4000: FS, M 3, 4: FS+30, M 3, 5: FS, M 3, 6: FF
508									
509	SJ04.C.1	SA3100	MEP Installation, with T&C	75	16-Dec-19	07-Mar-20	125	5A-2000: FS	5A-4000: FS, 5A-2100: FS, 5A-4000: FS, 5A-4000: FS, M 3, 4: FS+30, M 3, 5: FS
510	SA2.5.04.C.2		LPG Treatment Plant	554	31-Oct-18	09-Jul-20	0		
511	SJ04.C.2	SA3200	Main Plant Area (excluded Civil Works	394	31-Oct-18	09-Mar-20	0	2A-3300: FS, 1A-1100: FS	5A-3000: FS, 5A-4000: FS, 5A-3000: FS, 5A-3000: FS, 5A-2700: FS, 5A-3000: FS, 5A-3000: FS, M 3, 1: SF 30, M 3, 2: FS+200, M 3, 3: FS
512									
513	SJ04.C.2	SA3300	MEP Installation	119	16-Jun-20	06-Jul-20	0	5A-2000: FS, 12-2000: FF	5A-2000: FS, 5A-4000: FS, 5A-2000: FS, M 3, 4: FS+20, M 3, 5: FS
514									
515	SJ04.C.2	SA3400	GY5000 & Diesel 901 A&B Relocation	15	16-Jun-20	07-Mar-20	155	5A-2000: FS, 5A-4000: FS	5A-2000: FS, M 3, 4: FS+5, M 3, 5: FS
516	SJ04.C.2	SA3500	Pre-treatment	60	16-Jun-20	18-Mar-20	110	4A-2000: FS, 5A-2000: FS	5A-2000: FS, M 3, 4: FS+20, M 3, 5: FS
517	SJ04.C.2	SA3600	Piping (incl. PLC control, interface to Tuengun PF & LTP)	125	16-Jun-20	23-May-20	45	4A-3000: FS, 5A-4000: FS	5A-2000: FS, M 3, 4: FS+40, M 3, 5: FS
518	SJ04.C.2	SA3700	UFG Piping (incl. anti-corrosion protection, PLC control, flushing)	110	29-Nov-20	09-Jun-20	27	4A-3000: FS, 5A-4000: FS	5A-3000: FS, M 3, 4: FS+40
519	SJ04.C.2	SA3800	Cooling System	45	29-Nov-20	12-Jan-20	125	2A-4000: FS, 5A-4000: FS	5A-2000: FS, M 3, 4: FS+50, M 3, 5: FS
520									
521	SA2.5.04.C.3		LPG - Test & Commission	175	01-Jul-20	29-Dec-20	0		
522	SJ04.C.3	SA3900	MEP Testing	65	01-Jul-20	30-Sep-20	0	5A-2000: FS, 5A-2000: FS, 5A-2000: FS, 5A-2000: FS, 5A-2000: FS, 5A-2000: FS, 5A-2200: FS, 5A-2000: FS, 3A-2000: FS, 5A-2000: FS	2A-7000: SS+60, 2A-3000: SS, 5A-4000: FS, MH1, 1: FS+20, MH1, 2: FS
523									
524	SJ04.C.3	SA4000	Operational Testing	111	10-Nov-20	29-Dec-20	0	5A-2300: FS, 5A-2400: FS, 5A-2600: FS, 5A-2000: FS, 5A-2100: FS, 5A-2000: FS, 2A-2200: FS	2A-7000: FS, 5A-4000: FS, 5A-4000: FF, 5A-4000: FS, 5A-4000: FS, MH1, 3: FS, MH1, 4: FS
525									
526	SA2.5.04.D		Part X1 Area D	374	30-Jun-19	06-Jul-20	0		
527	SJ04.D	SA4100	General Area & Access Road	120	09-Nov-20	06-Jul-20	0	2A-3300: FS, 5A-5000: SS, 5A-5000: FF, 5A-3000: SS, 5A-5000: FF, 12-4000: FF, 1A-1100: FS	5A-5100: FS, 5A-5000: FS, 5A-5000: FS, 5A-5000: FS, 5A-5100: FS, 5A-5100: FS
528									
529	SJ04.D	SA4200	VWF Building	120	30-Oct-19	04-Feb-20	63	2A-3300: FS, 2A-3000: FS, 4A-4000: FS, 1A-1100: FS	5A-2100: FS, M 3, 4: FS, M 3, 6: FS+40, M 3, 7: FS, 12-1000: FS, 5A-4000: SS 60
530									
531	SJ04.D	SA4300	Weighbridge	75	30-Nov-19	11-Mar-19	63	4A-2000: FS, 2A-3300: FS, 2A-3000: FS, 1A-1100: FS, 5A-4000: SS 60	5A-2100: FS, M 3, 6: FS+40, M 3,

P	WBS Pack	Activity ID	Activity Name	Dur	Start	Finish	Total Float	Predecessor Detail	Successor Detail
308		**SA2.6.0.3**	**Cell Engineering Works**	1250	03-Mar-19	13-Jul-24	36		
310		**SA2.6.0.3.1**	**Landfill Cell 2**	440	03-Mar-19	23-Dec-20	850		
311		6J03.J	Earth bund (Eastern)	110	03-Mar-19	10-Aug-20	9	1A-1100 FS, 2A-2000 FS, 5A-5400 FS, 5X-1400 FS, 6A-2000 FS	6A-3000 FS, 6X-1500 FS, 6X-3000 FS, 6X-3100 FS, 6X-3200 FS, 6X-3300 FS, 6X-3500 FS, 6X-3600 FS, M12, 1 FS -40, M12, 2 FS, 6X-1000 FS
312		6J03.J	Earth bund (Western)	110	20-Mar-19	18-Jun-20	64	1A-1100 FS, 2A-2000 FS, 5A-5400 FS, 5X-1400 FS, 6A-2000 FS	6A-3000 FS, 6X-1500 FS, 6X-1700 FS, 6X-3000 FS, 6X-3400 FS, 6X-3500 FS
313		6J03.J	Inner Bund (Cell 2b)	90	07-Jun-19	08-Sep-20	734	1A-1100 FS, 2A-2000 FS, 5A-5400 FS, 5X-1400 FS, 5A-6600 FS, 6A-1000 FS	6A-3400 FS
314		6J03.J	Site Formation	75	03-Mar-19	15-Jun-20	11	1A-1100 FS, 2A-2000 FS, 5A-5400 FS, 5X-1400 FS	6A-3000 FS, 6A-3200 FS
315		6J03.J	Pump Station (PSR2X)	45	07-Jun-20	31-Jul-20	54	6A-3000 FS, 6A-1000 FS	6A-3400 FS, 6A-1700 FS
316		6J03.J	Lining Works	90	01-Jul-20	09-Dec-20	710	1A-1100 FS, 6A-1000 FS, 6A-1100 FS, 6A-3300 FS	6A-3400 FS, M12, 3 FS, 6A-3400 FS
317		6J03.J	Protective Stone Laying & Leachate Collection Pipe	25	30-Dec-20	23-Jan-21	510	6A-3000 FS, 4A-1000 FS, 6A-4100 FS	6A-3400 FS, M12, 3 FS
318		6J03.J	Install Leachate Force Main	75	24-Jul-20	06-Oct-20	64	6A-1100 FS, 4A-1000 FS, 6A-4100 FS	6A-3400 FS, M12, 3 FS
319		6J03.J	Install Landfill Gas Pipe on earth bund	35	20-Jul-20	31-Aug-20	168	4A-1000 FS, 6A-3000 FS	6A-3400 FS, M12, 3 FS
320		**SA2.6.0.3.2**	**Landfill Cell 3**	710	03-Mar-19	02-Feb-22	436		
321		6J03.J	Earth bund (Eastern)	110	20-Mar-19	18-Jun-20	9	1A-1100 FS, 2A-2000 FS, 5A-5400 FS, 5X-1400 FS, 6A-2000 FS	6A-3000 FS, 6X-1500 FS, 6A-3100 FS, 6A-3200 FS, 6A-3300 FS, M12, 1 FS -40, M12, 2 FS, 6A-3300 FS -40, 6X-2000 FS
322		6J03.J	Earth bund (Western)	110	29-Apr-19	12-Aug-20	19	1A-1100 FS, 2A-2000 FS, 6A-3400 FS -45	6A-3000 FS, 6A-3400 FS, 6A-3500 FS, 6A-3700 FS, 6A-3700 FS -45
323		6J03.J	Inner Bund (Cell 3b)	105	29-Jun-19	11-Feb-20	769	1A-1100 FS, 6A-3000 FS, 6A-3100 FS, 6A-3200 FS -45	6A-3400 FS
324		6J03.J	Site Formation	75	09-Jun-19	17-Aug-20	9	1A-1100 FS, 6A-3000 FS, 6A-3400 FS	6A-3400 FS
325		6J03.J	Pump Station (PSR3X)	45	23-Aug-19	08-Oct-20	9	6A-3000 FS, 6A-3000 FS	6A-3400 FS, 6A-3600 FS
326		6J03.J	Lining Works	100	01-Oct-20	04-Mar-21	435	4A-1000 FS, 6A-3000 FS, 6A-3000 FS, 6A-3100 FS, 6A-3100 FS	6A-3400 FS, M12, 3 FS
327		6J03.J	Protective Stone Laying & Leachate Collection Pipe	25	05-Nov-20	02-Feb-21	435	6A-3000 FS, 4A-1000 FS, 6A-3000 FS	6A-3400 FS, M12, 3 FS
328		6J03.J	Install Leachate Force Main	75	07-Oct-20	29-Dec-20	9	6A-3000 FS, 4A-1000 FS, 6A-3000 FS	6A-3400 SS -80, 6A-3600 FS, M12, 3 FS
329		6J03.J	Install Landfill Gas Pipe on earth bund	35	09-Nov-20	13-Jan-21	56	4A-1000 FS, 6A-3000 FS	6A-3400 FS, M12, 3 FS
330		**SA2.6.0.4**	**Landfill Cell 4**	550	01-Nov-21	13-Jul-23	38		
331		6J03.J	Remaining Portion of Baffles Wall	120	01-Nov-21	04-Jun-22	494	6A-1000 FS	
332		6J03.J	Earth bund (Western) incl. NSE Wall	120	01-Nov-21	04-Jun-22	239	6A-1000 FS	6A-3000 FS, 6A-3100 FS, 6A-3200 FS, 6A-3400 FS, 6A-3500 FS, 6A-3600 FS, 6A-4100 SS -40, M12, 6 FS -30, M12, 7 FS -30, M12, 8 FS
333		6J03.J	Site Formation	120	01-Nov-21	04-May-22	239	6A-1000 FS, 6A-1100 FS, 6A-3100 FS, 6A-3600 FS, 6A-4100 FS	6A-3100 FS
334		6J03.J	Pump Station (PSR4X)	45	05-May-22	15-Jun-22	239	6A-3000 FS, 6A-3600 FS	6A-3400 FS, 6A-3400 FS
335		6J03.J	Lining Works	135	01-Oct-22	12-Feb-23	0	4A-1000 FS, 6A-3000 FS	6A-3000 FS, M12, 8 FS
336		6J03.J	Protective Stone Laying & Leachate Collection Pipe	60	13-Feb-23	13-Apr-23	0	4A-1000 FS, 6A-3000 FS, 6A-3100 FS	6A-3000 FS, 6A-3100 FS, M12, 8 FS
337		6J03.J	Install Leachate Force Main & Remove Temporary Leachate Pipe	30	13-Apr-23	05-Jul-23	269	4A-1000 FS, 6A-3000 FS, 6A-3100 FS	6A-3100 FS, 6A-3100 FS, M12, 8 FS
338		**SA2.6.0.5**	**Drainage - Surface Run-Off**	750	10-Apr-19	03-Feb-22	494		
339		6J03.J	Perimeter Channel (V6A) at Cell 2 Western Bund	15	03-Apr-19	23-Apr-19	6084	6A-1100 FS	6A-3100 FS
340		6J03.J	Perimeter Channel (V7A) at Cell 2 Western Bund	30	08-Apr-19	19-Apr-19	6029	6A-1100 FS	6A-3100 FS
341		6J03.J	Perimeter Channel (V7A) at Cell 3 Western Bund	30	13-Apr-20	11-May-20	394	6A-3000 FS	6A-3100 FS
342		6J03.J	Perimeter Channel (V7A) at Cell 4 Western Bund	20	30-Apr-21	24-May-21	494	6A-3000 FS	6A-3100 FS
343		6J03.J	Perimeter Channel (V7C) at Cell 4 Western Bund	15	30-Apr-21	13-May-21	499	6A-3000 FS	6A-3100 FS
344		6J03.J	Connection to Existing DPS	10	25-Apr-22	03-Feb-22	494	6A-3000 FS, 6A-3100 FS, 6A-3100 FS, 6A-3600 FS	6A-3100 FS
345		6J03.J	Remove CL-A2R Channel (CL-2 at section of Baffles Wall)	30	30-Jun-22	30-Jul-22	619	6A-3000, SS -80	6A-3000 FS
346		6J03.J	Temporary Channel (NTT) at EBNT Infrastructure Area	30	30-Jun-22	14-Feb-22	14	6A-3000 FS	6A-3100 FS, 6A-3100 FS
347		**SA2.6.0.6**	**Drainage - Ground Water**	55	01-Nov-21	30-Jun-22	539		
348		6J03.J	Construct Temporary Channel (TC-1) from M-14 to Existing UC-E25	50	01-Nov-21	29-Dec-21	539	2A-1000 FS, 1A-1000 FS, 6A-3000 FS	6A-4000 FS
349		6J03.J	Open Gully at Km 1 to TC-1	5	29-Nov-21	04-Dec-21	539	6A-4000 FS	6A-4100 FS, M1A, 9 FS
350		6J03.J	Reconnection of GWCP across Cell 4	30	01-Jun-22	30-Jun-22	539	6A-1100 FS, 6A-3100 FS, 6A-4000 FS	1A-1100 FS
351		**SA2.6.0.9**	**Utilities - Works Associated with Utilities Undertakers**	200	15-Nov-21	31-Jul-22	656		
352		**SA2.6.0.9.1**	**CLP**	210	15-Nov-21	31-Jul-22	656		
353		6J3L5.1P	LPG Generator Overall Testing	180	30-Dec-21	27-Jun-22	656	5A-5500 FS, 1A-1100 FS, 5A-5600 FS	6A-1100 FS
354		6J3L5.1P	LPG Generator Overall Inspection & Verify	30	30-Jun-22	31-Jul-22	656	6A-4000 FS	1A-1100 FS
355		**SA2.6.0.9.2**	**TownGas**	15	15-Nov-21	06-Dec-21	656		
356		6J3L5.1M	Laying Gas Mains from LPG to Tower Gas (TP)	45	15-Nov-21	29-Dec-21	656	5A-5500 FF	6A-4000 FS
357		6J3L5.1M	Gas Meter Relocation & Connection at LPG	10	30-Dec-21	06-Jan-22	656	6A-4000 FS, 6A-4000 FS	1A-1100 FS
358		**SA2.6.0.9.4**	**Building & E&M Works**	601	01-Jul-20	23-Jul-21	650		
359		**SA2.6.0.9.4C**	**Part XI Area-C**	601	01-Jul-20	23-Jul-21	650		
360		**SA2.6.0.9.4C.02**	**LPG Temporary Plant**	601	01-Jul-20	23-Jul-21	650		
361		6J4L1.C2.0	UR1/DG Hyper/B01 C Relocation	15	08-Jul-21	23-Jul-21	650	3A-5500 FS	1A-1100 FS
362		6J4L1.C2.0	Absorption Chiller (Optional)	90	01-Jul-20	25-Dec-20	1231	6A-2500 FS	1A-1100 FS
363		**SA2.6.0.9**	**Landscape Works**	613	01-Apr-19	12-Mar-20	891		
364		**SA2.6.0.9.1**	**SENT Area - Tree Removal & Transplanting**	340	01-Apr-19	12-Jun-20	1284		
365		6J3L1	Assess trees condition and subject for transplanting	30	01-Apr-19	30-Apr-19	1284	1A-1100 FS	6A-1100 FS, 6A-1300 FS, 6A-1400 FS
366		6J3L1	Prepare new site to receive trees	90	01-May-19	30-Jul-19	1284	6A-3000 FS	6A-3300 SS
367		6J3L1	Transplant selected trees	120	01-Aug-19	29-Nov-19	1284	6A-3000 FS, 6A-3100, SS	6A-3300 FS
368		6J3L1	Prune trees prior to removal from Cell 4	90	29-Nov-19	29-Jun-20	1284	6A-3300 FS	1A-1100 FS
369		6J3L1	Tree Felling - Part XI	90	01-May-19	30-Jul-19	1384	2A-2000 FS, 3A-1000 FS, 6A-3000 FS	1A-1100 FS
370		**SA2.6.0.9.2**	**SENTX Area - Tree Nursery & Tree Planting**	300	01-May-19	12-Mar-20	891		
371		6J3L2	Trial Nursery	300	01-May-19	24-Feb-20	1174	1A-1000 FS, 5A-1000 SS 30	6A-1300 FS, M1.3, 2 FS
372		6J3L2	Landscaping in New Infrastructure Area	100	01-Jul-20	12-Dec-20	891	6A-3000 FS, 3A-1000 FS	1A-1100 FS

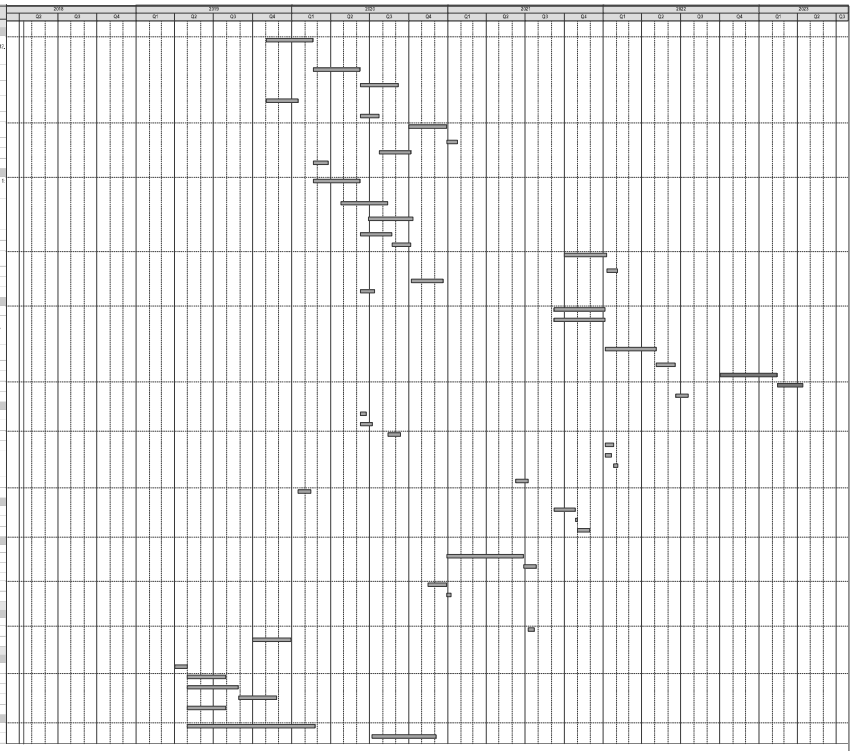

Remaining Work
Critical Remaining Work
◆ Milestone

South-East New Territories Land Fill Extension (SA2-SENTX)
Baseline Programme

GREEN VALLEY LANDFILL LIMITED

Date	Revision	Checked	Approved
11-May-18	SENTX-GVL-W-PB-Z-Z-0001 Rev. B01		
20-Jul-18	SENTX-GVL-W-PB-Z-Z-0001 Rev. B02 (Detailed)		
