Annex A

Work Programme

#	WBS Path	Activity ID	Activity Name	Dur	Start	Finish	Total Float	Predecessor Details	Successor Details
336									
337									
338									
339									
340									
341									
342									
343									
344									
345									
346									
347									
348									
349									
350									
351									
352	SA2.5 Construction (Initial Works)			1153	12-Apr-18	07-Jun-21	705		
353	SA2.5.02 Advance Works & Site Establishment			1148	12-Apr-18	02-Jun-21	35		
354	SA2.5.02.01 Site Establishment & Mobilization			333	12-Apr-18	10-Mar-19	820		
355	5.02.01	52-1000	Site Mobilization for Parts X1 & X2	30	31-Dec-18	29-Jan-19	820	11-1100: FS, 11-1200: FS	52-1300: FS, M 3. 1: FS, M 3. 2: FS
356	5.02.01	52-1100	Site Mobilization for Parts X3, X4 & X5	30	12-Apr-18	11-May-18	1083	11-1300: FS, 11-1400: FS, 11-1500: FS	52-1300: FS, M 3. 1: FF
357	5.02.01	52-1200	Temporary Office for Employer / ER / IC	60	10-Oct-18	08-Dec-18	0	23-1300: FS	11-1700: SS, M 3. 1: FS
358	5.02.01	52-1300	Hoarding and Fencing Works	40	30-Jan-19	10-Mar-19	820	52-1000: FS, 52-1100: FS	32-1500: FS, M10. 1: FS -26, M10. 2: FS -13, M10. 3: FS
359	SA2.5.02.02 Site Survey & Investigation Works for Parts X1 & X2			50	31-Dec-18	18-Feb-19	840		
360	5.02.02	52-1400	Condition Survey	25	31-Dec-18	24-Jan-19	840	11-1100: FS, 11-1200: FS	52-1600: FS
361	5.02.02	52-1500	Topographic Survey	20	31-Dec-18	19-Jan-19	845	11-1100: FS, 11-1200: FS	52-1600: FS
362	5.02.02	52-1600	Site inspection, Review of Condition Survey Report	25	25-Jan-19	18-Feb-19	840	52-1500: FS, 52-1400: FS	32-1500: FS
363	SA2.5.02.03 Site Survey & Investigation Works for Parts X3, X4 & X5			50	12-Apr-18	31-May-18	1103		
364	5.02.03	52-1700	Condition Survey	25	12-Apr-18	06-May-18	1103	11-1300: FS, 11-1400: FS, 11-1500: FS	52-1900: FS
365	5.02.03	52-1800	Topographic Survey	20	12-Apr-18	01-May-18	1108	11-1300: FS, 11-1400: FS, 11-1500: FS	52-1900: FS
366	5.02.03	52-1900	Site inspection, Review of Condition Survey Report	25	07-May-18	31-May-18	1103	52-1700: FS, 52-1800: FS	32-1500: FS
367	SA2.5.02.04 Environmental Monitoring			975	02-Oct-18	02-Jun-21	35		
368	5.02.04	52-2000	Installation of Monitoring Stations & Wells (GP & GW)	120	02-Oct-18	29-Jan-19	0	23-1600: FS	52-2200: SS 60
369	5.02.04	52-2100	Installation of Monitoring Stations & Wells (GP & GW) on Buttress Wall	120	02-Oct-18	29-Jan-19	0	23-1600: FS	52-2200: SS 60
370	5.02.04	52-2200	Conduct Baseline Monitoring for Construction (one month)	30	01-Dec-18	30-Dec-18	0	52-2000: SS 60, 52-2100: SS 60	11-1100: FS
371	5.02.04	52-2300	Conduct Baseline Monitoring for Operation (one year)	365	03-Jun-20	02-Jun-21	35	32-1500: FS -400, 53-4500: FS	12-1400: FS
372	SA2.5.03 Civil Engineering Works			748	13-Jan-19	29-Jan-21	834		
373	SA2.5.03.0 Buttress Wall			475	02-Mar-19	18-Jun-20	83		
374	5.03.0	53-1000	Section adj. SENT	300	13-Apr-19	06-Feb-20	96	11-1300: FS, 23-2500: FS, 53-3000: FS, 31-1200: FS, 11-1400: FS	53-1100: FS, 53-1300: FS, 53-3100: FS, M 3. 5: FS -150, M 3. 7: FS
375	5.03.0	53-1100	Diversion of SENT Landfill Gas Pipe	45	07-Feb-20	22-Mar-20	96	23-2500: FS, 53-1000: FS	53-1300: FS, 54-4000: FS, M 3. 3: FS
376	5.03.0	53-1200	Section at Cell 4	400	02-Mar-19	04-Apr-20	83	11-1300: FS, 23-2500: FS, 53-3000: FS, 11-1400: FS	53-1300: FS, 53-3100: FS, M 3. 7: FS, M 3. 6: FS -200
377	5.03.0	53-1300	Install Landfill Gas Pipe on Buttress Wall	75	05-Apr-20	18-Jun-20	83	41-1500: FS, 53-1100: FS, 53-1200: FS, 53-1000: FS	54-4000: FS
378	SA2.5.03.1 Landfill Cell 1			503	13-Jan-19	29-May-20	214		
379	5.03.1	53-1400	Earth bund (Eastern)	90	04-Aug-19	01-Nov-19	9	11-1100: FS, 23-2500: FS, 53-4200: FS, 53-2800: FS	53-2000: FS, 53-2300: FS, 53-3400: FS, 63-1000: FS, 63-1100: FS, 63-1200: FS, 63-1300: FS, M 4. 2: FS
380	5.03.1	53-1500	Earth bund (Southern)	90	26-Apr-19	24-Jul-19	314	11-1100: FS, 23-2500: FS, 53-2800: FS	53-2000: FS, 53-2200: FS, 53-2300: FS, 53-3400: FS, 53-3700: FS, 53-3800: FS
381	5.03.1	53-1600	Earth bund (Western)	90	13-Jan-19	12-Apr-19	417	11-1100: FS, 23-2500: FS	53-1900: FS, 53-2000: FS, 53-2200: FS, 53-3800: FS
382	5.03.1	53-1700	Intercell bund (Cell 1/2)	75	13-Jan-19	28-Mar-19	432	11-1100: FS, 23-2500: FS	53-2000: FS
383	5.03.1	53-1800	Site Formation	90	13-Jan-19	12-Apr-19	217	11-1100: FS, 23-2500: FS, 31-1300: FS	53-1900: FS, 63-1100: FS, 63-1200: FS, 63-1300: FS, M 4. 1: FS -45
384	5.03.1	53-1900	Pump Station (PS#1X)	45	13-Apr-19	27-May-19	507	53-1800: FS, 53-1600: FS	53-2100: FS, 53-2200: FS
385	5.03.1	53-2000	Lining Works	135	02-Nov-19*	15-Mar-20	214	41-1500: FS, 53-1400: FS, 53-1500: FS, 53-1600: FS, 53-1700: FS	53-2100: FS
386	5.03.1	53-2100	Protective Stone Laying & Leachate Collection Pipe	75	16-Mar-20	29-May-20	214	53-2000: FS, 41-1500: FS, 53-1900: FS	32-1500: FS, 54-2800: FS, M 4. 3: FS
387	5.03.1	53-2200	Install Leachate Force Main	75	25-Jul-19	07-Oct-19	449	53-1500: FS, 53-1600: FS, 41-1500: FS, 53-1900: FS	54-2800: FS
388	5.03.1	53-2300	Install Landfill Gas Pipe on earth bund	55	02-Nov-19	26-Dec-19	258	41-1500: FS, 53-1400: FS, 53-1500: FS	54-4000: FS
389	5.03.1	53-2400	Leachate Pipe Connection (Cell 1 to LTP)	30	09-Mar-20	07-Apr-20	266	23-2500: FS, 54-1000: SS	54-2800: FS
390	SA2.5.03.4 Landfill Cell 4			30	09-Jul-20	07-Aug-20	144		
391	5.03.4	53-2500	Provide Temporary Leachate Pipe on Cell 4 Area	30	09-Jul-20	07-Aug-20	144	23-2500: FS, 63-2600: SS -90	54-2800: FS, M 3. 3: FS
392	SA2.5.03.5 Drainage - Surface Run-Off			740	16-Jan-19	24-Jan-21	839		
393	5.03.5	53-2600	Construct Cut-Off Channel 12A	60	16-Jan-19	16-Mar-19	9	11-1100: FS, 23-2800: FS	53-2700: FS
394	5.03.5	53-2700	Connect Cut-Off Channel 12A to DP6	20	17-Mar-19	05-Apr-19	9	53-2600: FS, 31-1400: FS, 23-1900: FS	53-2800: FS
395	5.03.5	53-2800	Diversion from Existing Trapezoidal Channel into Channel 12A	20	06-Apr-19	25-Apr-19	9	53-2700: FS	53-1400: FS, 53-1500: FS, 53-2900: FS, 63-1000: FS, 63-1900: FS, M 3. 3: FS
396	5.03.5	53-2900	Removal of Existing Trapezoidal Channel along Eastern Bund	30	26-Apr-19	25-May-19	9	53-2800: FS	53-4200: FS
397	5.03.5	53-3000	Cut-Off Channel C4 Diversion to Cut-Off Channel 17-2	45	16-Jan-19	01-Mar-19	83	11-1300: FS, 23-2800: FS	53-1000: FS, 53-1200: FS
398	5.03.5	53-3100	Cut-Off Channel X5 on Buttress Wall, Cell 4, Cell 3	90	05-Apr-20	03-Jul-20	289	53-1000: FS, 53-1200: FS	53-3200: FS
399	5.03.5	53-3200	Temporary Diversion Cut-Off Channel X5 to 12A	20	04-Jul-20	23-Jul-20	289	53-3100: FS, 23-1900: FS	53-3300: FS, M 3. 4: FS
400	5.03.5	53-3300	Culvert X5 (5m long) & Perm Connection of Cut-Off Channel X5	30	26-Dec-20	24-Jan-21	134	53-4100: FF, 63-1900: FS, 53-3200: FS	32-1500: FS
401	5.03.5	53-3400	Construct Perimeter Channel X6 on Eastern Bund & Southern Bund of Cell 1	50	02-Nov-19	21-Dec-19	249	53-1400: FS, 53-1500: FS	53-3500: FS
402	5.03.5	53-3500	Construct Perimeter Channel X6 on Eastern Bund of Cell 2	50	20-Feb-20	09-Apr-20	189	63-1000: FS, 53-3400: FS	53-3600: FS
403	5.03.5	53-3600	Construct Perimeter Channel X6 Eastern Bund of Cell 3	50	09-Jun-20	28-Jul-20	129	63-1900: FS, 53-3500: FS	53-3900: FS
404	5.03.5	53-3700	Culvert X6 (25m long) at Cell 1 Southern Bund	75	25-Jul-19	07-Oct-19	1314	53-1500: FS	
405	5.03.5	53-3800	Perimeter Channel (X9B) at Cell 1 Southern & Western Bund	45	25-Jul-19	07-Sep-19	1344	53-1500: FS, 53-1600: FS	
406	5.03.5	53-3900	Drop Inlet & Culvert (X9) - 21m long	180	29-Jul-20	24-Jan-21	129	11-1100: FS, 23-1900: FS, 53-3600: FS	53-4000: FF, 53-4100: FF, 53-6000: FS, M 9. 1: FS -90, M 9. 2: FS
407	5.03.5	53-4000	Sediment Trap (ST)	180	29-Jul-20	24-Jan-21	129	11-1100: FS, 23-1900: FS, 11-1200: FS, 53-3900: FF	53-6000: FS, M 9. 3: FS -90, M 9. 4: FS
408	5.03.5	53-4100	Dual Culvert 74m long (connect to DP4)	180	29-Jul-20	24-Jan-21	129	11-1100: FS, 11-1200: FS, 23-1900: FS, 53-3900: FF	53-3300: FF, 53-6000: FS, M 9. 1: FS -90, M 9. 2: FS
409	SA2.5.03.6 Drainage - Ground Water			200	26-May-19	11-Dec-19	209		
410	5.03.6	53-4200	Construct Groundwater Collection Pipe along Cells X1 & X2 Eastern Bund	70	26-May-19	03-Aug-19	9	11-1100: FS, 23-1600: FS, 53-2900: FS	53-1400: FS, 53-4300: FS, 63-1000: FS, 63-1900: FS
411	5.03.6	53-4300	Construct Groundwater Collection Pipe along Cell X3 Eastern Bund	50	04-Aug-19	22-Sep-19	159	53-4200: FS	53-4400: FS, 63-1900: FS
412	5.03.6	53-4400	Construct Groundwater Collection Pipe along Intercell Bund X2/X3	50	23-Sep-19	11-Nov-19	209	53-4300: FS	53-4500: FS, 63-1200: FS
413	5.03.6	53-4500	Construct Manhole MH-X1	30	12-Nov-19	11-Dec-19	209	53-4400: FS	52-2300: FS, M 9. 5: FS
414	SA2.5.03.7 Utilities - Distribution within New Infrastructure Area			391	11-Aug-19	04-Sep-20	276		
415	5.03.7	53-4600	Power Supply HV Works (Transformer & HV switchgear)	5	30-Jun-20	04-Jul-20	0	54-3000: FS	12-1200: FS
416	5.03.7	53-4700	Power Distribution, LV Power Supply Works	2	05-Jul-20	06-Jul-20	0	54-3100: FS, 12-1200: FS	12-1000: FS
417	5.03.7	53-4800	Sewerage (Collection to LTP)	60	07-Jul-20	04-Sep-20	271	54-1000: FS, 54-3100: FS, 54-3300: FS, 54-4100: FS	12-1100: FS, 53-6100: FS
418	5.03.7	53-4900	Sewerage (Discharge to Site Boundary)	60	07-Jul-20	04-Sep-20	271	54-1000: FS, 54-4100: FS, 54-4600: FS	12-1100: FS, 53-6100: FS
419	5.03.7	53-5000	Lighting Provision	30	07-Jul-20	05-Aug-20	6	54-1000: FS, 54-4100: FS, 54-4600: FS	12-1100: FS, 32-2100: FS
420	5.03.7	53-5100	Fire Services	115	12-Mar-20	04-Jul-20	2	53-6800: FS	12-1000: FS
421	5.03.7	53-5200	Water Supply (Fresh & Salt)	115	12-Mar-20	04-Jul-20	338	53-6600: FS, 53-6700: FS	12-1100: FS
422	5.03.7	53-5300	Telecom & Network	45	11-Aug-19	24-Sep-19	622	53-6400: FS	12-1100: FS
423	5.03.7	53-5400	Gas Network (LFG to LTP)	15	22-Jun-20	06-Jul-20	176	54-1000: FF	54-2800: FS
424	SA2.5.03.8 Utilities - Works Associated with Utilities Undertakers			703	27-Feb-19	29-Jan-21	129		
425	SA2.5.03.8.U1_CLP			459	27-Feb-19	30-May-20	43		
426	5.03.8.U1	53-5500	Excavate Trench for CLP Cable	100	13-May-19	20-Aug-19	194	23-2900: FS	53-5800: FS, 54-1000: SS, 54-4100: SS, 54-4600: SS, M10. 1: FS -60, M10. 2: FS -30, M10. 3: FS
427	5.03.8.U1	53-5600	Backfill Trench after CLP Cable Laying	30	01-May-20	30-May-20	43	53-5800: FS	54-1000: FF, 54-4100: FF, 54-4600: FF
428	5.03.8.U1	53-5700	CLP Cable Laying (from CLP Substation to Site Boundary)	200	27-Feb-19	14-Sep-19	229	32-2400: FS	54-3000: FS
429	5.03.8.U1	53-5800	CLP Cable Laying (from Site Boundary to HV Switchroom)	60	02-Mar-20	30-Apr-20	0	53-5500: FS, 54-2900: FS, 32-2400: FS, 53-5900: FF 15	53-5600: FS, 54-3000: FS
430	5.03.8.U1	53-5900	CLP HV associated equipment installation	120	18-Dec-19	15-Apr-20	0	54-2900: FS, 32-2400: FS	53-5800: FF 15
431	SA2.5.03.8.U2_DSD			147	05-Sep-20	29-Jan-21	129		
432	5.03.8.U2	53-6000	Connection to Storm Drain System	5	25-Jan-21	29-Jan-21	129	53-4100: FS, 53-4000: FS, 53-3900: FS	32-1500: FS
433	5.03.8.U2	53-6100	Connection to Foul Drain System	5	05-Sep-20	09-Sep-20	271	53-4800: FS, 53-4900: FS	32-1500: FS
434	SA2.5.03.8.U3_Telecom			100	13-May-19	20-Aug-19	327		
435	5.03.8.U3	53-6200	Excavate Trench for PCCW	60	13-May-19	11-Jul-19	307	23-2900: FS	53-6400: FS, 54-1000: SS, 54-4100: SS, 54-4600: SS, M10. 1: FS -40, M10. 2: FS -20, M10. 3: FS
436	5.03.8.U3	53-6300	Backfill Trench after PCCW Cable Laying	10	11-Aug-19	20-Aug-19	327	53-6400: FS	54-1000: FF, 54-4100: FF, 54-4600: FF
437	5.03.8.U3	53-6400	Laying Cables & Connection	30	12-Jul-19	10-Aug-19	327	53-6200: FS	53-5300: FS, 53-6300: FS
438	SA2.5.03.8.U4_WSD			304	13-May-19	11-Mar-20	338		
439	5.03.8.U4	53-6500	Install Watermain & Piping for Water Supplies	60	13-May-19	11-Jul-19	216	23-2900: FS	53-6600: FS, 53-6700: FS, 53-6800: FS, 53-6900: FS
440	5.03.8.U4	53-6600	Connection for Fresh Water & Meter Installation	30	11-Feb-20	11-Mar-20	338	53-6500: FS, 32-2300: FS	53-5200: FS
441	5.03.8.U4	53-6700	Connection for Salt Water	30	11-Feb-20	11-Mar-20	338	53-6500: FS, 32-2300: FS	53-5200: FS
442	5.03.8.U4	53-6800	Connection for Fire Services	30	11-Feb-20	11-Mar-20	2	53-6500: FS, 32-2300: FS	53-5100: FS
443	5.03.8.U4	53-6900	Connection for Cooling Tower & Meter Installation	30	11-Feb-20	11-Mar-20	117	53-6500: FS, 32-2300: FS	54-2700: FS, 54-3900: FS
444	SA2.5.03.8.U5_HyD Lighting			120	07-Jul-20	03-Nov-20	216		
445	5.03.8.U5	53-7000	Installation of Public Street Lighting / Handover	120	07-Jul-20	03-Nov-20	216	54-4100: FS, 54-4600: FS, 54-1000: FS	32-1500: FS
446	SA2.5.04 Building Construction, incl. E&M and System Installation, and T&C			890	31-Dec-18	07-Jun-21	0		
447	SA2.5.04.A Part X1 Area A			554	31-Dec-18	06-Jul-20	36		
448	5.04.A	54-1000	General Area & Access Road	120	09-Mar-20	06-Jul-20	6	23-1300: FS, 53-5500: SS, 53-5600: FF, 53-6200: SS, 53-6300: FF, 12-1000: FF, 11-1100: FS, 54-1100: FF, 54-1800: FF	32-2100: FS, 53-2400: SS, 53-4800: FS, 53-4900: FS, 53-5000: FS, 53-5400: FF, 53-7000: FS, 68-1700: FS
449	5.04.A	54-1100	Carpark & Supporting Area	60	31-Dec-18	28-Feb-19	64	23-1300: FS, 11-1100: FS	32-1500: FS, M 5.11: FS -30, M 5.12: FS, 54-1000: FF, 54-1800: FS
450	5.04.A	54-1200	Diesel Fuel Tanks	60	08-May-20	06-Jul-20	36	23-1300: FS, 23-5200: FS, 12-1000: FF, 11-1100: FS	32-2200: FS
451	5.04.A	54-1300	EPD Building	270	30-Apr-19	24-Jan-20	44	23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1700: SS 60	32-2100: FS, M 5. 4: FS -135, M 5. 5: FS, 12-1000: FS, 54-1400: SS 60
452	5.04.A	54-1400	Fire Service Tank	270	29-Jun-19	24-Mar-20	44	23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1300: SS 60	32-2100: FS, M 5.10: FS, 12-1000: FS, 54-1600: SS 60
453	5.04.A	54-1500	GVL Building	300	31-Dec-18	26-Oct-19	44	23-1300: FS, 23-5200: FS, 11-1100: FS	32-2100: FS, M 5. 1: SF 30, M 5. 2: SF 150, M 5. 3: FS, 54-1700: SS 60
454	5.04.A	54-1600	Laboratory Building	270	28-Aug-19	23-May-20	44	23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1400: SS 60	32-2100: FS, M 5. 6: FS -135, M 5. 7: FS, 12-1000: FS, 32-2200: FS
455	5.04.A	54-1700	Maintenance Building & Area	270	01-Mar-19	25-Nov-19	44	23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1500: SS 60	32-2100: FS, M 5. 8: FS -135, M 5. 9: FS, 12-1000: FS, 54-1300: SS 60
456	5.04.A	54-1800	Storage Facility & Area	60	01-Mar-19	29-Apr-19	64	23-1300: FS, 11-1100: FS, 54-1100: FS	32-1500: FS, M 5.11: FS -30, M 5.12: FS, 54-1000: FF, 54-2000: FS
457	5.04.A	54-1900	Waste Oil Tanks	90	08-Apr-20	06-Jul-20	36	23-1300: FS, 23-5200: FS, 12-1000: FF, 11-1100: FS	32-2200: FS
458	5.04.A	54-2000	Water Service House	60	30-Apr-19	28-Jun-19	64	23-1300: FS, 23-5200: FS, 11-1100: FS, 54-1800: FS	32-2100: FS, M 5.10: FS, 12-1000: FS, 54-4400: FS
459	SA2.5.04.B Part X1 Area B			890	31-Dec-18	07-Jun-21	0		
460	SA2.5.04.B.1 BioPlant Building			330	17-Jan-19	12-Dec-19	243		
461	5.04.B.1	54-2100	LTP BioPlant Building	330	17-Jan-19	12-Dec-19	243	23-1300: FS, 23-5200: FS, 23-3200: FS, 11-1100: FS, 31-1000: FS	32-2100: FS, 32-2200: FS, M 6. 2: FS -165, M 6. 3: FS
462	SA2.5.04.B.2 Leachate Treatment Plant			589	31-Dec-18	10-Aug-20	21		
463	5.04.B.2	54-2200	Main Plant Area included Civil works	274	31-Dec-18	30-Sep-19	0	23-1300: FS, 23-3200: FS, 11-1100: FS	54-2300: FS, 54-2400: FS, 54-2500: FS, 64-1100: FS, M 6. 1: SF 30, M 6. 4: FS -137, M 6. 5: FS
464	5.04.B.2	54-2300	MEP Installation	220	01-Oct-19	07-May-20	0	41-2100: FS, 41-1800: FS, 22-2100: FS, 54-2200: FS, 11-1100: FS	12-1000: FS 60, 32-1900: FS, 54-2600: FS, M 6. 8: FS -110, M 6. 9: FS, 32-2200: FS
465	5.04.B.2	54-2400	SBR Tanks	100	01-Oct-19	08-Jan-20	236	41-2400: FS, 54-2200: FS	54-2600: FS, M 6. 6: FS
466	5.04.B.2	54-2500	Ammonia Stripper	315	01-Oct-19	10-Aug-20	21	41-3000: FS, 54-2200: FS	54-2600: FS, M 6. 8: FS -150, M 6. 9: FS
467	SA2.5.04.B.3 LTP - Test & Commission			301	11-Aug-20	07-Jun-21	0		
468	5.04.B.3	54-2600	Dry testing	45	11-Aug-20	24-Sep-20	21	54-2300: FS, 54-2400: FS, 54-2500: FS	23-6600: FS -150, 23-6900: SS, 54-2700: FS, M11. 1: FS
469	5.04.B.3	54-2700	Wet testing	75	25-Sep-20	08-Dec-20	21	54-2600: FS, 12-1200: FS, 53-6900: FS, 31-2200: FS, 23-6800: FS	54-2800: FS, M11. 2: FS
470	5.04.B.3	54-2800	Operational testing	160	30-Dec-20	07-Jun-21	0	54-2700: FS, 53-2400: FS, 53-2500: FS, 53-2100: FS, 53-2200: FS, 63-1700: FS, 63-2600: FS, 53-5400: FS, 54-4000: FS	32-1500: FS, M11. 3: FS, M11. 4: FS
471	SA2.5.04.C Part X1 Area C			730	31-Dec-18	29-Dec-20	0		
472	SA2.5.04.C.1 LFG - Power Supply Building			530	17-Jan-19	29-Jun-20	5		
473	5.04.C.1	54-2900	LFG Building (with Transformer Room)	335	17-Jan-19	17-Dec-19	0	23-1300: FS, 23-3500: FS, 11-1100: FS, 31-1000: FS	53-5800: FS, 53-5900: FS, 54-3000: FS, 54-3100: FS, M 7. 6: FS
474	5.04.C.1	54-3000	Transformer & HV Switchgear Installation	60	01-May-20	29-Jun-20	0	54-2900: FS, 41-1200: FS, 53-5800: FS, 53-5700: FS	53-4600: FS, M 7. 4: FS -30, M 7. 5: FS, M 7. 5: FF
475	5.04.C.1	54-3100	MEP Installation, with T&C	75	18-Dec-19	01-Mar-20	125	54-2900: FS	32-1400: FS, 32-2100: FS, 53-4700: FS, 53-4800: FS, M 7. 4: FS -30, M 7. 5: FS
476	SA2.5.04.C.2 LFG Treatment Plant			554	31-Dec-18	06-Jul-20	0		
477	5.04.C.2	54-3200	Main Plant Area included Civil Works	384	31-Dec-18	18-Jan-20	0	23-3500: FS, 11-1100: FS	54-3300: FS, 54-3400: FS, 54-3500: FS, 54-3600: FS, 54-3700: FS, 54-3800: FS, M 7. 1: SF 30, M 7. 2: FS -200, M 7. 3: FS
478	5.04.C.2	54-3300	MEP Installation	170	19-Jan-20	06-Jul-20	0	54-3200: FS, 12-1000: FF	32-2000: FS, 53-4800: FS, 54-3900: FS, M 7. 4: FS -80, M 7. 5: FS
479	5.04.C.2	54-3400	GHS600 Blower 601 A&B Relocation	15	19-Jan-20	02-Feb-20	155	23-5800: FS, 54-3200: FS	54-3900: FS, M 7. 4: FS -8, M 7. 5: FS
480	5.04.C.2	54-3500	Pre-treatment	60	19-Jan-20	18-Mar-20	110	41-3900: FS, 54-3200: FS	54-3900: FS, M 7. 4: FS -30, M 7. 5: FS
481	5.04.C.2	54-3600	Flares (incl. PLC control, interlink to Towngas PF & LTP)	125	19-Jan-20	22-May-20	45	41-3300: FS, 54-3200: FS	54-3900: FS, M 7. 4: FS -60, M 7. 5: FS
482	5.04.C.2	54-3700	LFG Engine (incl. on-grid protection, PLC control, turning)	110	21-Feb-20	09-Jun-20	27	41-3600: FS, 54-3200: FS	54-3900: FS, M 7. 4: FS -60
483	5.04.C.2	54-3800	Cooling System	45	19-Jan-20	03-Mar-20	125	22-1500: FS, 54-3200: FS	54-3900: FS, M 7. 4: FS -25, M 7. 5: FS
484	SA2.5.04.C.3 LFG - Test & Commission			176	07-Jul-20	29-Dec-20	0		
485	5.04.C.3	54-3900	MEP Testing	65	07-Jul-20	09-Sep-20	0	54-3400: FS, 54-3500: FS, 54-3600: FS, 54-3700: FS, 54-3800: FS, 12-1200: FS, 53-6900: FS, 31-2200: FS, 54-3300: FS	23-7000: SS -150, 23-7300: SS, 54-4000: FS, M11. 1: FS -30, M11. 2: FS
486	5.04.C.3	54-4000	Operational Testing	111	10-Sep-20	29-Dec-20	0	53-1300: FS, 63-2700: FS, 63-1800: FS, 53-2300: FS, 53-1100: FS, 54-3900: FS, 23-7200: FS	32-1500: FS, 54-2800: FS, 63-4800: FF, 63-4900: FS, 63-4600: FS, M11. 3: FS, M11. 4: FS
487	SA2.5.04.D Part X1 Area D			374	29-Jun-19	06-Jul-20	6		
488	5.04.D	54-4100	General Area & Access Road	120	09-Mar-20	06-Jul-20	6	23-1300: FS, 53-5500: SS, 53-5600: FF, 53-6200: SS, 53-6300: FF, 12-1000: FF, 11-1100: FS	32-2100: FS, 53-4800: FS, 53-4900: FS, 53-5000: FS, 53-7000: FS, M 8. 5: FS
489	5.04.D	54-4200	VWF Building	120	28-Oct-19	24-Feb-20	63	23-1300: FS, 23-5200: FS, 41-4500: FS, 11-1100: FS, 54-4300: SS 60	32-2100: FS, M 8. 4: FS, M 8. 6: FS -60, M 8. 7: FS, 12-1000: FS, 54-4500: SS 60
490	5.04.D	54-4300	Weighbridge	75	29-Aug-19	11-Nov-19	63	41-4200: FS, 23-1300: FS, 23-5200: FS, 11-1100: FS, 54-4400: SS 60	32-2100: FS, M 8. 6: FS -40, M 8. 7: FS, 54-4200: SS 60
491	5.04.D	54-4400	Weighmaster House	120	29-Jun-19	26-Oct-19	64	23-1300: FS, 23-5200: FS, 11-1100: FS, 54-2000: FS	32-2100: FS, M 8. 1: FS, 12-1000: FS, 54-4300: SS 60
492	5.04.D	54-4500	Wheel Wash Bath	75	27-Dec-19	10-Mar-20	63	23-1300: FS, 23-5200: FS, 41-4500: FS, 11-1100: FS, 54-4200: SS 60	32-2100: FS, M 8. 3: FS, 12-1000: FS, 54-4700: SS 30
493	SA2.5.04.E Part X1 Area E & Part X2			163	26-Jan-20	06-Jul-20	6		
494	5.04.E	54-4600	General Area & Access Road	120	09-Mar-20	06-Jul-20	6	53-5500: SS, 53-5600: FF, 53-6200: SS, 53-6300: FF, 12-1000: FF, 11-1100: FS, 11-1200: FS	32-2100: FS, 53-4900: FS, 53-5000: FS, 53-7000: FS
495	5.04.E	54-4700	Guard House & Entrance Gate	100	26-Jan-20	04-May-20	63	23-1300: FS, 23-5200: FS, 11-1100: FS, 11-1200: FS, 54-4500: SS 30	32-2100: FS, M 8. 2: FS, 12-1000: FS
496	SA2.5.08 Landscape Works - Advance Screen Planting in CWB Country Park			270	01-Apr-19	26-Dec-19	529		
497	SA2.5.08.N Area N			270	01-Apr-19	26-Dec-19	529		
498	5.08.N	58-1000	Advance Screen Planting	90	01-Apr-19*	29-Jun-19	529	23-7900: FS, 31-1100: FS, 11-1500: FS	14-1800: SS -60, 58-1100: SS, 68-1600: SS 30, M 3. 2: FS
499	5.08.N	58-1100	Establishment of Screen Planting	270	01-Apr-19*	26-Dec-19	529	58-1000: SS, 14-1800: FS	32-1500: FS
500	SA2.5.08.S Area S			270	01-Apr-19	26-Dec-19	529		
501	5.08.S	58-1200	Advance Screen Planting	90	01-Apr

#	WBS Path	Activity ID	Activity Name	Dur	Start	Finish	Total Float	Predecessor Details	Successor Details
509	**SA2.6.03**		**Civil Engineering Works**	1259	02-Nov-19	13-Apr-23	30		
510	**SA2.6.03.2**		**Landfill Cell 2**	449	02-Nov-19	23-Jan-21	810		
511	6.03.2	63-1000	Earth bund (Eastern)	110	02-Nov-19	19-Feb-20	9	11-1100: FS, 23-2500: FS, 53-4200: FS, 53-1400: FS, 53-2800: FS	53-3500: FS, 63-1500: FS, 63-1800: FS, 63-1900: FS, 63-2000: FS, 63-2100: FS, 63-2200: FS, M12. 1: FS -50, M12. 2: FS, 63-1100: FS
512	6.03.2	63-1100	Earth bund (Western)	110	20-Feb-20	08-Jun-20	84	11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: FS, 63-1000: FS	63-1400: FS, 63-1500: FS, 63-1700: FS, 63-3500: FS, 63-3600: FS, 63-1200: FS
513	6.03.2	63-1200	Intercell bund (Cell 2/3)	90	09-Jun-20	06-Sep-20	734	11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: FS, 53-4400: FS, 63-1100: FS	63-1500: FS
514	6.03.2	63-1300	Site Formation	75	02-Nov-19	15-Jan-20	14	11-1100: FS, 23-2500: FS, 53-1800: FS, 53-1400: FS	63-1400: FS, 63-4200: FS
515	6.03.2	63-1400	Pump Station (PS#2X)	45	09-Jun-20	23-Jul-20	84	63-1300: FS, 63-1100: FS	63-1600: FS, 63-1700: FS
516	6.03.2	63-1500	Lining Works	90	01-Oct-20*	29-Dec-20	710	41-1500: FS, 63-1000: FS, 63-1100: FS, 63-1200: FS	63-1600: FS, M12. 3: FS, 63-2400: FS
517	6.03.2	63-1600	Protective Stone Laying & Leachate Collection Pipe	25	30-Dec-20	23-Jan-21	810	63-1500: FS, 41-1500: FS, 63-1400: FS	32-1600: FS, M12. 3: FS
518	6.03.2	63-1700	Install Leachate Force Main	75	24-Jul-20	06-Oct-20	84	63-1100: FS, 41-1500: FS, 63-1400: FS	54-2800: FS, M12. 3: FS
519	6.03.2	63-1800	Install Landfill Gas Pipe on earth bund	35	20-Feb-20	25-Mar-20	168	41-1500: FS, 63-1000: FS	54-4000: FS, M12. 3: FS
520	**SA2.6.03.3**		**Landfill Cell 3**	714	20-Feb-20	02-Feb-22	435		
521	6.03.3	63-1900	Earth bund (Eastern)	110	20-Feb-20	08-Jun-20	9	11-1100: FS, 53-4200: FS, 63-1000: FS, 53-4300: FS, 53-2800: FS, 63-4200: FS	53-3300: FS, 53-3600: FS, 63-2400: FS, 63-2700: FS, M12. 1: FS -50, M12. 2: FS, 63-2000: FS -45, 63-2200: FS
522	6.03.3	63-2000	Earth bund (Western)	110	25-Apr-20	12-Aug-20	19	11-1100: FS, 63-1000: FS, 63-1900: FS -45	63-2300: FS, 63-2400: FS, 63-2600: FS, 63-3700: FS, 63-2100: FS -45
523	6.03.3	63-2100	Intercell bund (Cell 3/4)	105	29-Jun-20	11-Oct-20	789	11-1100: FS, 63-1000: FS, 63-4200: FS, 63-2000: FS -45	63-2400: FS
524	6.03.3	63-2200	Site Formation	75	09-Jun-20	22-Aug-20	9	11-1100: FS, 63-1000: FS, 63-1900: FS	63-2300: FS
525	6.03.3	63-2300	Pump Station (PS#3X)	45	23-Aug-20	06-Oct-20	9	63-2200: FS, 63-2000: FS	63-2500: FS, 63-2600: FS
526	6.03.3	63-2400	Lining Works	100	01-Oct-21*	08-Jan-22	435	41-1500: FS, 63-1900: FS, 63-2000: FS, 63-2100: FS, 63-1500: FS	63-2500: FS, M12. 3: FS
527	6.03.3	63-2500	Protective Stone Laying & Leachate Collection Pipe	25	09-Jan-22	02-Feb-22	435	63-2400: FS, 41-1500: FS, 63-2300: FS	32-1700: FS, M12. 3: FS
528	6.03.3	63-2600	Install Leachate Force Main	75	07-Oct-20	20-Dec-20	9	63-2000: FS, 41-1500: FS, 63-2300: FS	53-2500: SS -90, 54-2800: FS, M12. 3: FS
529	6.03.3	63-2700	Install Landfill Gas Pipe on earth bund	35	09-Jun-20	13-Jul-20	58	41-1500: FS, 63-1900: FS	54-4000: FS, M12. 3: FS
530	**SA2.6.03.4**		**Landfill Cell 4**	584	07-Sep-21	13-Apr-23	30		
531	6.03.4	63-2800	Remaining Portion of Buttress Wall	120	07-Sep-21	04-Jan-22	494	62-1000: FS	
532	6.03.4	63-2900	Earth bund (Western) incl. MSE Wall	120	07-Sep-21	04-Jan-22	239	62-1000: FS	63-3000: FS, 63-3100: FS, 63-3200: FS, 63-3400: FS, 63-3800: FS, 63-3900: FS, 63-4100: SS -90, M 9. 6: FS -60, M 9. 7: FS -30, M 9. 8: FS
533	6.03.4	63-3000	Site Formation	120	05-Jan-22	04-May-22	239	62-1000: FS, 62-1100: FS, 62-1200: FS, 63-2900: FS, 63-4100: FS	63-3100: FS
534	6.03.4	63-3100	Pump Station (PS#4X)	45	05-May-22	18-Jun-22	239	63-3000: FS, 63-2900: FS	63-3300: FS, 63-3400: FS
535	6.03.4	63-3200	Lining Works	135	01-Oct-22*	12-Feb-23	0	41-1500: FS, 63-2900: FS	63-3300: FS, M12. 6: FS
536	6.03.4	63-3300	Protective Stone Laying & Leachate Collection Pipe	60	13-Feb-23	13-Apr-23	0	41-1500: FS, 63-3200: FS, 63-3100: FS	12-1900: FS, 32-1800: FS, M12. 6: FS
537	6.03.4	63-3400	Install Leachate Force Main & Remove Temporary Leachate Pipe	30	19-Jun-22	18-Jul-22	269	41-1500: FS, 63-2900: FS, 63-3100: FS	12-1900: FS, 32-1800: FS, M12. 6: FS
538	**SA2.6.03.5**		**Drainage - Surface Run-Off**	750	16-Jan-20	03-Feb-22	464		
539	6.03.5	63-3500	Perimeter Channel (X9A) at Cell 2 Western Bund	15	09-Jun-20	23-Jun-20	1054	63-1100: FS	12-1900: FS
540	6.03.5	63-3600	Perimeter Channel (X10A) at Cell 2 Western Bund	30	09-Jun-20	08-Jul-20	1029	63-1100: FS	63-4000: FS
541	6.03.5	63-3700	Perimeter Channel (X10A) at Cell 3 Western Bund	30	13-Aug-20	11-Sep-20	964	63-2000: FS	63-4000: FS
542	6.03.5	63-3800	Perimeter Channel (X10A) at Cell 4 Western Bund	20	05-Jan-22	24-Jan-22	464	63-2900: FS	63-4000: FS
543	6.03.5	63-3900	Perimeter Channel (X10C) at Cell 4 Western Bund	15	05-Jan-22	19-Jan-22	469	63-2900: FS	63-4000: FS
544	6.03.5	63-4000	Connection to Existing DP3	10	25-Jan-22	03-Feb-22	464	63-3900: FS, 63-3600: FS, 63-3700: FS, 63-3800: FS	12-1900: FS
545	6.03.5	63-4100	Remove Cut-Off Channel C-7 at bottom of Buttress Wall	30	09-Jun-21	08-Jul-21	419	63-2900: SS -90	63-3000: FS
546	6.03.5	63-4200	Temporary Channel (X7T) at SENT Infrastructure Area	30	16-Jan-20	14-Feb-20	14	63-1300: FS	63-1900: FS, 63-2100: FS
547	**SA2.6.03.6**		**Drainage - Ground Water**	85	07-Sep-21	30-Nov-21	529		
548	6.03.6	63-4300	Construct Temporary Channel (TC-1), from MH-1 to Existing UC-825	50	07-Sep-21	26-Oct-21	529	23-1900: FS, 11-1300: FS, 62-1000: FS	63-4400: FS
549	6.03.6	63-4400	Divert GW at MH-1 to TC-1	5	27-Oct-21	31-Oct-21	529	63-4300: FS	63-4500: FS, M 9. 9: FS
550	6.03.6	63-4500	Reconnection of GWCP across Cell 4	30	01-Nov-21	30-Nov-21	529	62-1100: FS, 62-1200: FS, 63-4400: FS	12-1900: FS
551	**SA2.6.03.8**		**Utilities - Works Associated with Utilities Undertakers**	255	15-Nov-20	27-Jul-21	655		
552	**SA2.6.03.8.U1**		**CLP**	210	30-Dec-20	27-Jul-21	655		
553	6.03.8.U1	63-4600	LFG Generator On-grid Testing	180	30-Dec-20	27-Jun-21	655	32-2500: FS, 12-1200: FS, 54-4000: FS	63-4700: FS
554	6.03.8.U1	63-4700	LFG Generator On-grid Inspection & Verify	30	28-Jun-21	27-Jul-21	655	63-4600: FS	12-1900: FS
555	**SA2.6.03.8.U6**		**TownGas**	55	15-Nov-20	08-Jan-21	855		
556	6.03.8.U6	63-4800	Laying Gas Mains (from LFG to Town Gas PF)	45	15-Nov-20	29-Dec-20	855	54-4000: FF	63-4900: FS
557	6.03.8.U6	63-4900	Gas Meter Relocation & Connection at LFG	10	30-Dec-20	08-Jan-21	855	63-4800: FS, 54-4000: FS	12-1900: FS
558	**SA2.6.04**		**Building & E&M Works**	661	01-Oct-19	22-Jul-21	660		
559	**SA2.6.04.C**		**Part X1 Area C**	661	01-Oct-19	22-Jul-21	660		
560	**SA2.6.04.C.02**		**LFG Treatment Plant**	661	01-Oct-19	22-Jul-21	660		
561	6.04.C.02	64-1000	GHS600 Blower 601 C Relocation	15	08-Jul-21	22-Jul-21	660	32-1500: FS	12-1900: FS
562	6.04.C.02	64-1100	Absorption Chiller (Optional)	90	01-Oct-19	29-Dec-19	1231	54-2200: FS	12-1900: FS
563	**SA2.6.08**		**Landscape Works**	613	01-Apr-19	03-Dec-20	891		
564	**SA2.6.08.1**		**SENT Area - Tree Removal & Transplanting**	240	01-Apr-19	26-Nov-19	1264		
565	6.08.1	68-1000	Access trees condition and select for transplanting	30	01-Apr-19*	30-Apr-19	1264	14-1300: FS	68-1100: FS, 68-1200: FS, 68-1400: FS
566	6.08.1	68-1100	Prepare new site to receive trees	90	01-May-19	29-Jul-19	1264	68-1000: FS	68-1200: SS
567	6.08.1	68-1200	Transplant selected trees	120	01-May-19	28-Aug-19	1264	68-1000: FS, 68-1100: SS	68-1300: FS
568	6.08.1	68-1300	Prune trees prior to removal from Cell 4	90	29-Aug-19	26-Nov-19	1264	68-1200: FS	12-1900: FS
569	6.08.1	68-1400	Tree Felling - Part X3	90	01-May-19	29-Jul-19	1384	23-8200: FS, 31-1600: FS, 68-1000: FS	12-1900: FS
570	**SA2.6.08.2**		**SENTX Area - Trial Nursery & Tree Planting**	583	01-May-19	03-Dec-20	891		
571	6.08.2	68-1600	Trial Nursery	300	01-May-19	24-Feb-20	1174	14-1800: FS, 58-1000: SS 30	12-1900: FS, M 3. 2: FS
572	6.08.2	68-1700	Landscaping in New Infrastructure Area	150	07-Jul-20	03-Dec-20	891	54-1000: FS, 23-7600: FS	12-1900: FS

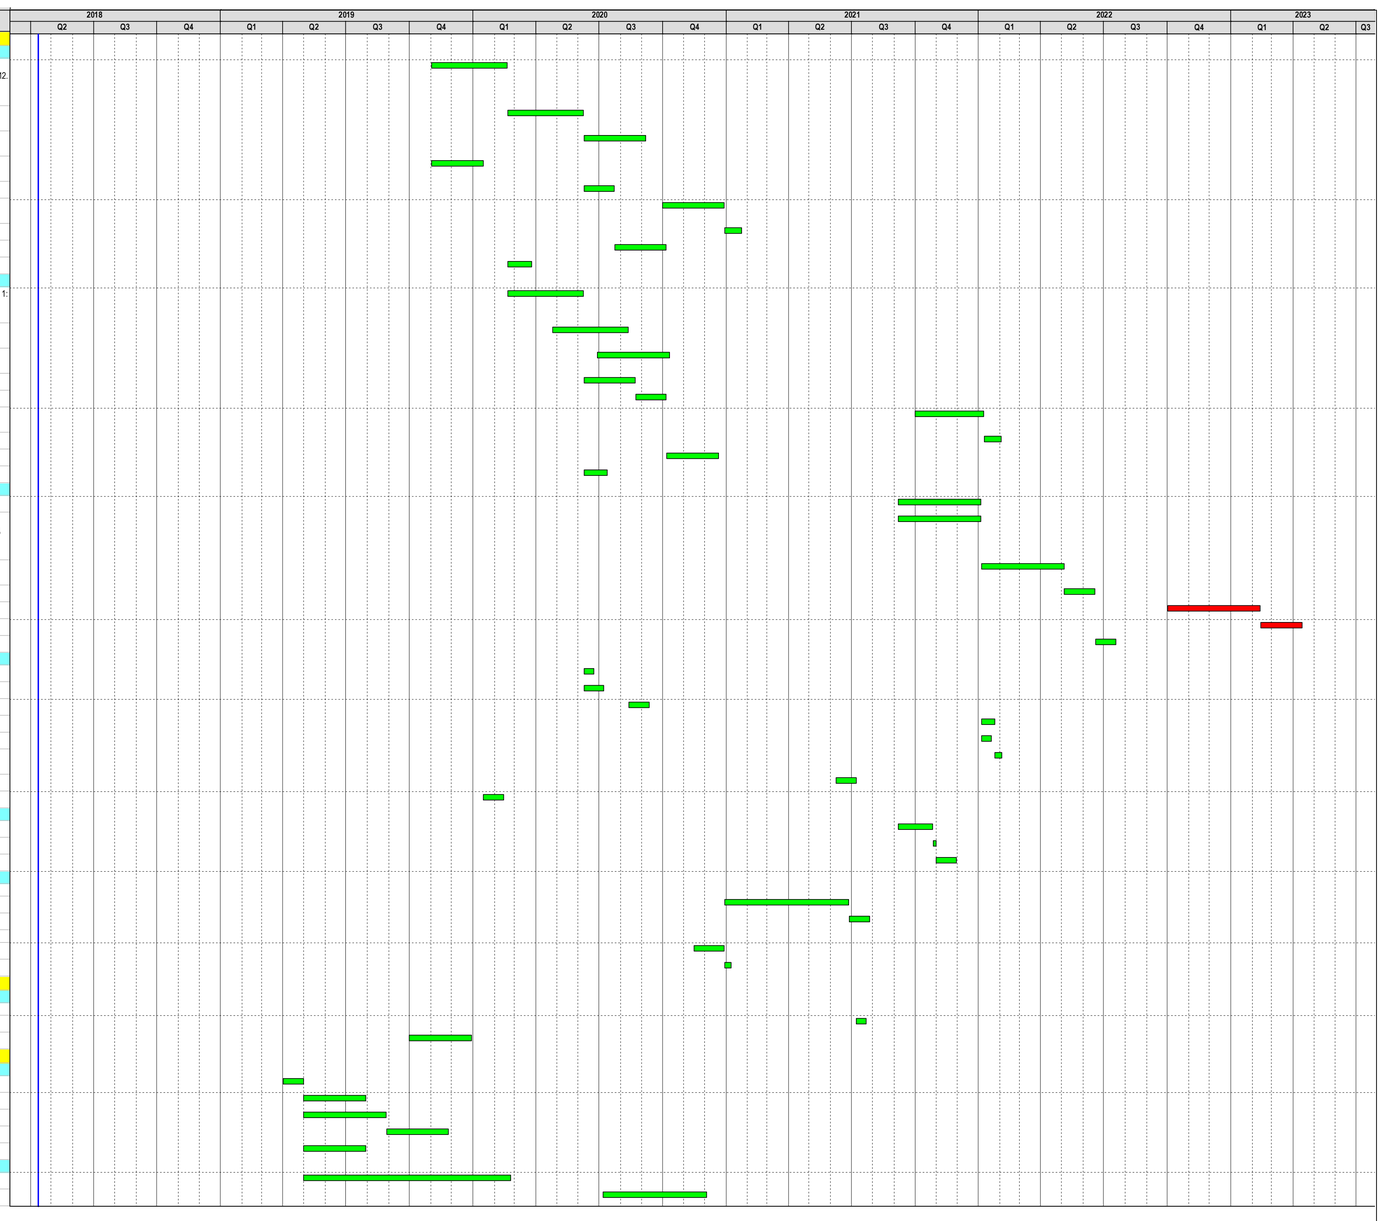

Remaining Work
Critical Remaining Work
Milestone

South-East New Territories Land Fill Extension (SA2-SENTX)
Baseline Programme

GREEN VALLEY LANDFILL LIMITED

Date	Revision	Checked	Approved
11-May-18	SENTX-GVL-W-PB-ZZ-0001 Rev. I01		
20-Jul-18	SENTX-GVL-W-PB-ZZ-0001 Rev. I02 (Detailed)		
